BLUEPRINT INFRASTRUCTURE Q2 2021 PROJECT STATUS

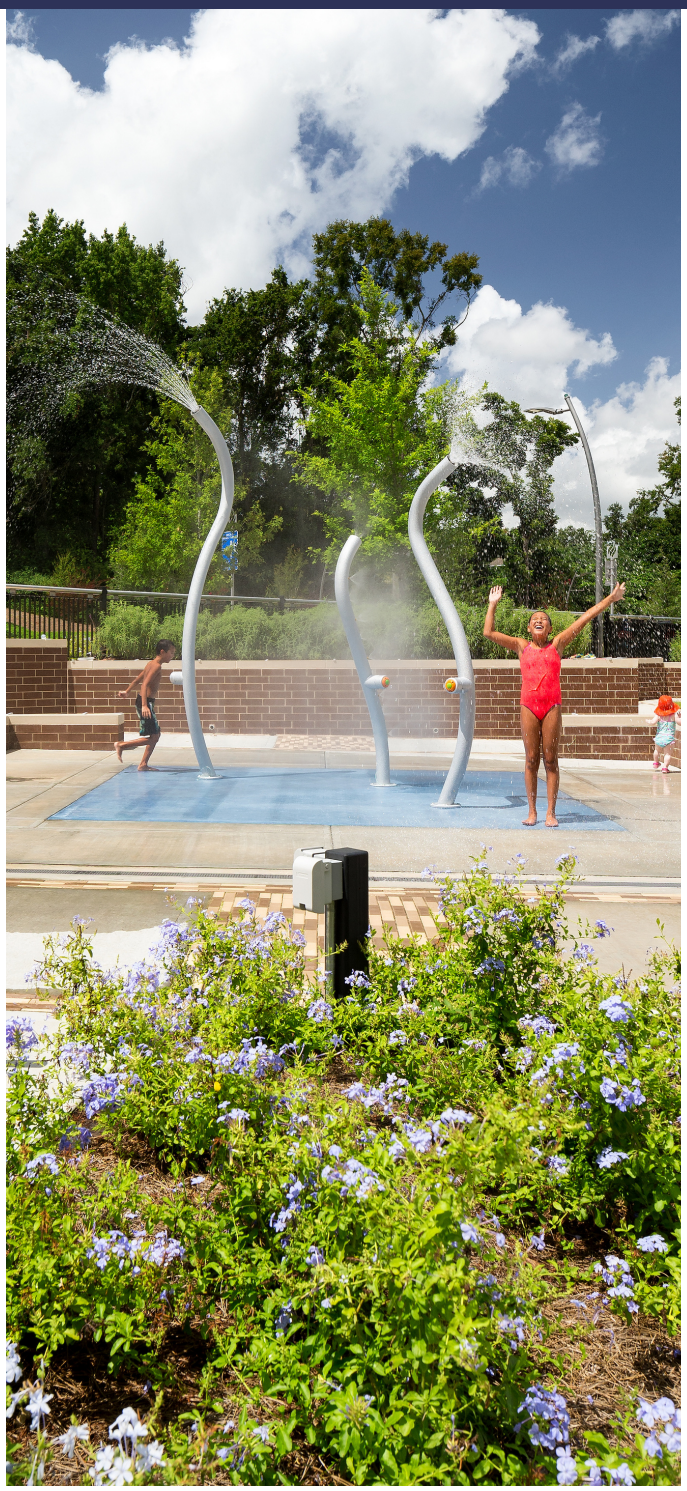

PROJECTS ACTIVE

IN PLANNING, DESIGN, AND CONSTRUCTION

29	ACTIVE PROJECTS/ SUBPROJECTS
22.06	MILES OF ROADWAY TO BE IMPROVED
78.85	TOTAL MILES OF BICYCLE/ PEDESTRIAN FACILITIES TO BE CONSTRUCTED
406	TREE PLANTINGS INCLUDED IN PROJECTS AT 100% DESIGN
200.06 Acres 8,714,447 Sq Ft	PUBLIC SPACE TO BE DEVELOPED

BLUEPRINT INTERGOVERNMENTAL AGENCY

BLUEPRINT
INTERGOVERNMENTAL AGENCY

BLUEPRINT INFRASTRUCTURE QUARTERLY PROJECT STATUS REPORT

This document provides an update on active Blueprint Infrastructure projects for the second quarter of 2021 (April 1, 2021 to June 30, 2021). Its purpose is to give an overview of all active projects and subprojects, project timelines, and also provide statistics about the improvements these projects will provide, once completed. Included in the Q2 2021 Status Report are project snapshots for all active and planned Blueprint Infrastructure projects.

CONTACT

850.219.1060
BlueprintIA.org
info@BlueprintIA.org

315 S. Calhoun Street, Suite 450
Tallahassee, FL 32301

Blueprint Intergovernmental Agency
@BlueprintIA2020

PROJECTS INITIATED IN Q2 2021

(IA Board Approved Procurement Authorization)

PROJECT GROUND BREAKINGS & RIBBON CUTTINGS IN Q2 2021

(Beginning or Completing Construction)

Cascades Trail Seg. 3DB Reg. Stormwater Facility

Van Buren Street

Q2 2021 ACTIVE PROJECTS & SUBPROJECTS

Project	PHASE
Van Buren Street	CONSTRUCTION
Cascades Trail Seg. 3DB Reg. Stormwater Facility & Trailhead	CONSTRUCTION
FAMU Way Playground Restroom	CONST. PROCUR.
Coal Chute Pond	CONSTRUCTION
Skateable Art	PERMITTING
History and Culture Trail	DESIGN
Magnolia Drive Trail	CONST. PROCUR./ DESIGN
Cascades Trail Seg. 4	PLANNING
Debbie Lightsey Nature Park	DESIGN
Capital Circle SW Greenway	DESIGN

Project	PHASE
Capital Circle SW Road Project	ROW
Lake Jackson Greenway	PRE-ENG.
Lake Lafayette and St. Marks Regional Linear Park	PLANNING/ PRE-ENG.
Downtown-University Protected Bike Lane	PLANNING
Market District Park	DESIGN
Market District Connectivity	PRE-PLANNING
Midtown Placemaking	DESIGN SCOPE DEVELOPMENT
Monroe-Adams Placemaking	PLANNING/ PRE-ENG.
Northeast Connector	PLANNING/ PRE-ENG.
Northeast Gateway	PLANNING/ PRE-ENG.

Project	PHASE
Orange-Meridian Placemaking	PLANNING/ DESIGN
Fairgrounds Beautification and Improv.	PLANNING/ MARKET STUDY
Comprehensive Wastewater Treatment Plan	PRE-ENG.
Thomasville Rd. Greenway	FEASIBILITY STUDY (CRTPA)
University Greenway	PLANNING
Southwood Greenway	CONST. (COT)
Airport Gateway	PLANNING
Implementing the Greenways Master Plan (GWMP)	
Bike Route System (BRS)	

Schedule of Current Blueprint 2000 and 2020 Project Phases and Timelines

Program	Project	Phase	2021		2022				2023		2024		2025		2026	
			3rd Q	4th Q	1st Q	2nd Q	3rd Q	4th Q	1-6 Mos	7-12 Mos	1-6 Mos	7-12 Mos	1-6 Mos	7-12 Mos	1-6 Mos	7-12 Mos
Blueprint 2000	Capital Cascades Trail Segment 3 - Van Buren Street	*Planning*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Capital Cascades Trail Segment 3D	*Planning*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Capital Cascades Trail Segment 3 - Amenities[1]	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Capital Cascades Trail Segment 4	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Cascades Park Alum	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Magnolia Drive[2]	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
Blueprint 2020	Alternative Sewer Solutions Study	*Comprehensive Wastewater*														
	Debbie Lightsey Nature Park & Capital Cir Southwest Greenway	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Lake Jackson Greenway	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Orange Avenue (FDOT Project)	*Planning/Pre-Engineering*														
		Design & Permitting														
	Orange/Meridian Placemaking	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Thomasville Rd Greenway (CRTPA)	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	University Greenway	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Market District Park Element	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Market District Pedestrian/Trail Connectivity	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Monroe-Adams Corridor	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Lake Lafayette and St Marks Regional Park	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Midtown Placemaking (Thomasville from Monroe to 7th)	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Airport Gateway	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Northeast Connector - Bannerman Road	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														
	Northeast Gateway Welaunee Boulevard	*Planning/Pre-Engineering*														
		Design & Permitting														
		Right-of-Way Acquisition														
		Construction														

1. Amenities may include those around Coal Chute pond, Skate Feature and, History and Culture Trail. The proposed trailhead will be constructed as part of Pond 3D-B.

2. Projects being managed and administered by Leon County with Blueprint support

Planning/Pre-Engineering

PD&E

Design

Right-of-Way Acquisition

Construction

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:

blueprintia.org/projects/airport-gateway

Staff Contact: Abraham Prado
(850) 219-1076 Abe.Prado@BlueprintIA.org

Airport Gateway

Project Highlights

- The purpose of the Project is to create a unique, safety-enhanced, multimodal gateway entrance into Downtown, FSU, and FAMU from the Tallahassee International Airport. Other project goals include expanded investment in Southwest Tallahassee-Leon County, supporting local growth of the high-tech sector in areas such as Innovation Park, and improving neighborhood safety.
- The Project includes planned improvements for over 7 miles of southwest area roadways, a new road within FSU's southwest campus, and includes approximately 12 miles of new sidewalks, bicycle lanes, and multiuse trails.

Current Status:

- The Southwest Area Transportation Plan, which provides planning and analysis of existing traffic data for road segments included in this project, was completed in 2019.
- Coordination with the Florida Department of Transportation regarding its current PD&E Study of Orange Avenue from Monroe Street to Capital Circle Southwest.
- Planning for the Airport Gateway is underway. A project kickoff meeting for Phase 1 was held March 5, 2021. The design of roadway improvements for Springhill Road, Stuckey Avenue, and a new road within FSU's southwest campus, as well as Levy Avenue and neighborhood improvements, are scheduled for Phase 1.

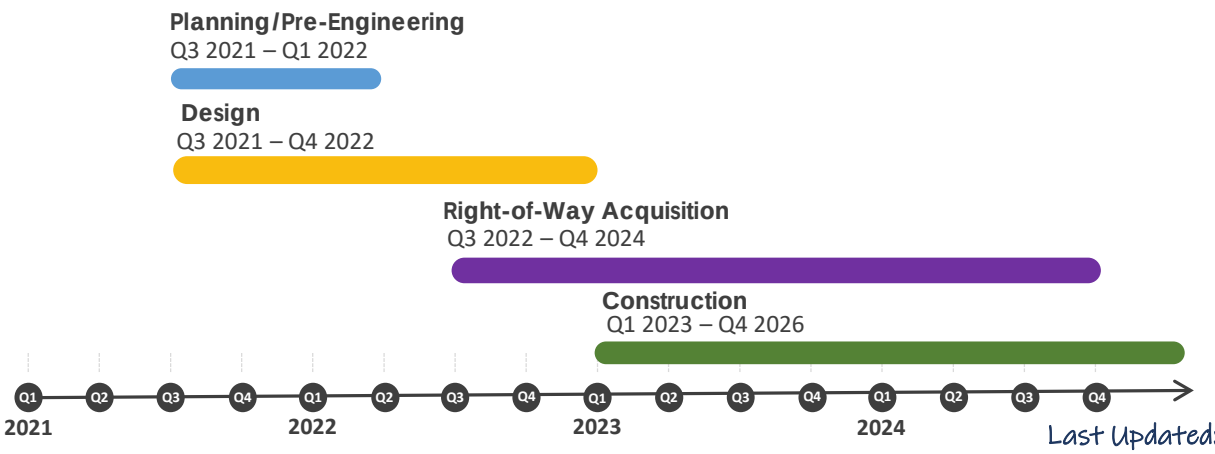

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

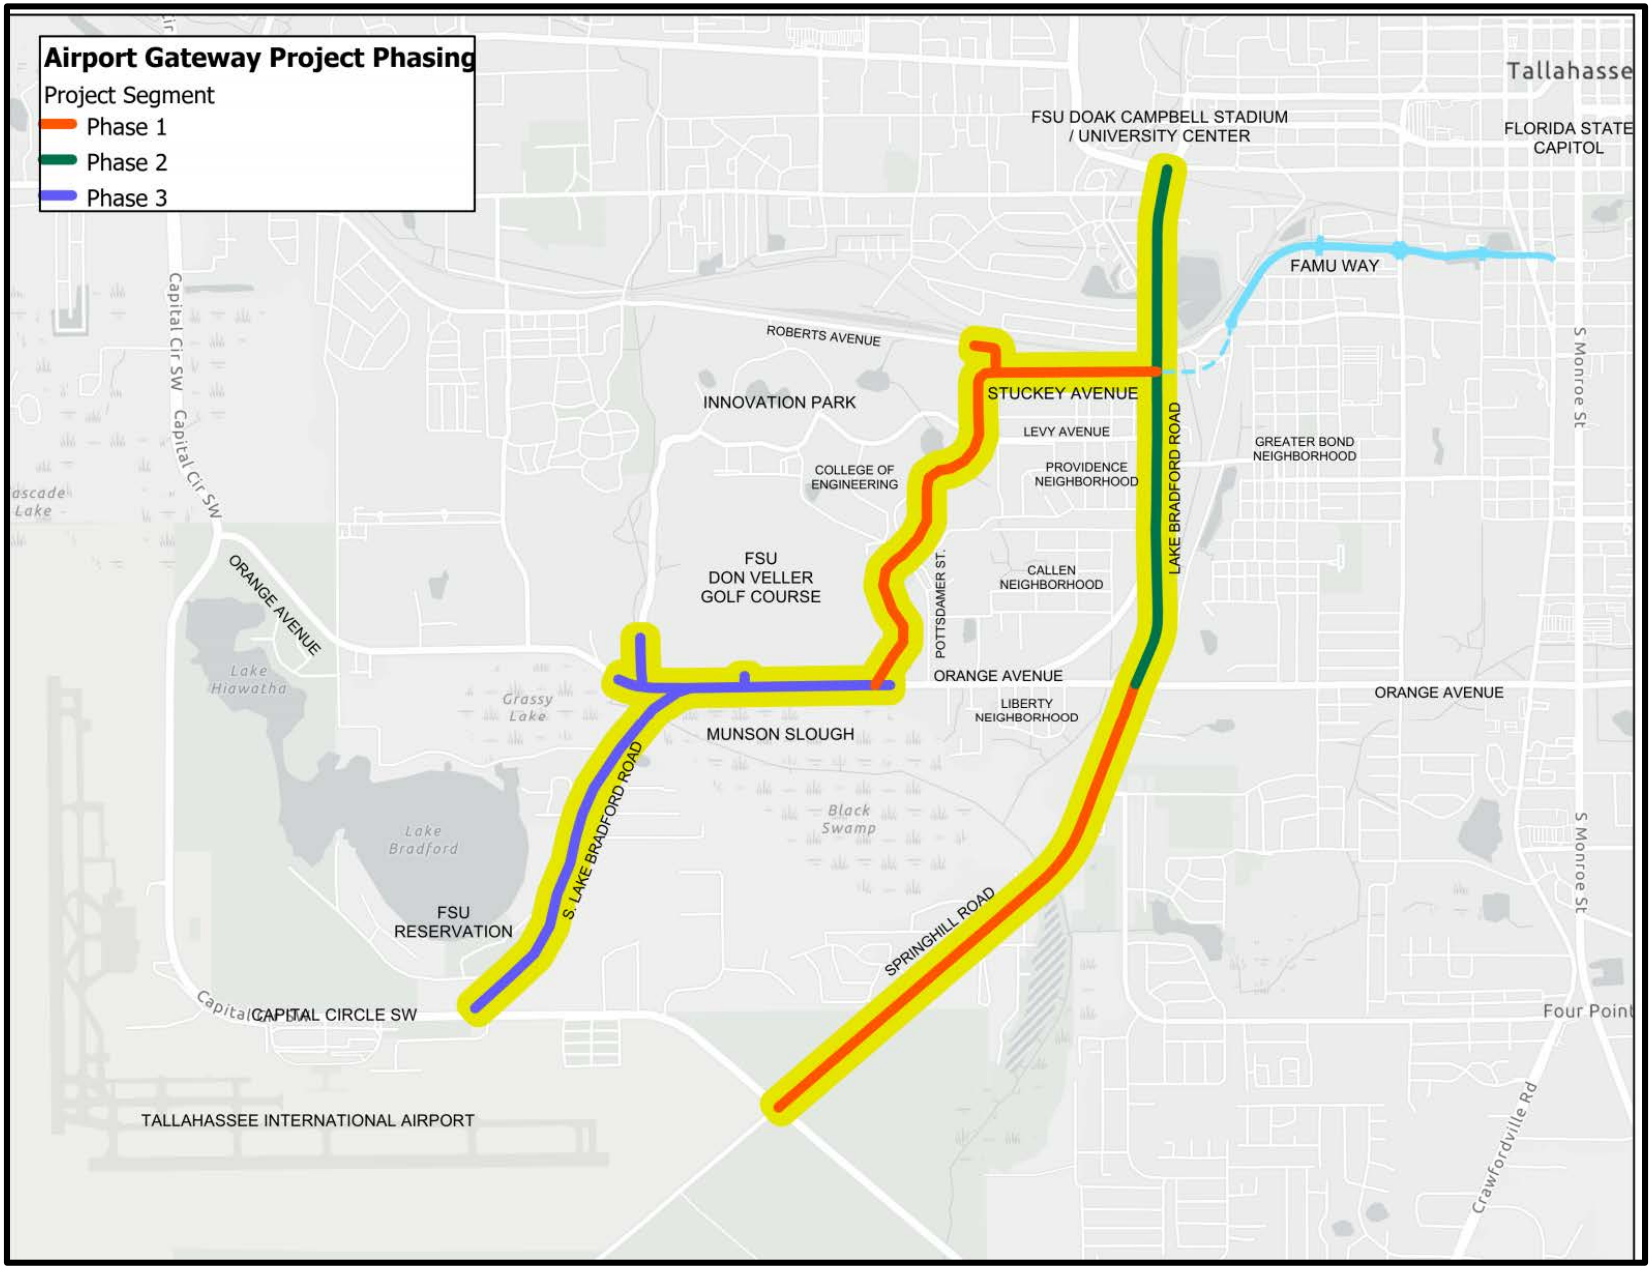

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Leon County Government Contact:

Felton Ard, (850) 606-1515
LeonCountySprings@LeonCountyFL.gov

Alternative Sewer Solutions

Project Highlights

- Project provides funding for the Alternative Sewer Solutions Study; study area is unincorporated Leon County, and includes Primary Springs Protection Zone.

Current Status:

- Leon County is currently managing the first phase of this project: the Comprehensive Wastewater Treatment Facilities Plan (CWTFP), which began in November 2019.
- The Task 1 Report on Nitrogen Reduction Performance Criteria for Alternative Wastewater Treatment Systems was received in April 2020. The Draft Task 2 Report on Cost-Effectiveness of Alterative Technologies was submitted on November 3, 2020 and is under review by Leon County staff. The draft Task 3 Report on Factors Other than Cost-Effectiveness that Influence Selection of Treatment Technologies was received on December 1, 2020 and is also under review.
- Another round of public meetings are planned for 2021 which relate to the nitrogen reduction performance for alternative treatment systems and the factors influencing selection of treatment technology.



Last Updated: 06.22.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

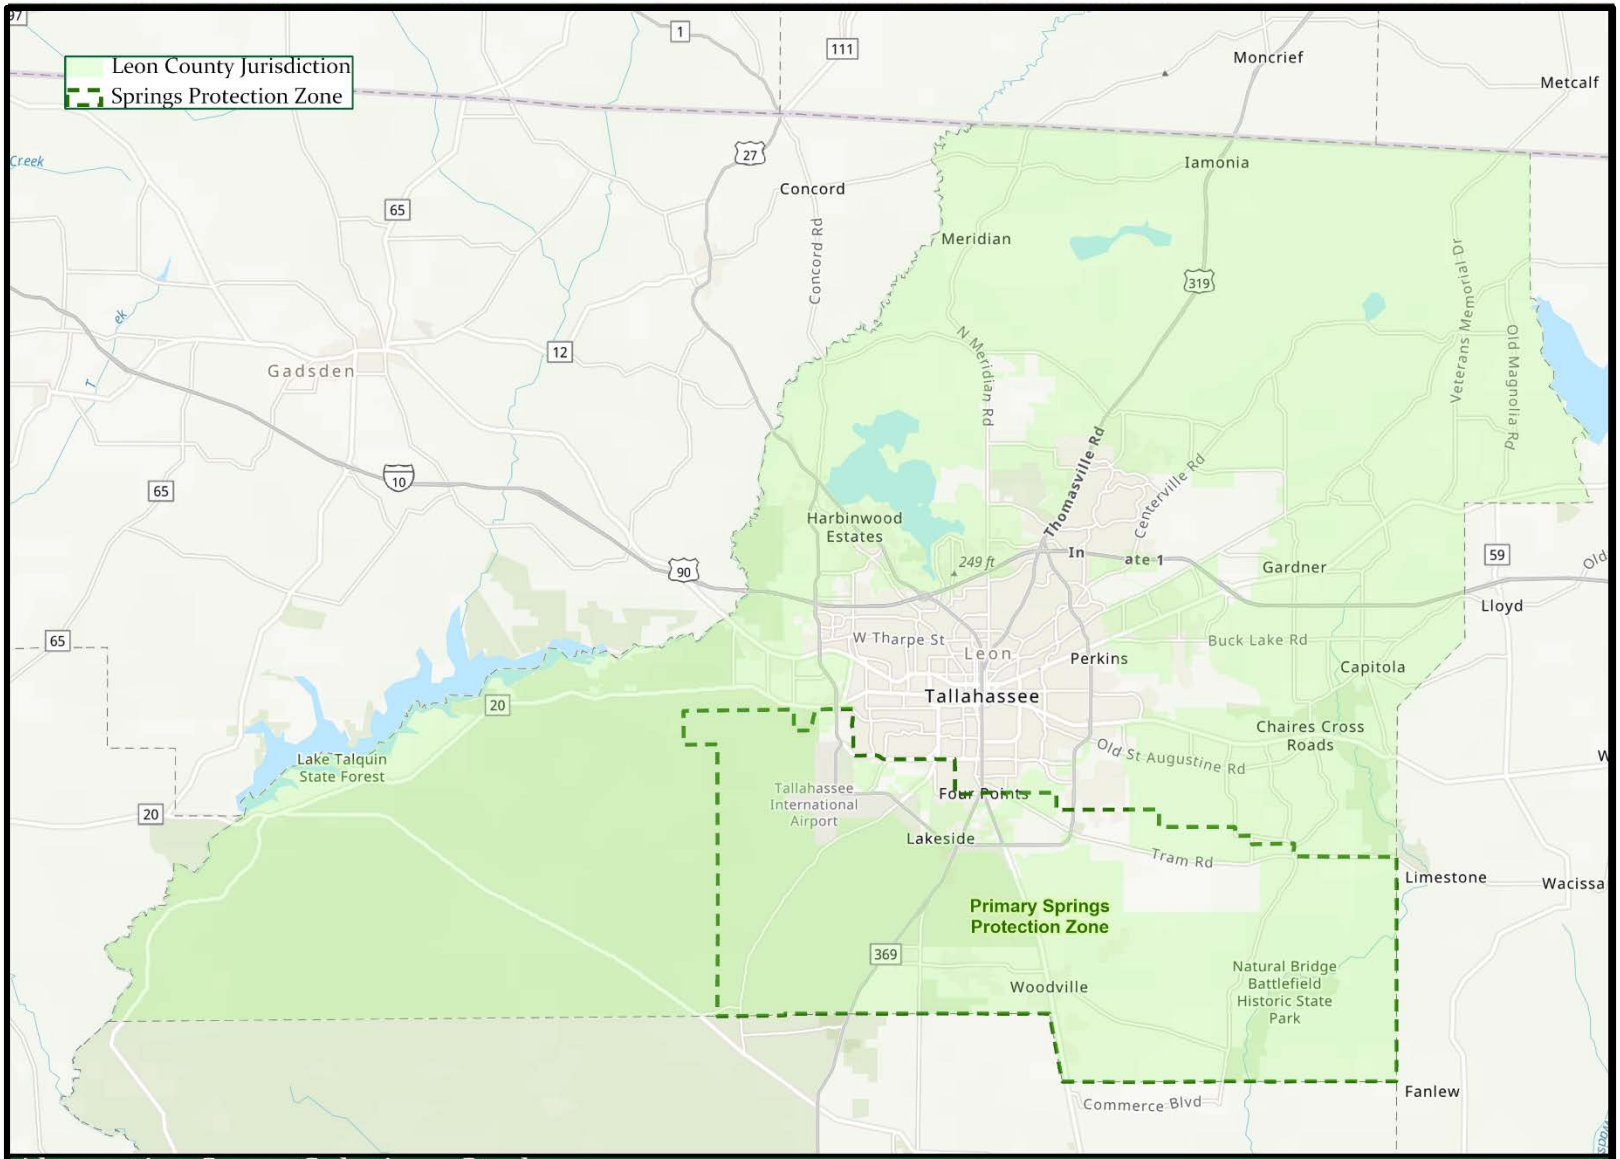

Alternative Sewer Solutions Study

Map of Unincorporated Area in Leon County with Primary Springs Protection Zone

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Contact: (850) 219-1060
info@blueprintia.org

Animal Service Center

Project Highlights

- Sales tax funding will support construction of a new facility or significant renovations of the current Animal Service Center.
- Potential Improvements Include:
  - Educational facilities
  - Expansion of veterinary facilities
  - Additional upgrades to create a world-class facility that is a source of pride in the community

Current Status

- This project has not been initiated yet.

Last Updated: 06.08.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

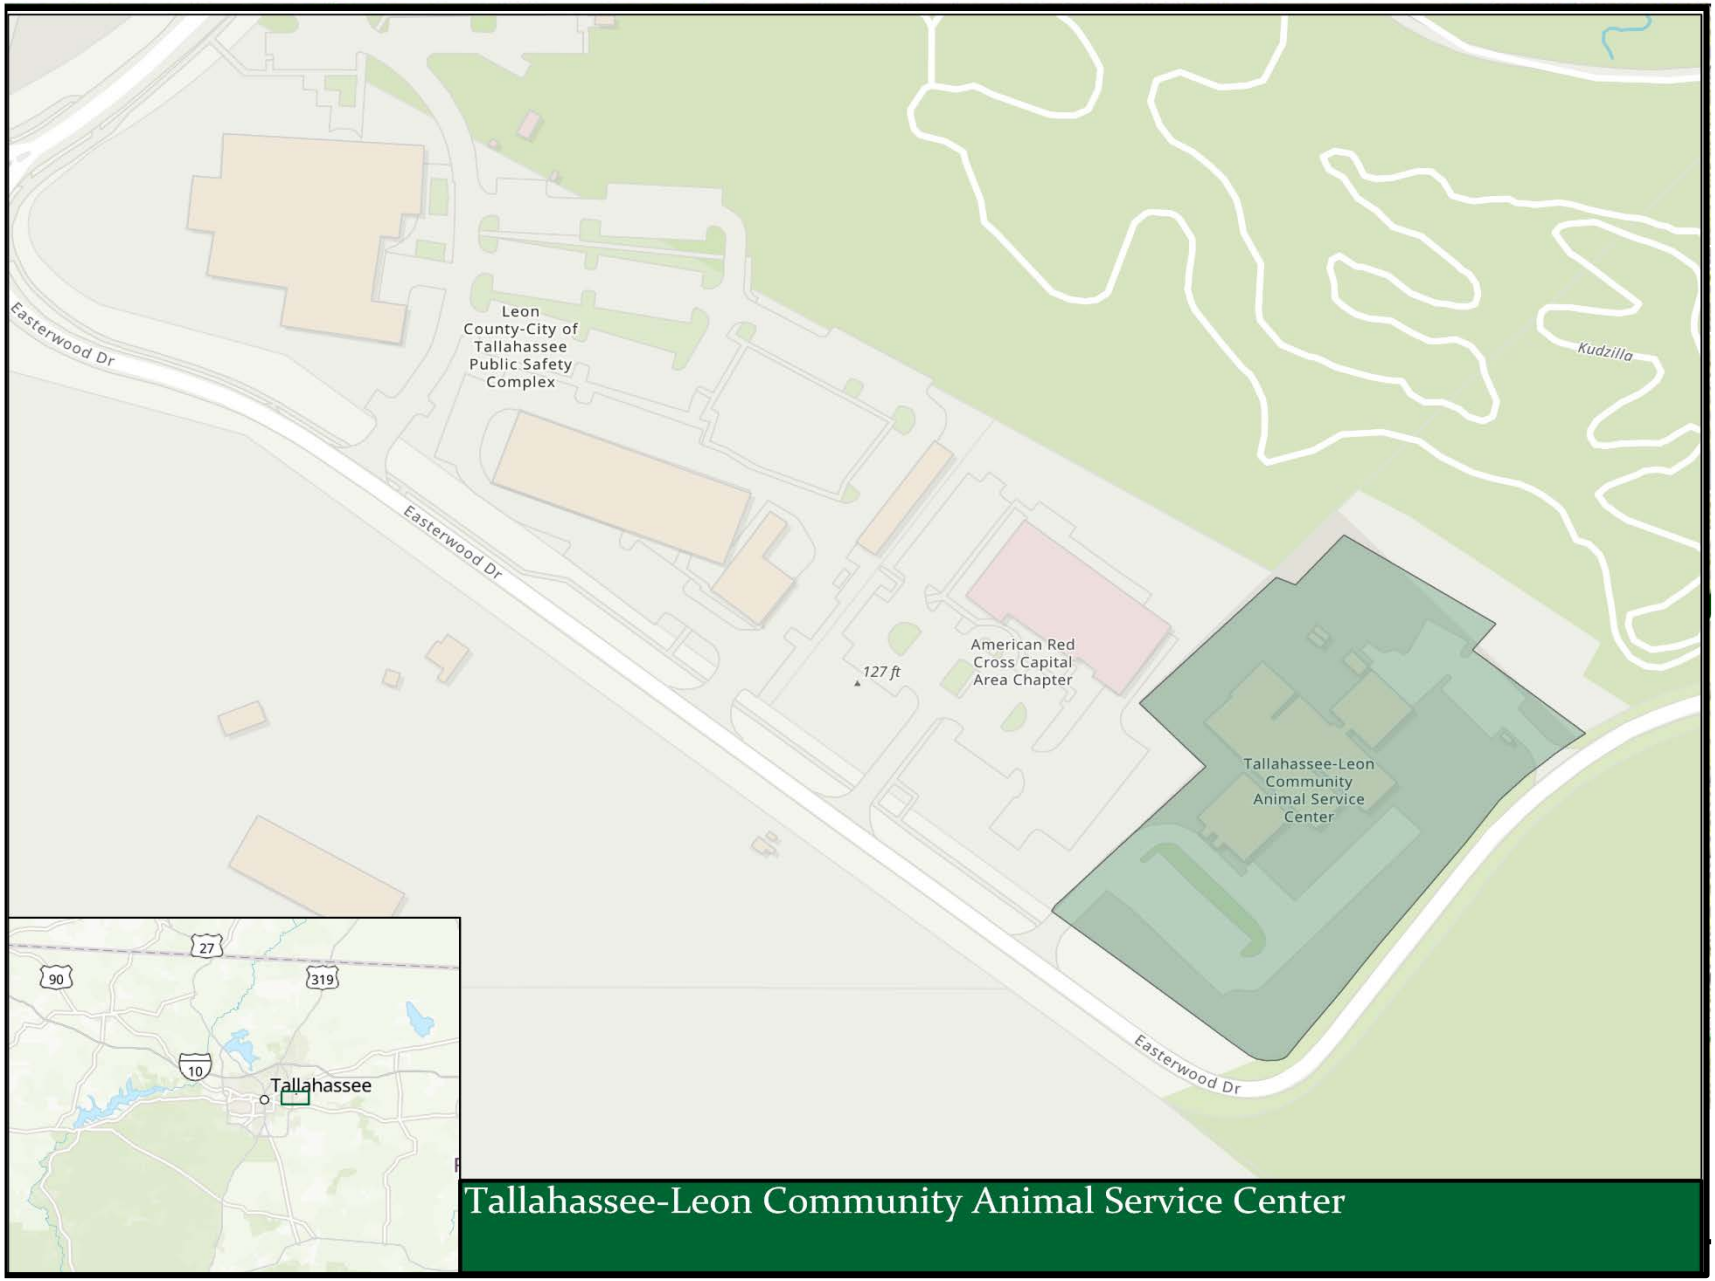

Tallahassee-Leon Community Animal Service Center

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: Mike Alfano
(850) 219-1075
Michael.Alfano@blueprintia.org

Build the Bike Route System

Project Highlights

- Blueprint has been tasked with Building the Bike Route System (BRS)
- IA Board has allocated $15 Million in annual installments of $750,000.
- Consistent with updates provided to the IA Board, Blueprint will implement projects under this program according to the below process:
    - Leveraging opportunities with Blueprint, City, County, and private road projects that have bicycle facility improvements identified.
    - Tier 1 Bicycle and Pedestrian Master Plan Projects
    - Projects identified as part of the Facilities Gap Analysis completed by the Tallahassee-Leon County Planning Department.

Current Status:

- The IA Board authorized procurement of design and construction services for the Downtown-University Protected Bike Lane project at its February 18, 2021 meeting.
- The IA Board was presented a Proposed FY 2022 BRS work program in May 2021, which includes feasibility studies on three BRS projects:
    - Ridge Road Trail
    - Blairstone Road Trail
    - SW Area – which will include connections betweent the Tallahassee Museum, Debbie Lightsey Nature Park, the FSU RecPlex, the University Greenway, and surrounding neighborhoods.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

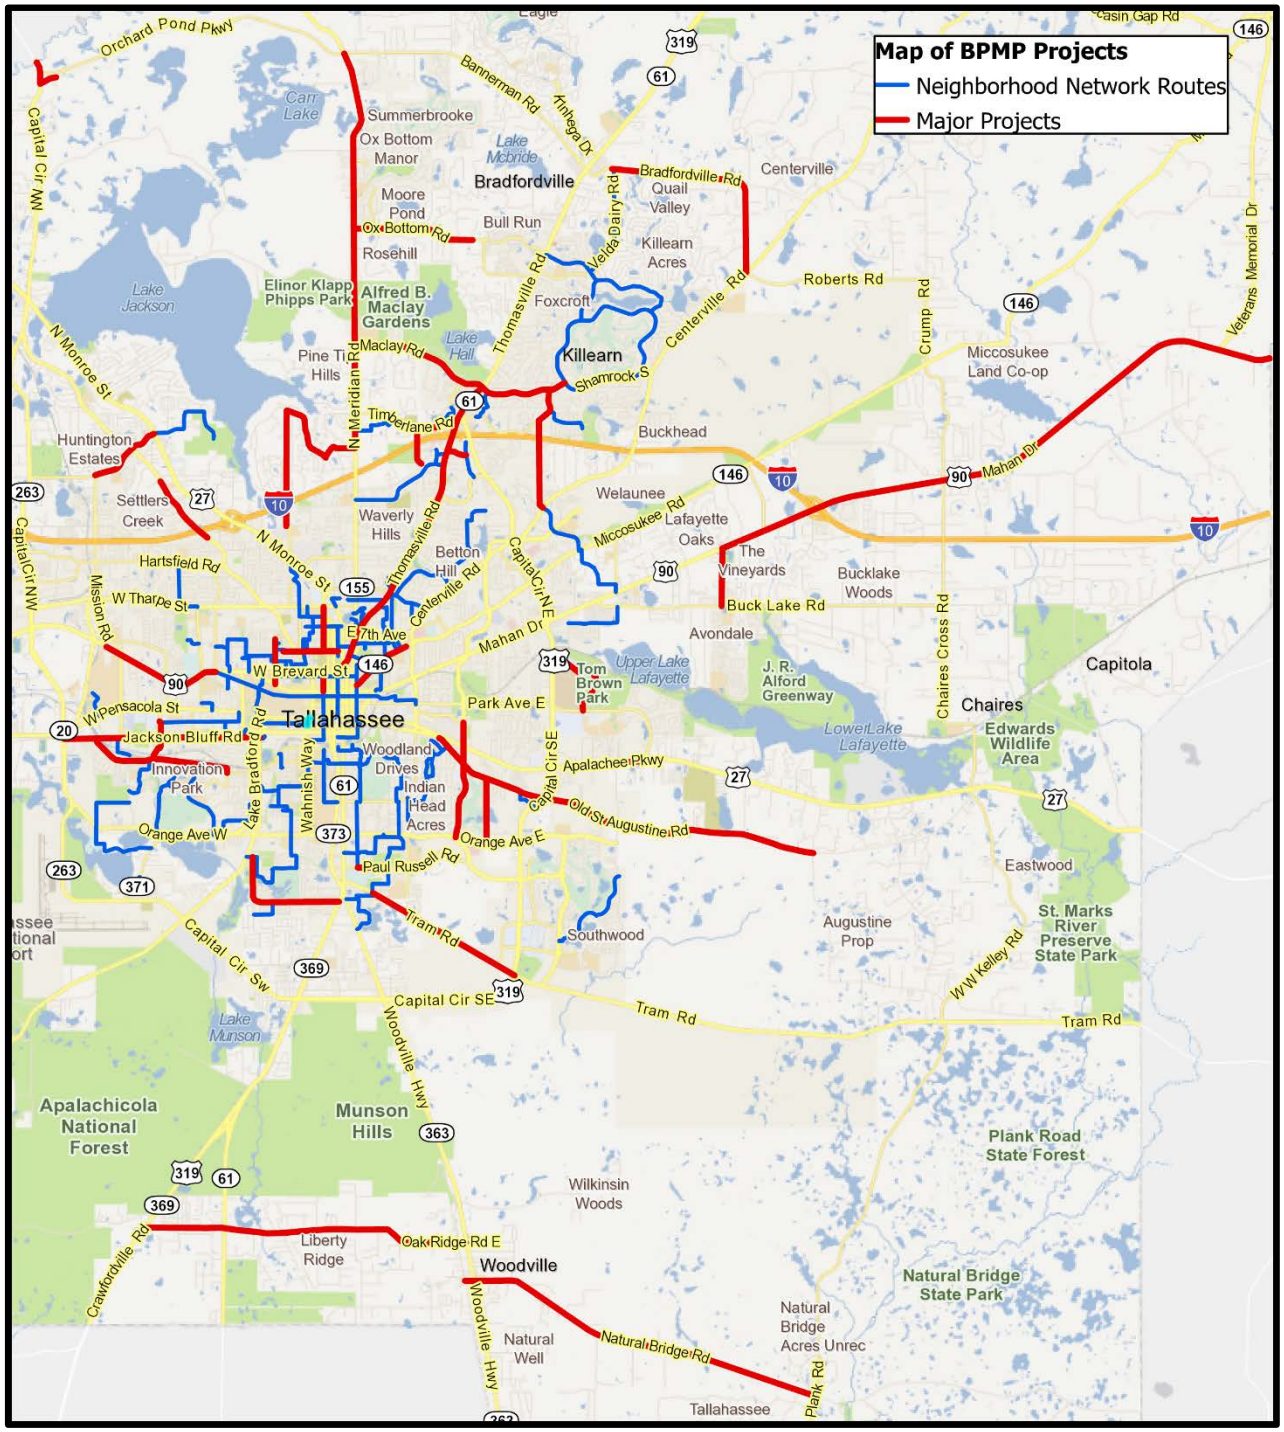

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/capital-cascades-trail

Staff Contact: Dan Scheer, (850) 219-1066
Daniel.Scheer@blueprintia.org

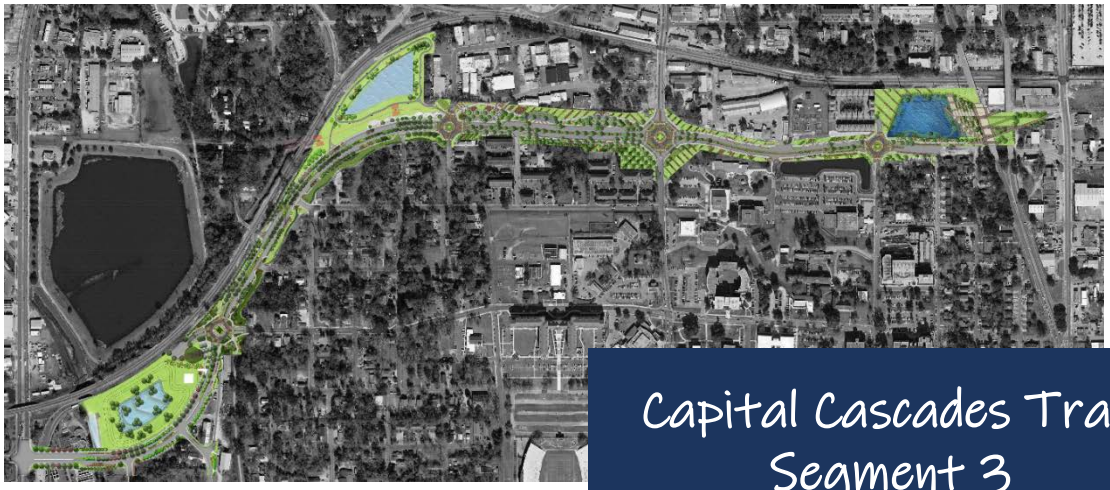

Capital Cascades Trail: Segment 3

Project Highlights

- The Capital Cascades Trail: Segment 3 project is a continuation of the Capital Cascades Trail network, which will provide connectivity and improvements linking Leon High School in Downtown Tallahassee to Lake Henrietta.
- This project creates a linear park, alongside the newly constructed FAMU Way, stretching from Adams Street to the confluence with the Central Drainage Ditch east of Lake Bradford Road.
- The Project will transform an open stormwater ditch into a beautiful linear park and trail, with a number of park amenities.

Current Status:

- Construction is underway and is anticipated to be complete Q2 2022.
- In addition to the initial $500,000 Springs Restoration Grant from FDEP for the project's innovative stormwater treatment methods, the project was notified on March 19, 2021 that it was also awarded an additional $235,000 Non-Point Source Water-Quality Assistance Grant from FDEP.

Construction
Q1 2021 – Q2 2022



Last Updated: 06.22.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

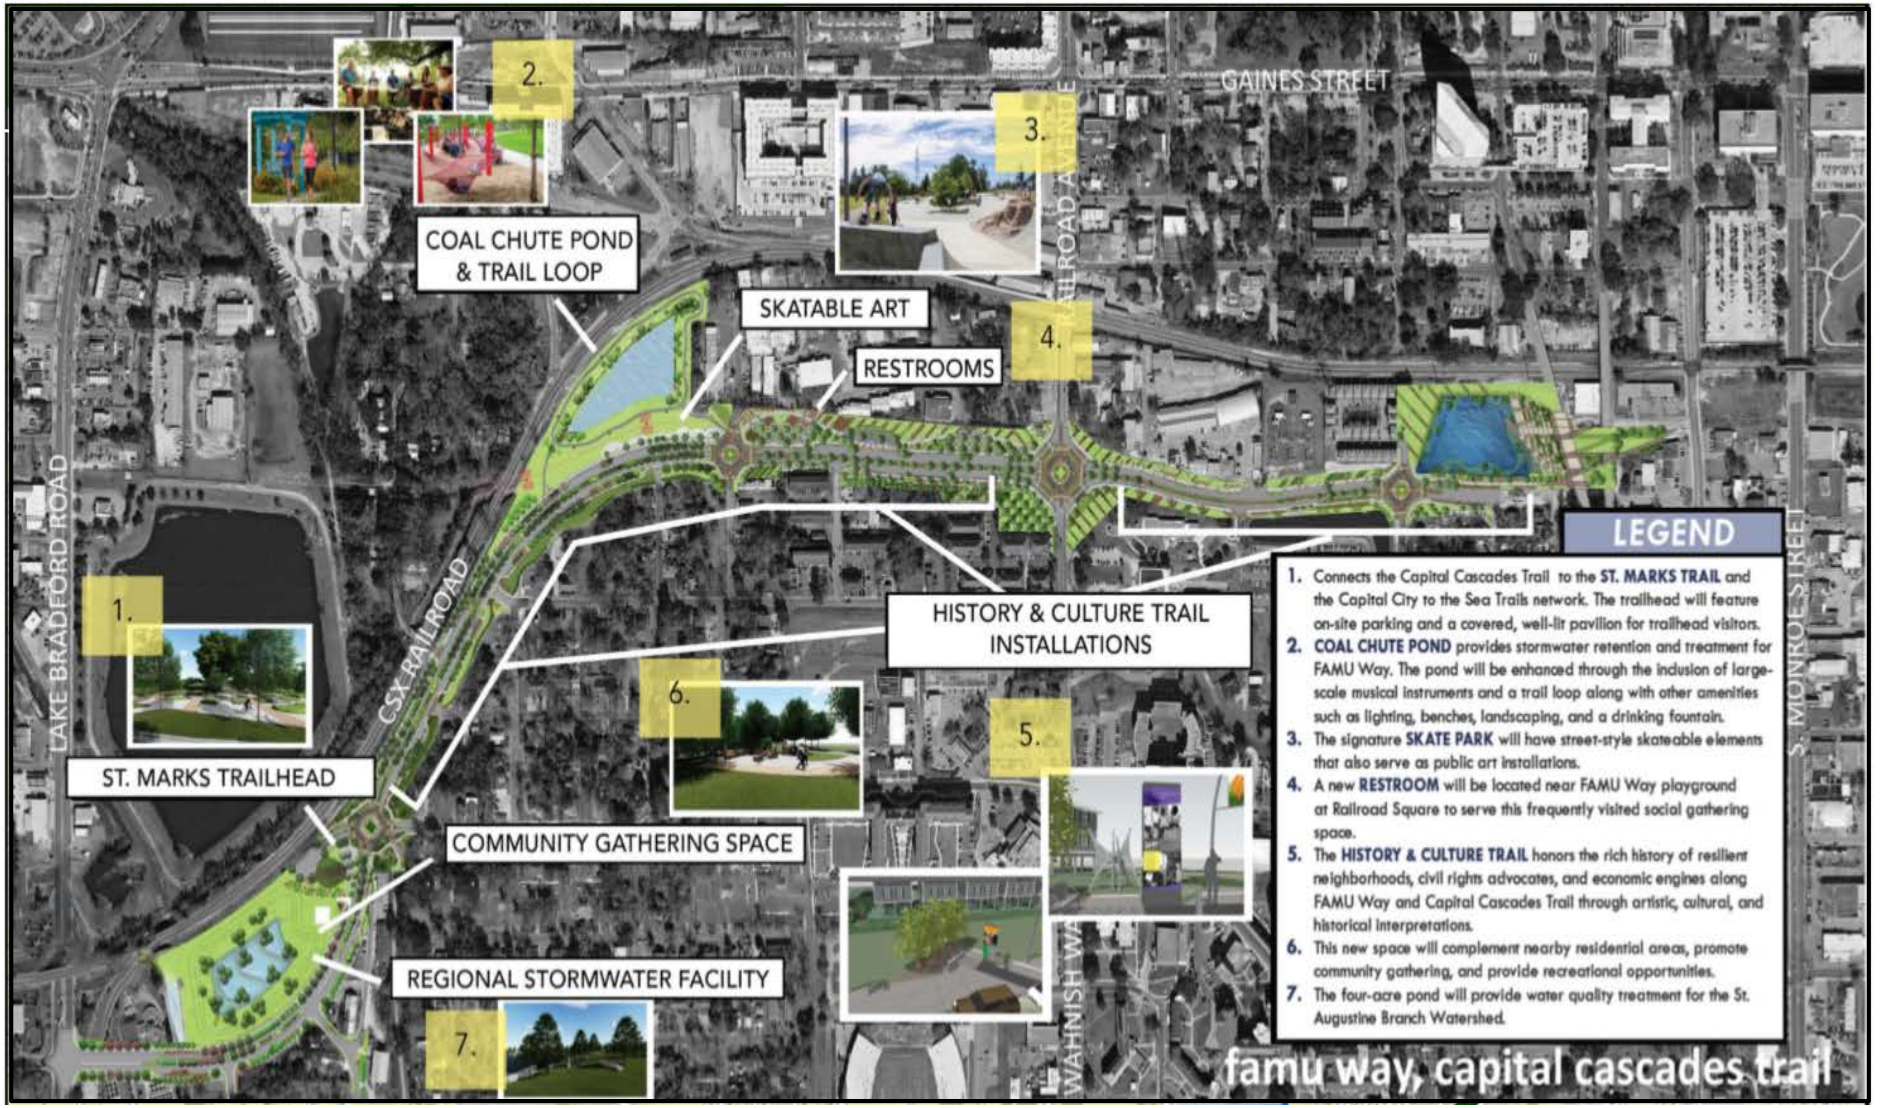

Project Website:
blueprintia.org/projects/cct-segment-3-amenities
Staff Contact: Junious Brown
(850) 219-1063
Junious.Brown@BlueprintIA.org

Capital Cascades Trail Segment 3 Coal Chute Pond

Project Highlights

- Coal Chute Pond provides stormwater retention and treatment for FAMU Way.
- The pond will be enhanced through the inclusion of Skateable Art feature that will be created alongside the pond, and other amenities such as lighting, benches, and landscaping.
- Amenities were refined through a public involvement process conducted in spring 2019, with FAMU, FSU, surrounding neighborhoods and businesses, and 300 citizens submitting their amenities preferences.

Current Status:

- Construction for Coal Chute Pond is underway as of May 2021 with a completion date anticipated in November 2021.



Last Updated: 06.21.2021

BLUEPRINT INTERGOVERNMENTAL AGENCY

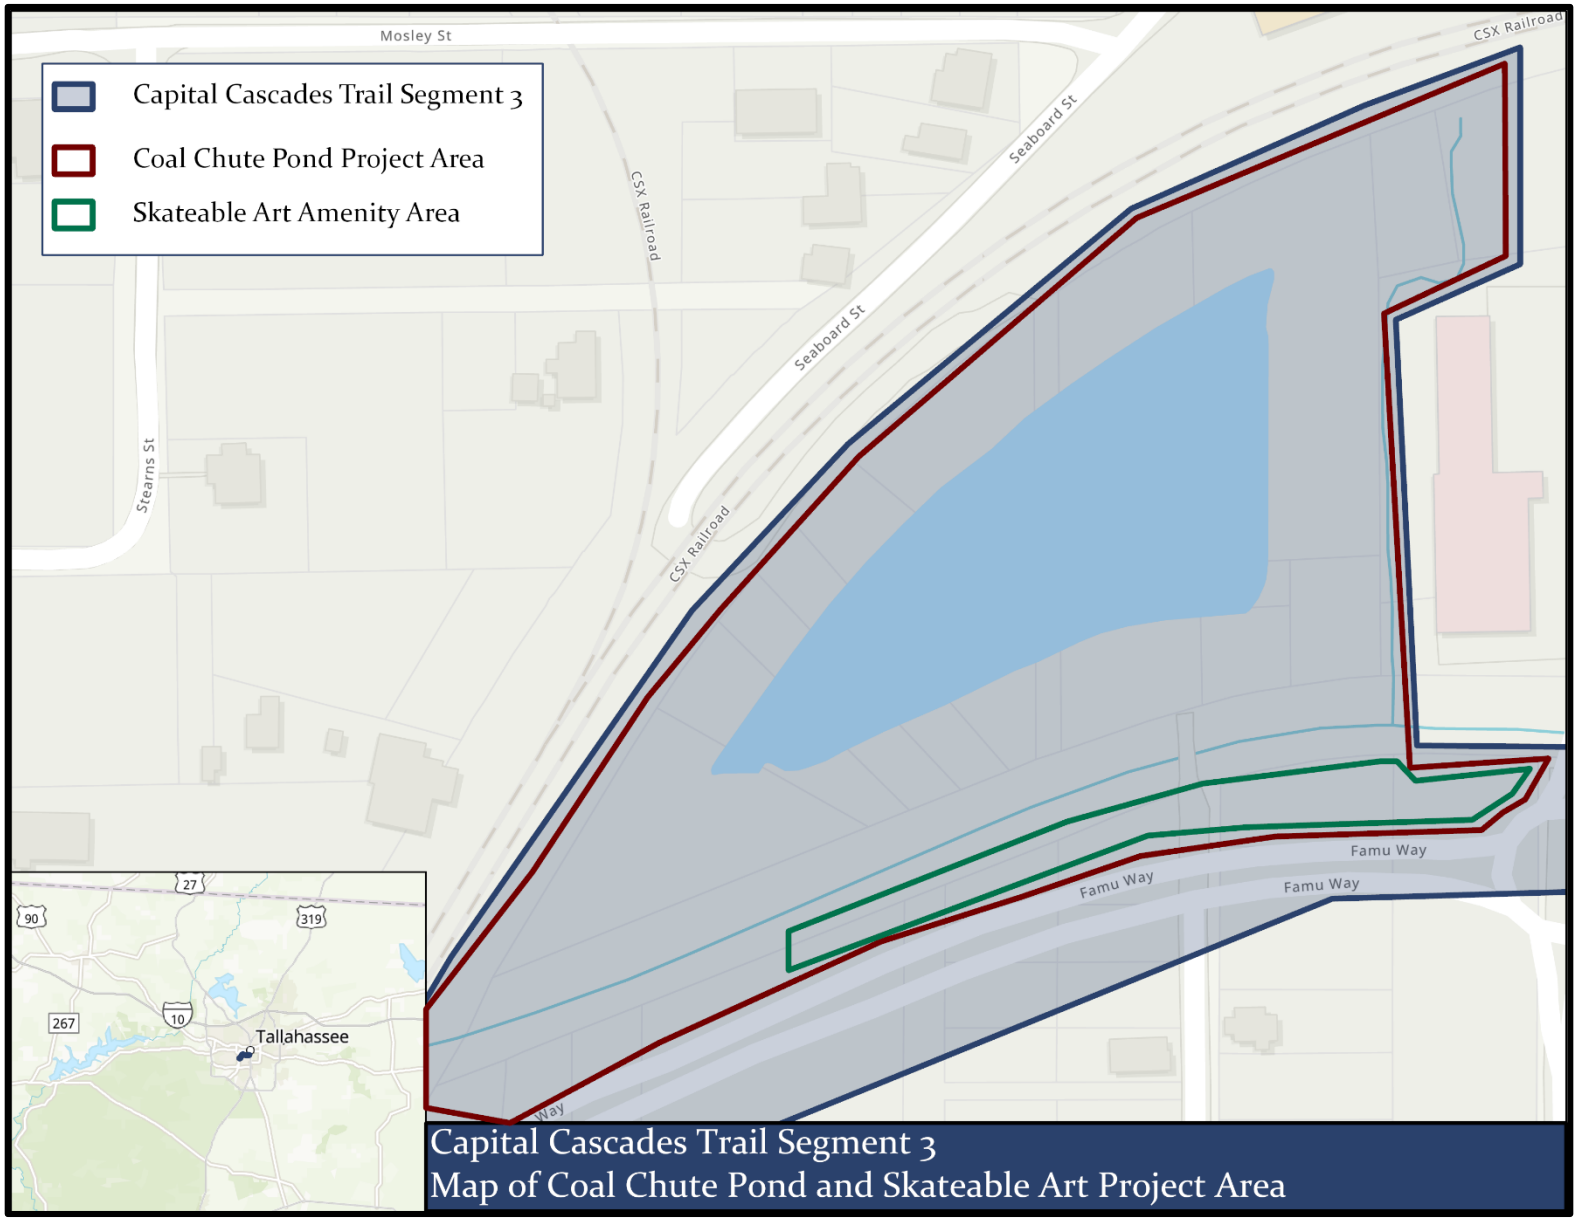

Capital Cascades Trail Segment 3
Map of Coal Chute Pond and Skateable Art Project Area

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/cct-segment-3-amenities/
Staff Contact: Tatiana Daguillard
(850) 219-1081
Tatiana.daguillard@blueprintia.org

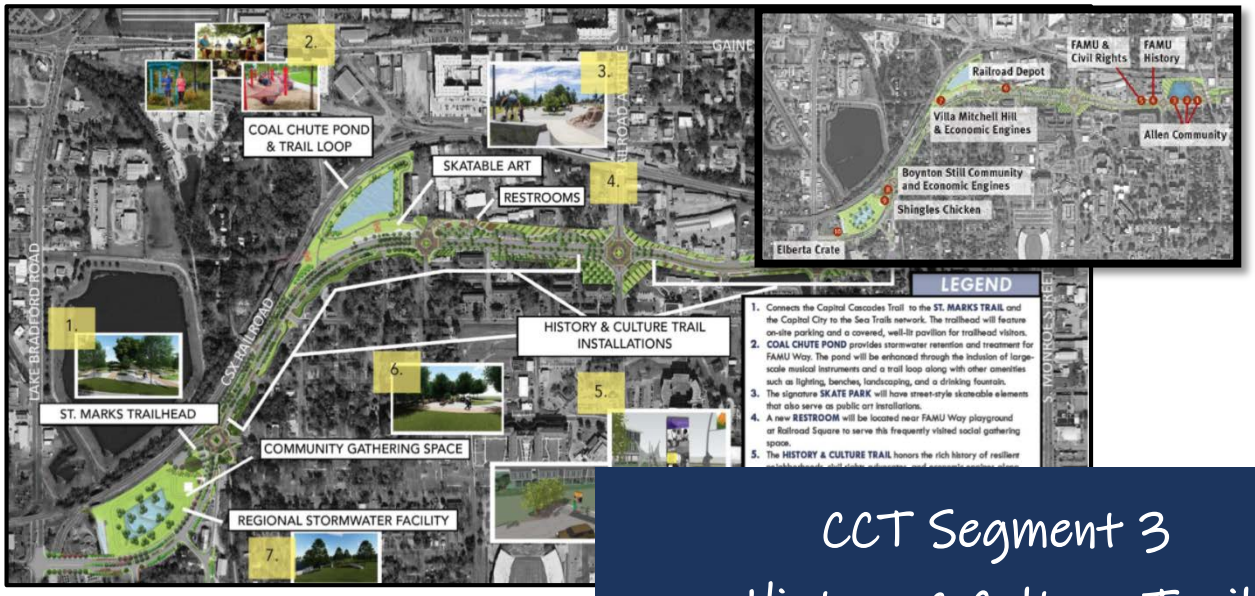

CCT Segment 3
History & Culture Trail

Project Highlights

- The project will celebrate and highlight the history and culture of the neighborhoods and businesses along FAMU Way through artistic cultural and historical interpretative kiosks that will display images, photographs, and historic information.
- Through a partnership with the Council on Culture and Art (COCA), artistic installations are planned to complement the interpretive kiosks.
- The project team includes a citizen working group that will assist in the concept and content development for historical and cultural interpretations

Current Status

- The project kickoff meeting was held December 18, 2021.
- Design is estimated to be completed in Q2 2022.
- Initial community engagement activities took place in June 2021.

Design
Q1 – Q4 2021

Construction
Q3 2021 – Q1 2022



Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

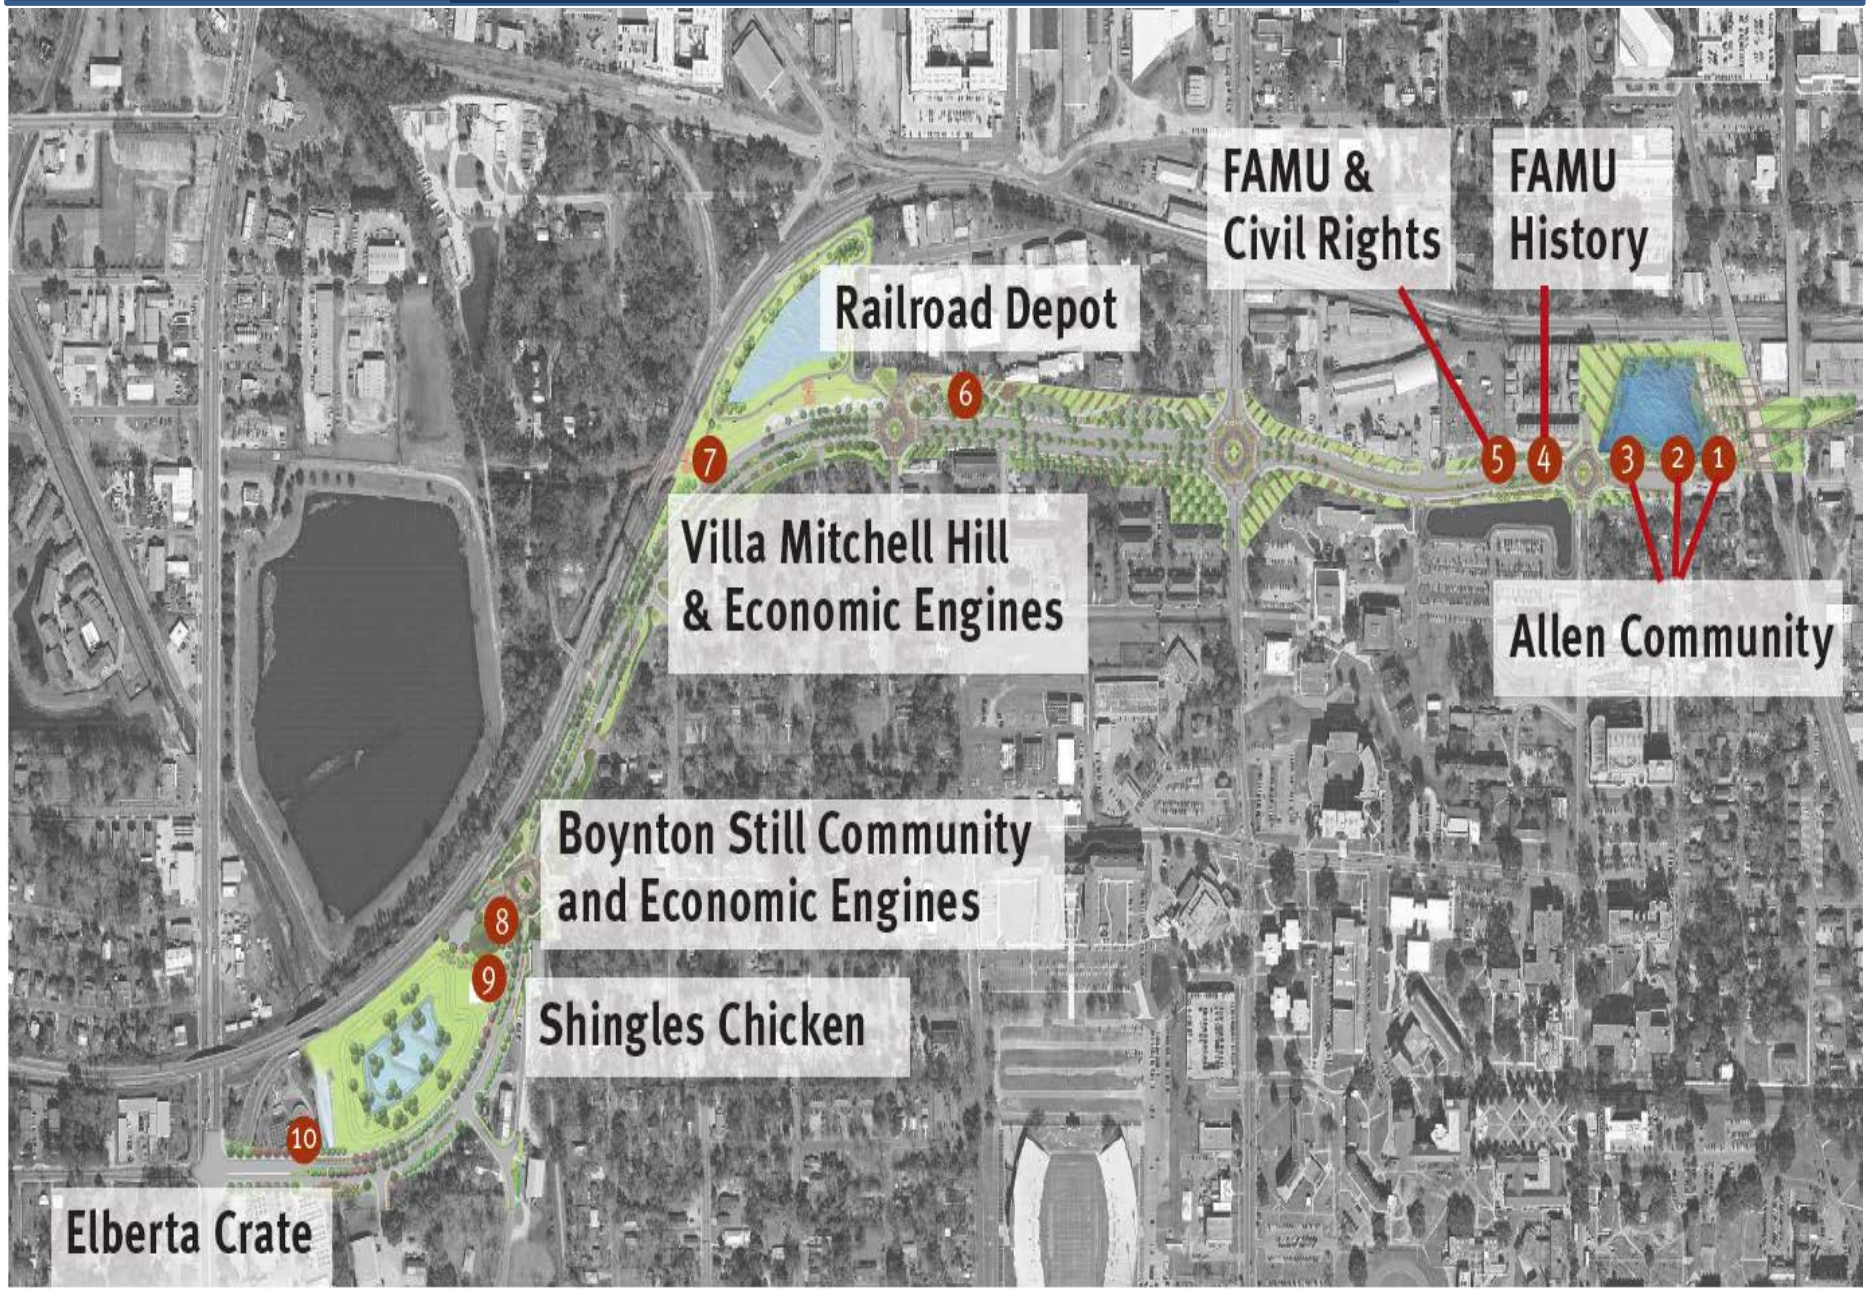

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/cct-segment-3-amenities/
Staff Contact: Sue Tanski
(850) 219-1071
Susan.Tanski@BlueprintIA.org

Capital Cascades Trail Segment 3 Skateable Art

Project Highlights

- The FAMU Way Skateable Art Project will develop a world class skate park that embraces artistic elements to provide an optimal riding experience for park users and also provides a visually stimulating space for spectators.
- The skate park will include a snake run feature that stretches roughly 225 feet, making it the longest snake run in Florida.
- The skate park also will feature a 300 foot long linear street course featuring many obstacles.

Current Status:

- Skateable Art public engagement took place in January to reveal design concepts that were approved by the IA Board in February 2021.
- Design and permitting is underway on the skate park.



Last Updated: 06.08.2021

BLUEPRINT INTERGOVERNMENTAL AGENCY

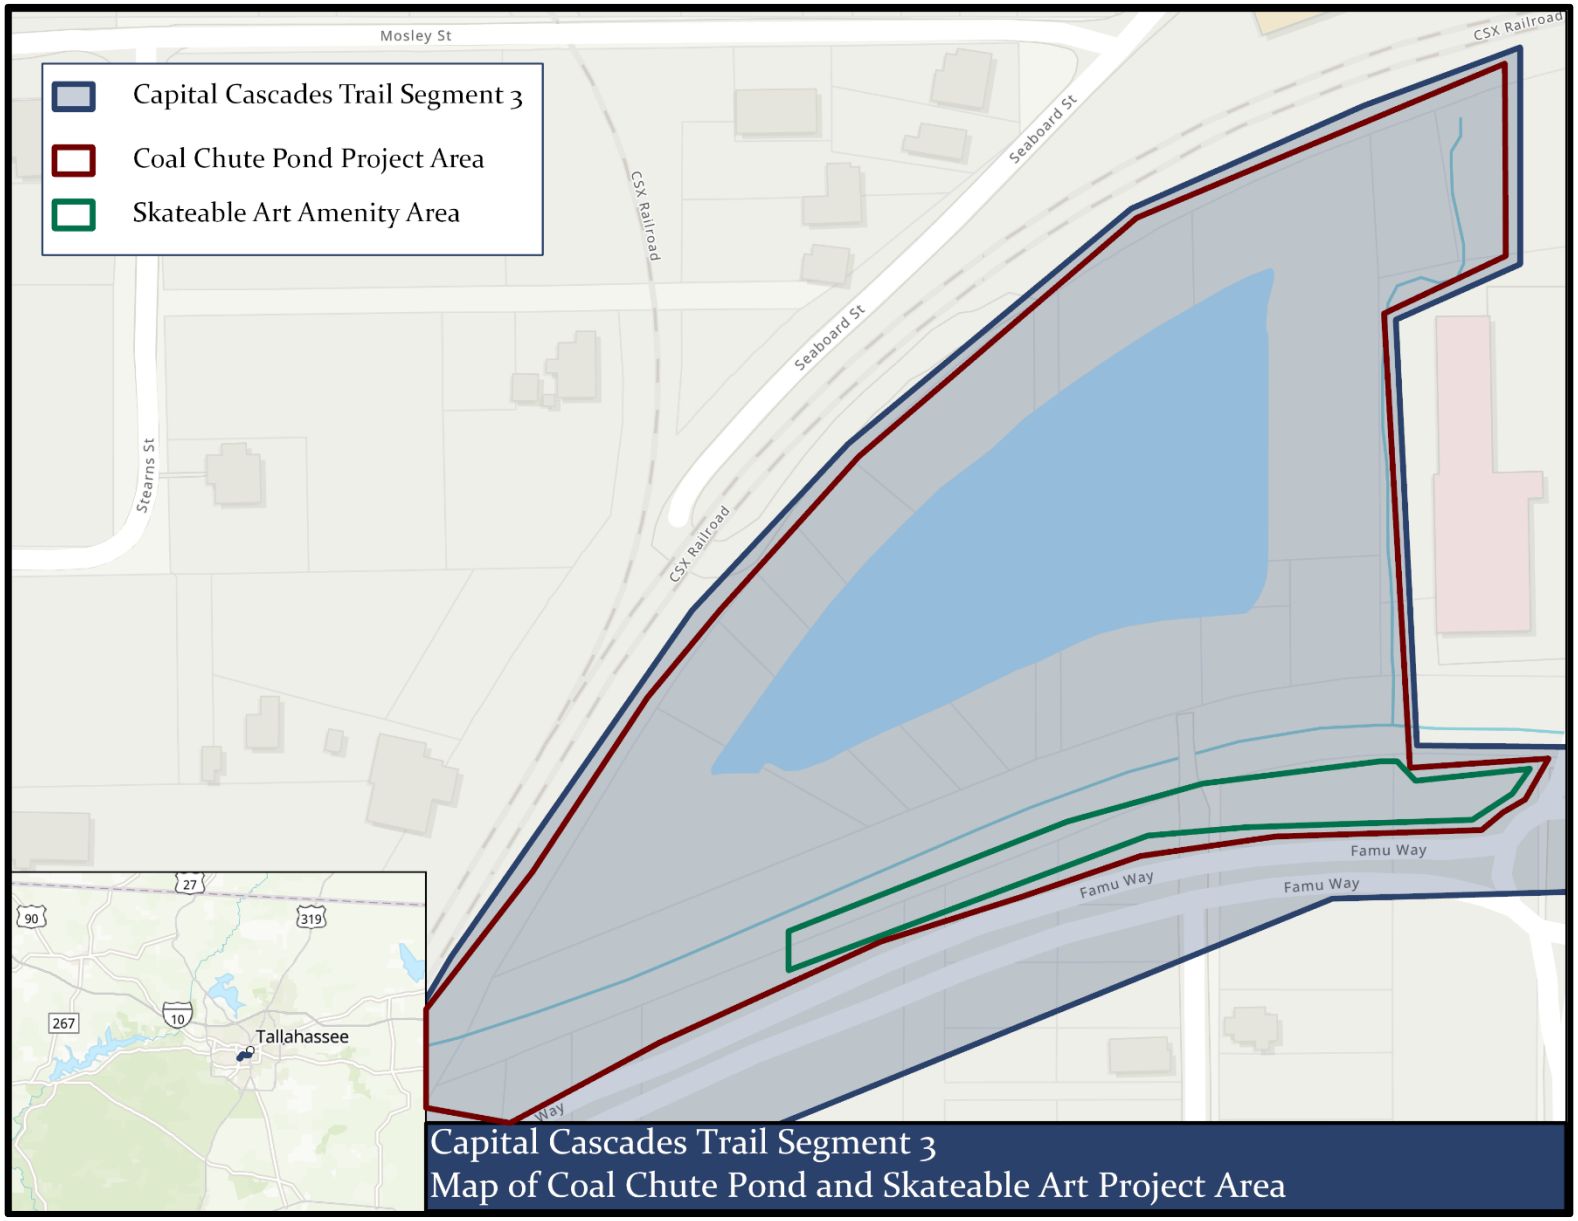

Capital Cascades Trail Segment 3
Map of Coal Chute Pond and Skateable Art Project Area

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/cct-segment-3-amenities
Staff Contact: Junious Brown
(850) 219-1063
Junious.Brown@BlueprintIA.org

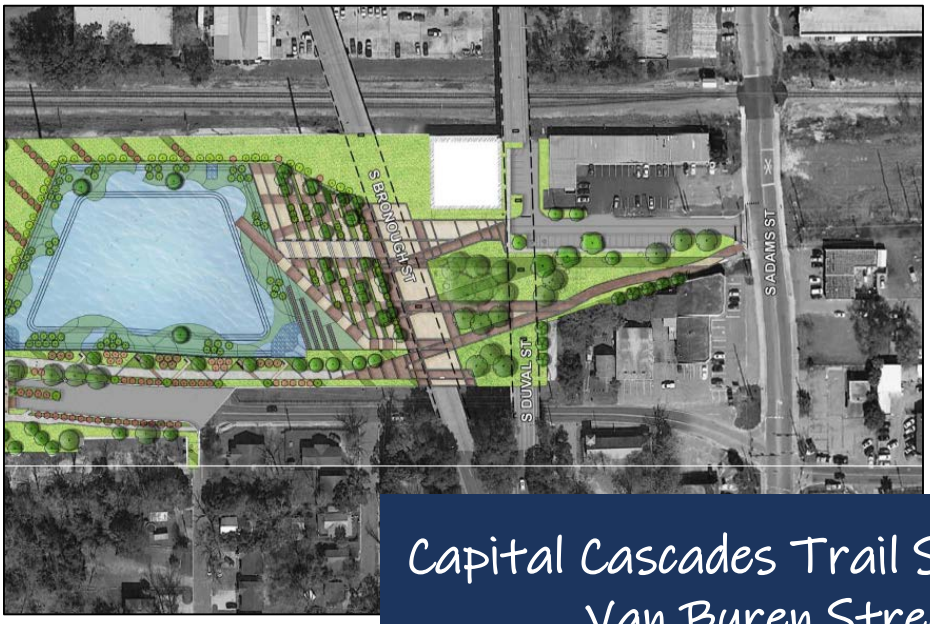

Capital Cascades Trail Segment 3
Van Buren Street

Project Highlights

- This project will enhance an area adjacent to the Anita Favors Thompson Plaza, and will provide parking to both the Plaza and Capital Cascades Trail.
- This project will also provide new pedestrian accessibility, underground utilities, greenspace, and decorative lights that will match the rest of the Capital Cascades Trail.

Current Status:

- A construction contract has been awarded to North Florida Asphalt.
- Construction started in May 2021 with a completion date anticipated in Q4 2021.



Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

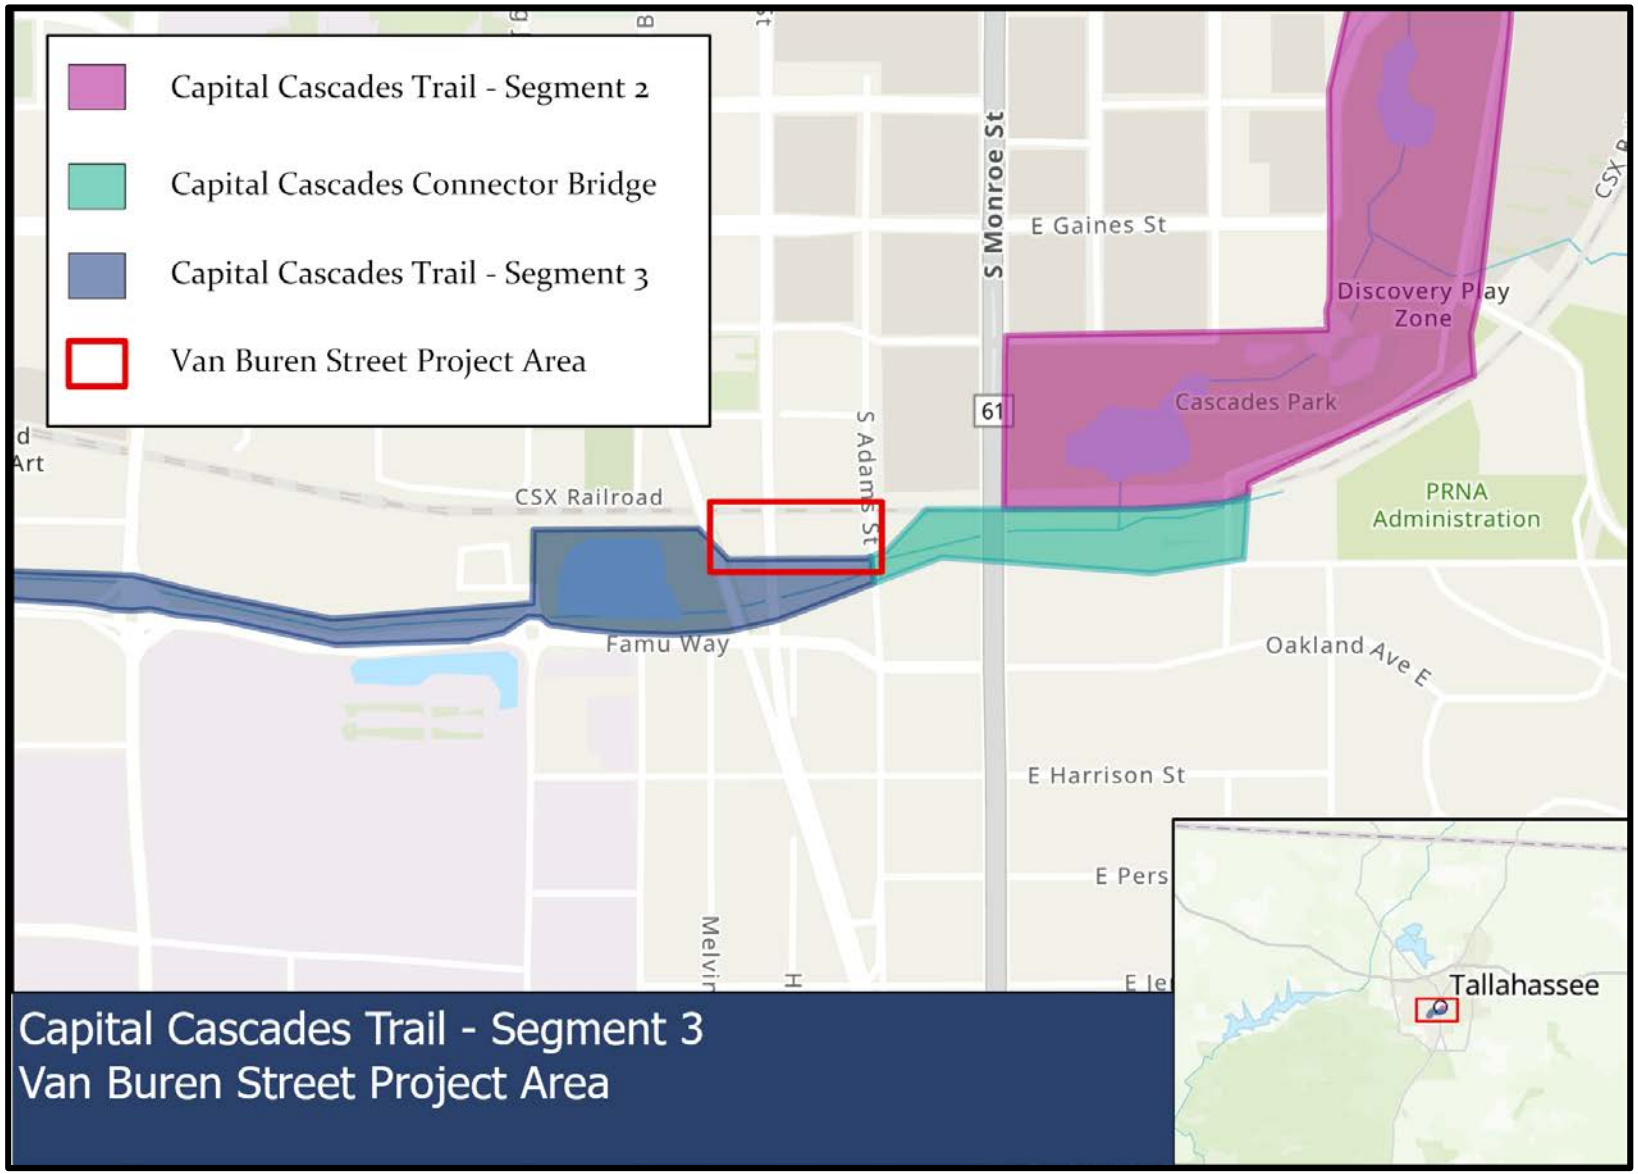

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/capital-cascades-trail/
Staff Contact: Abraham Prado
(850) 219-1076
Abe.Prado@BlueprintIA.org

Capital Cascades Trail Segment 4

Project Highlights

- This project will complete the Capital Cascades Trail network, which provides connectivity and stormwater improvements linking Leon High School in Downtown Tallahassee to Lake Henrietta.
- The project area is approximately 1.7 miles in length commencing at the confluence of the St. Augustine Branch and the Central Drainage Ditch (CDD), which is south of the new intersection of FAMU Way at Lake Bradford Road, and continues east to the CDD's confluence with Munson Slough, which is south of Orange Avenue and east of Springhill Road.
- The scope of the project includes achieving water quality improvements, greenway interconnectivity, and wetland creation.

Current Status:

- A consulting team has been selected for the design and planning of the project. Final contract negotiations are underway with a contract expected in the next 30 to 60 days.

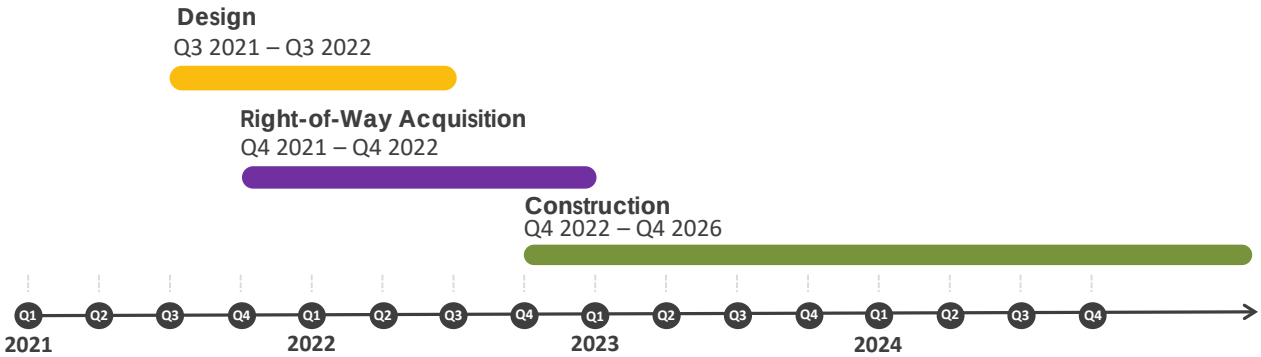

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

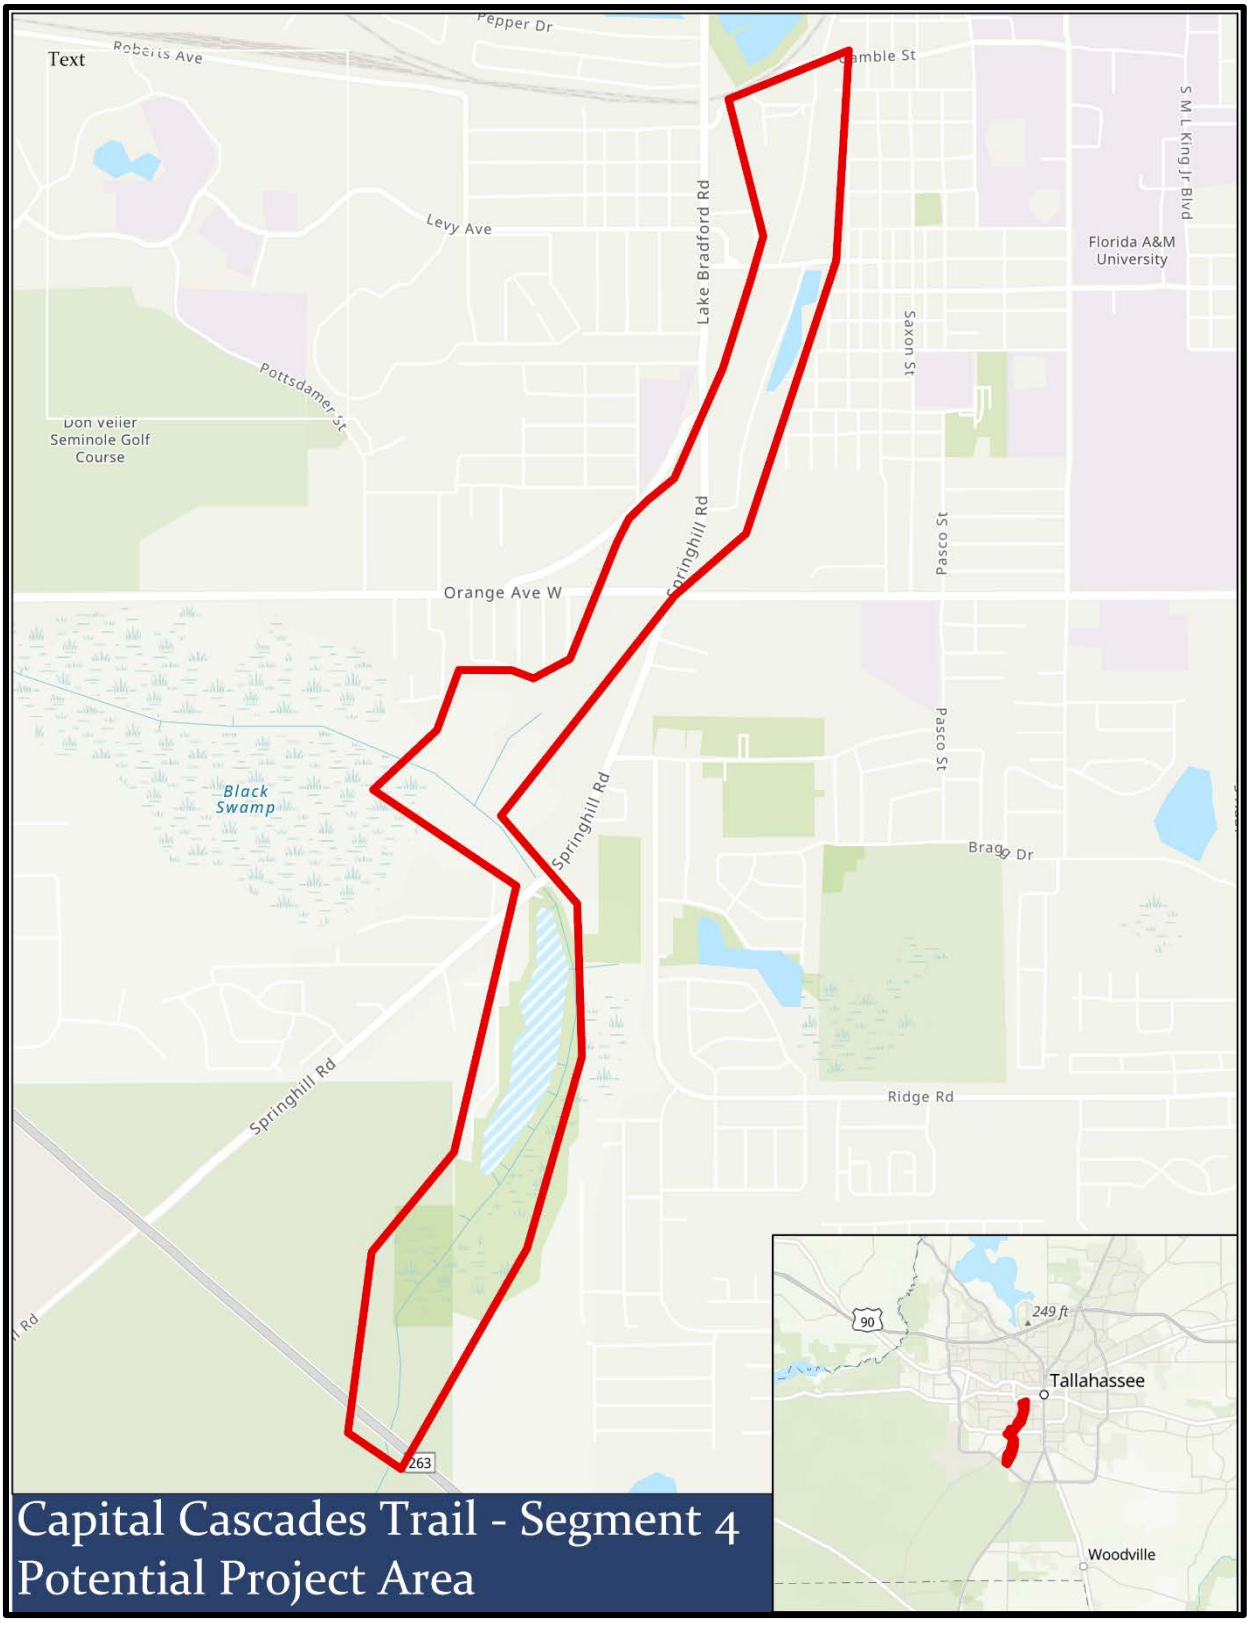

Capital Cascades Trail - Segment 4
Potential Project Area

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/capital-circle-southwest/
Contact: (850) 219-1060
nfo@blueprintia.org

Capital Circle Southwest

Project Highlights

- This approximately 5.5 mile project is the last phase of 16.5 miles of improvements to the Capital Circle corridor from Orange Avenue to Crawfordville Road .
- Consistent with other phases, this project will widen the road from two to six lanes, include bike lanes, a 10-foot wide multi-use trail, and a 5-foot sidewalk.
- Will include stormwater for roadway improvements, water quality enhancements, and land acquisition for the Capital Circle Southwest Greenway.

Current Status:

- Project is managed by Florida Department of Transportation (FDOT).
- Springhill Road to Orange Ave
    - Right-of-Way acquisition is underway through a partnership with FDOT and Blueprint.
    - Construction funded in FY 2022, in the amount of $58.2 million.
- Crawfordville Road to Springhill Road
    - Right-of-Way acquisition is underway through a partnership with FDOT and Blueprint for $4.9 million.
    - Construction deferred by FDOT to FY29 in the amount of $41.4 million.
- **Total FDOT Investment: + $125 million**

Preliminary Estimated Timeline



Last Updated: 06.22.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

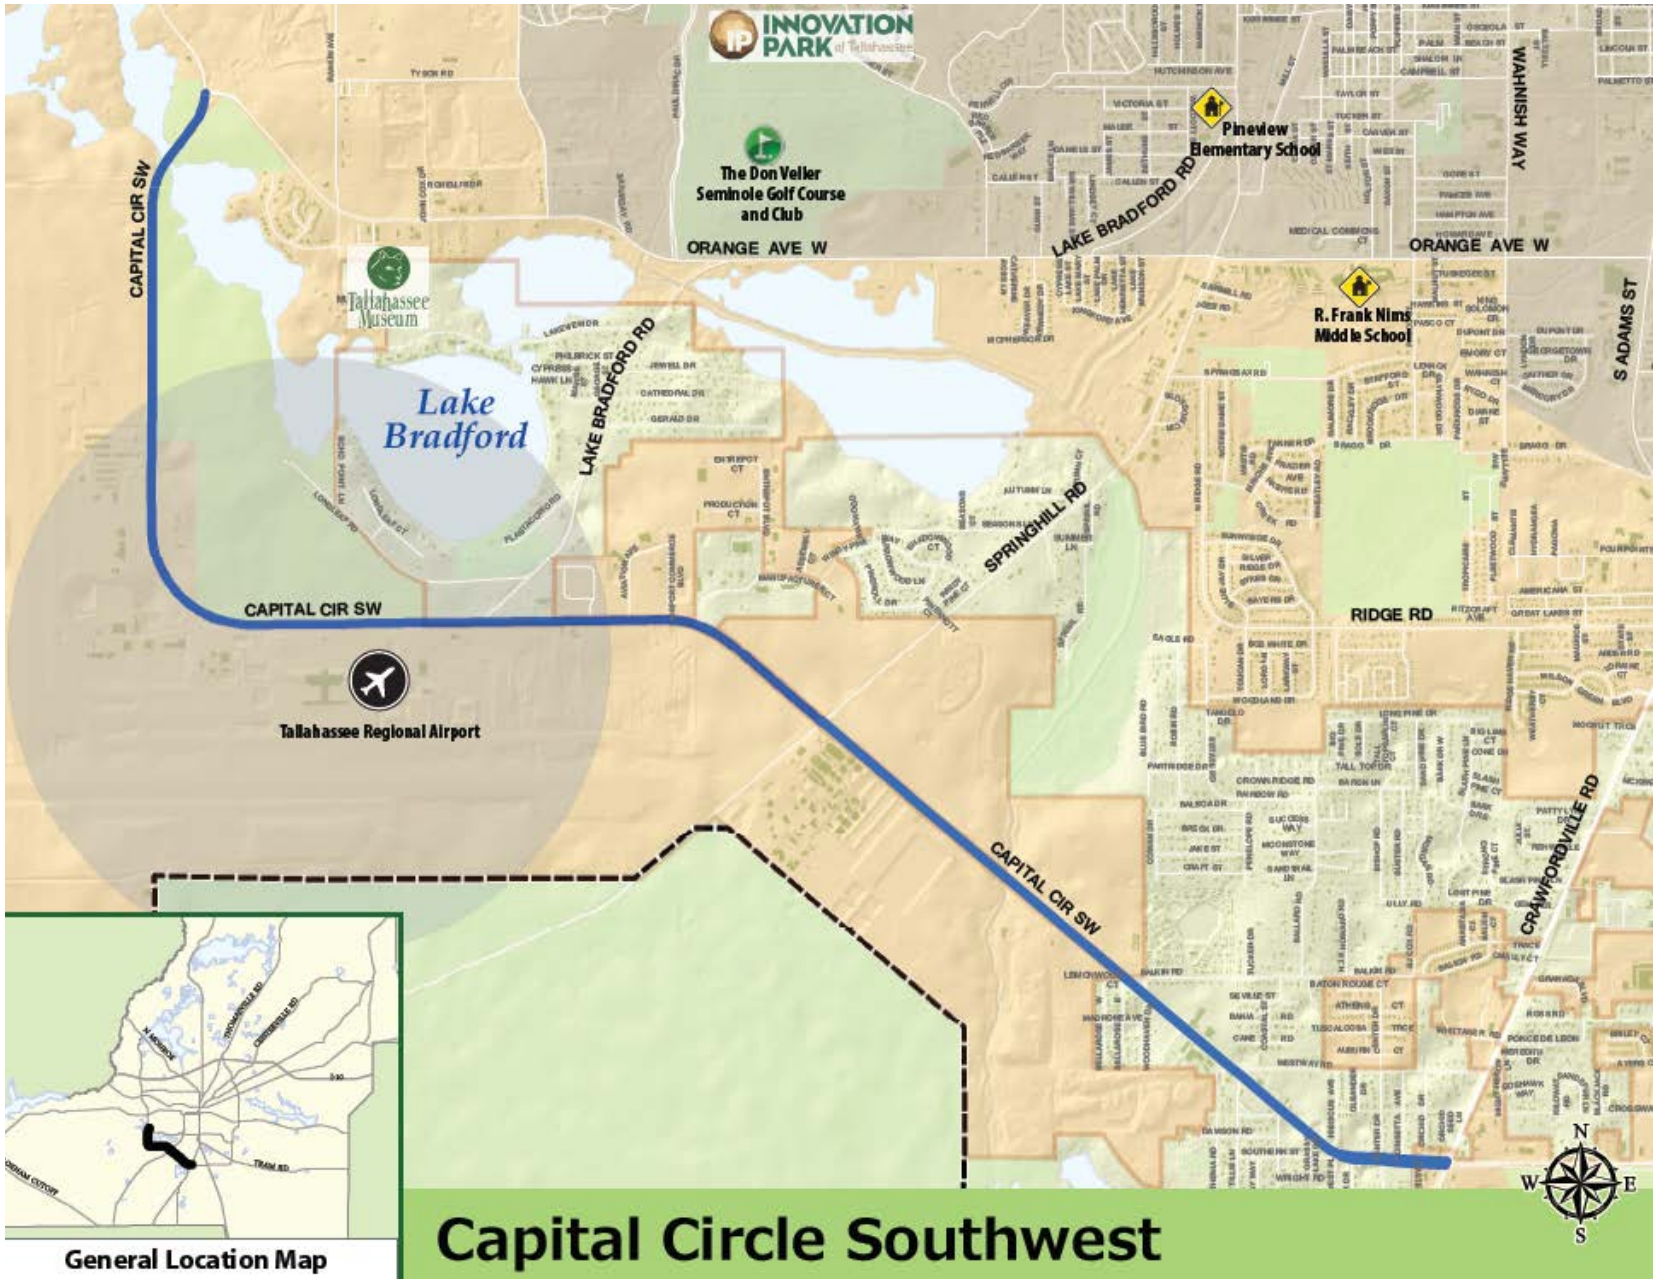

Capital Circle Southwest

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www. BlueprintIA.org
Staff Contact: Eric Mason
(850) 219-1085
Eric.Mason@BlueprintIA.org

Cascades Park Amphitheater Weatherization

Project Highlights

- In February 2018, Leon County Commissioners approved a concept to reduce rainwater impacts on the Amphitheater stage.
- This project implemented that concept, with the Leon County Division of Tourism acting as fiscal agent, and Blueprint managing the design construction and inspection services. Construction is complete.

Current Status:

- A new house speaker system purchase is currently being procured.
- The new system the last phase of an effort to reduce the impact of sound from the amphitheater on the nearby neighborhoods.

Preliminary Estimated Timeline



Last Updated: 06.22.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

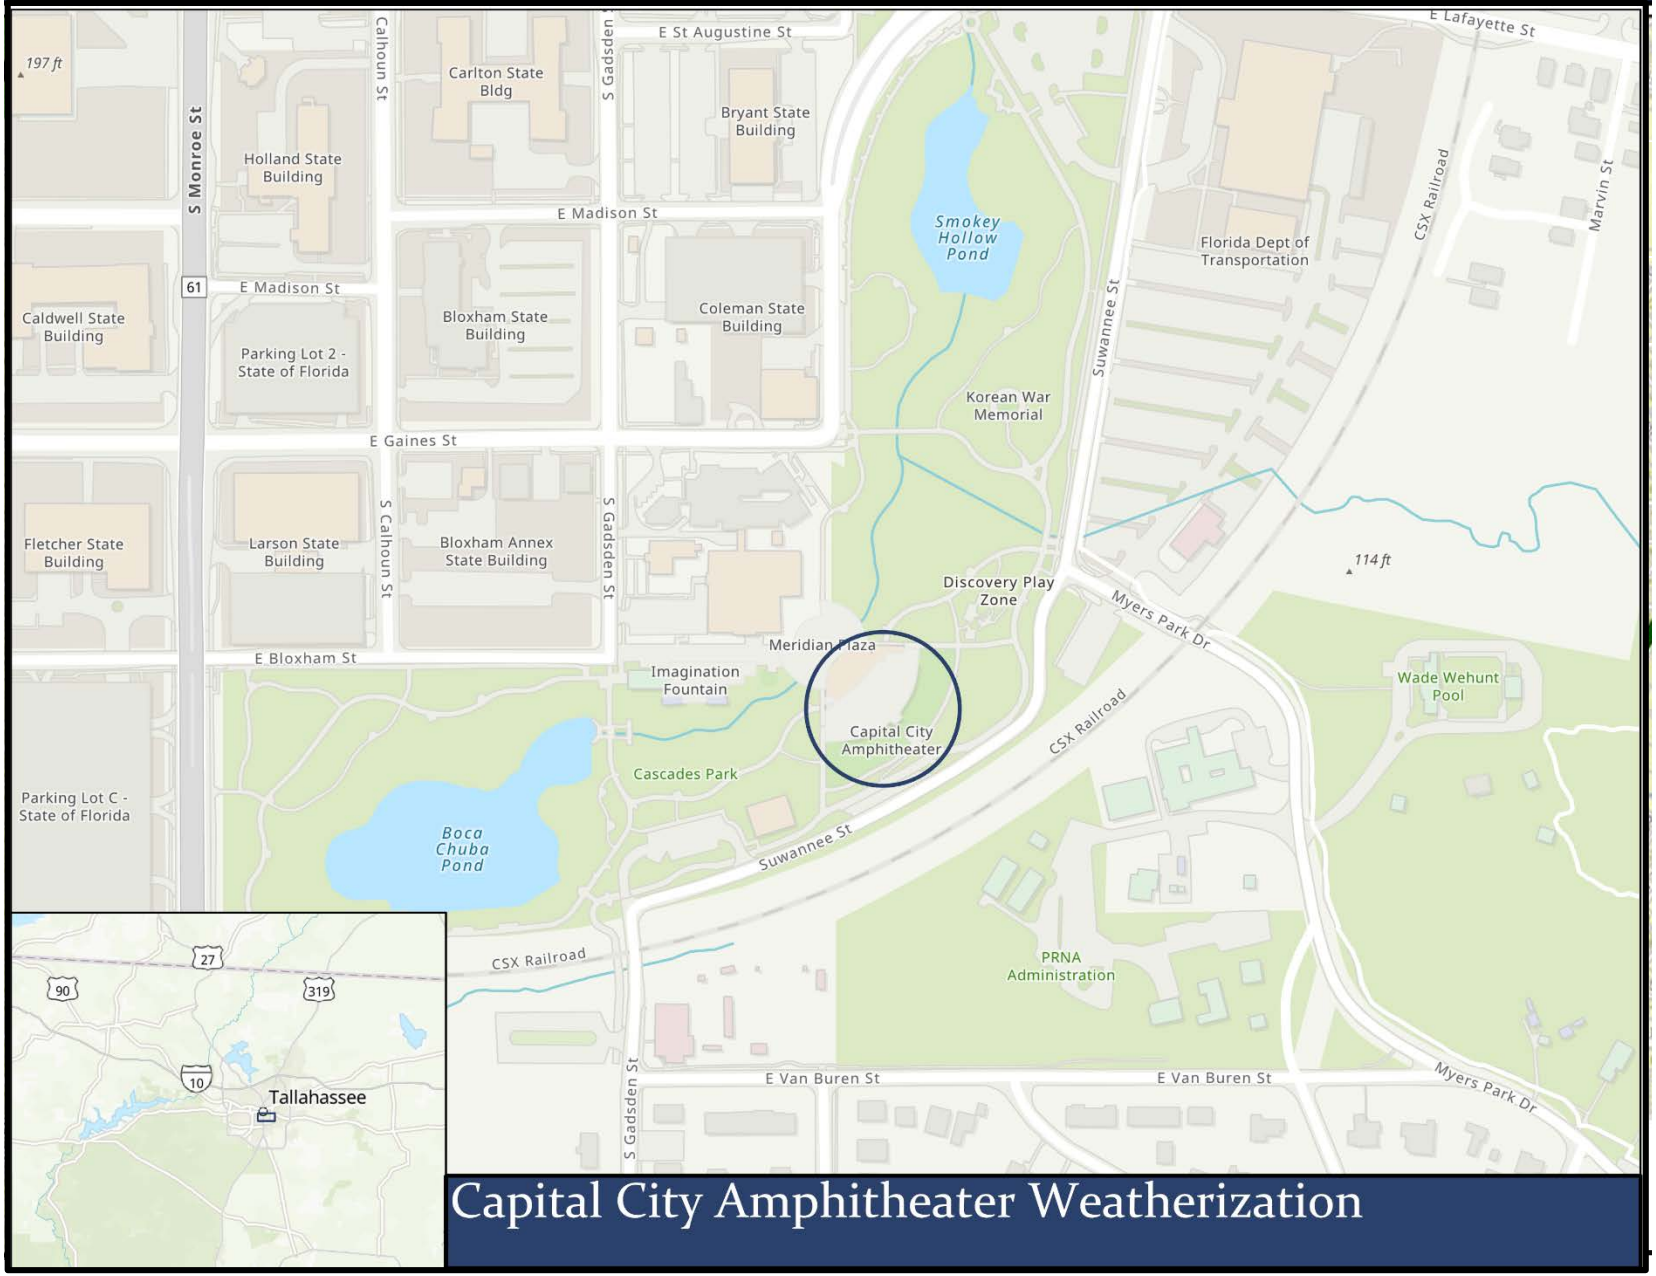

Capital City Amphitheater Weatherization

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Contact: (850) 219-1060
info@blueprintia.org

College Avenue Placemaking

Project Highlights

- This project implements the College Avenue Placemaking Action Plan which includes construction, stormwater improvements, streetscaping, and gateway enhancements.
- Specific improvements to be provided by this project will be determined at the time of project initiation.

Current Status:

- At the May 27, 2021 IA Board meeting, the request was made for staff to bring back an analysis on the current status on improvements proposed in the College Avenue Placemaking Project.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

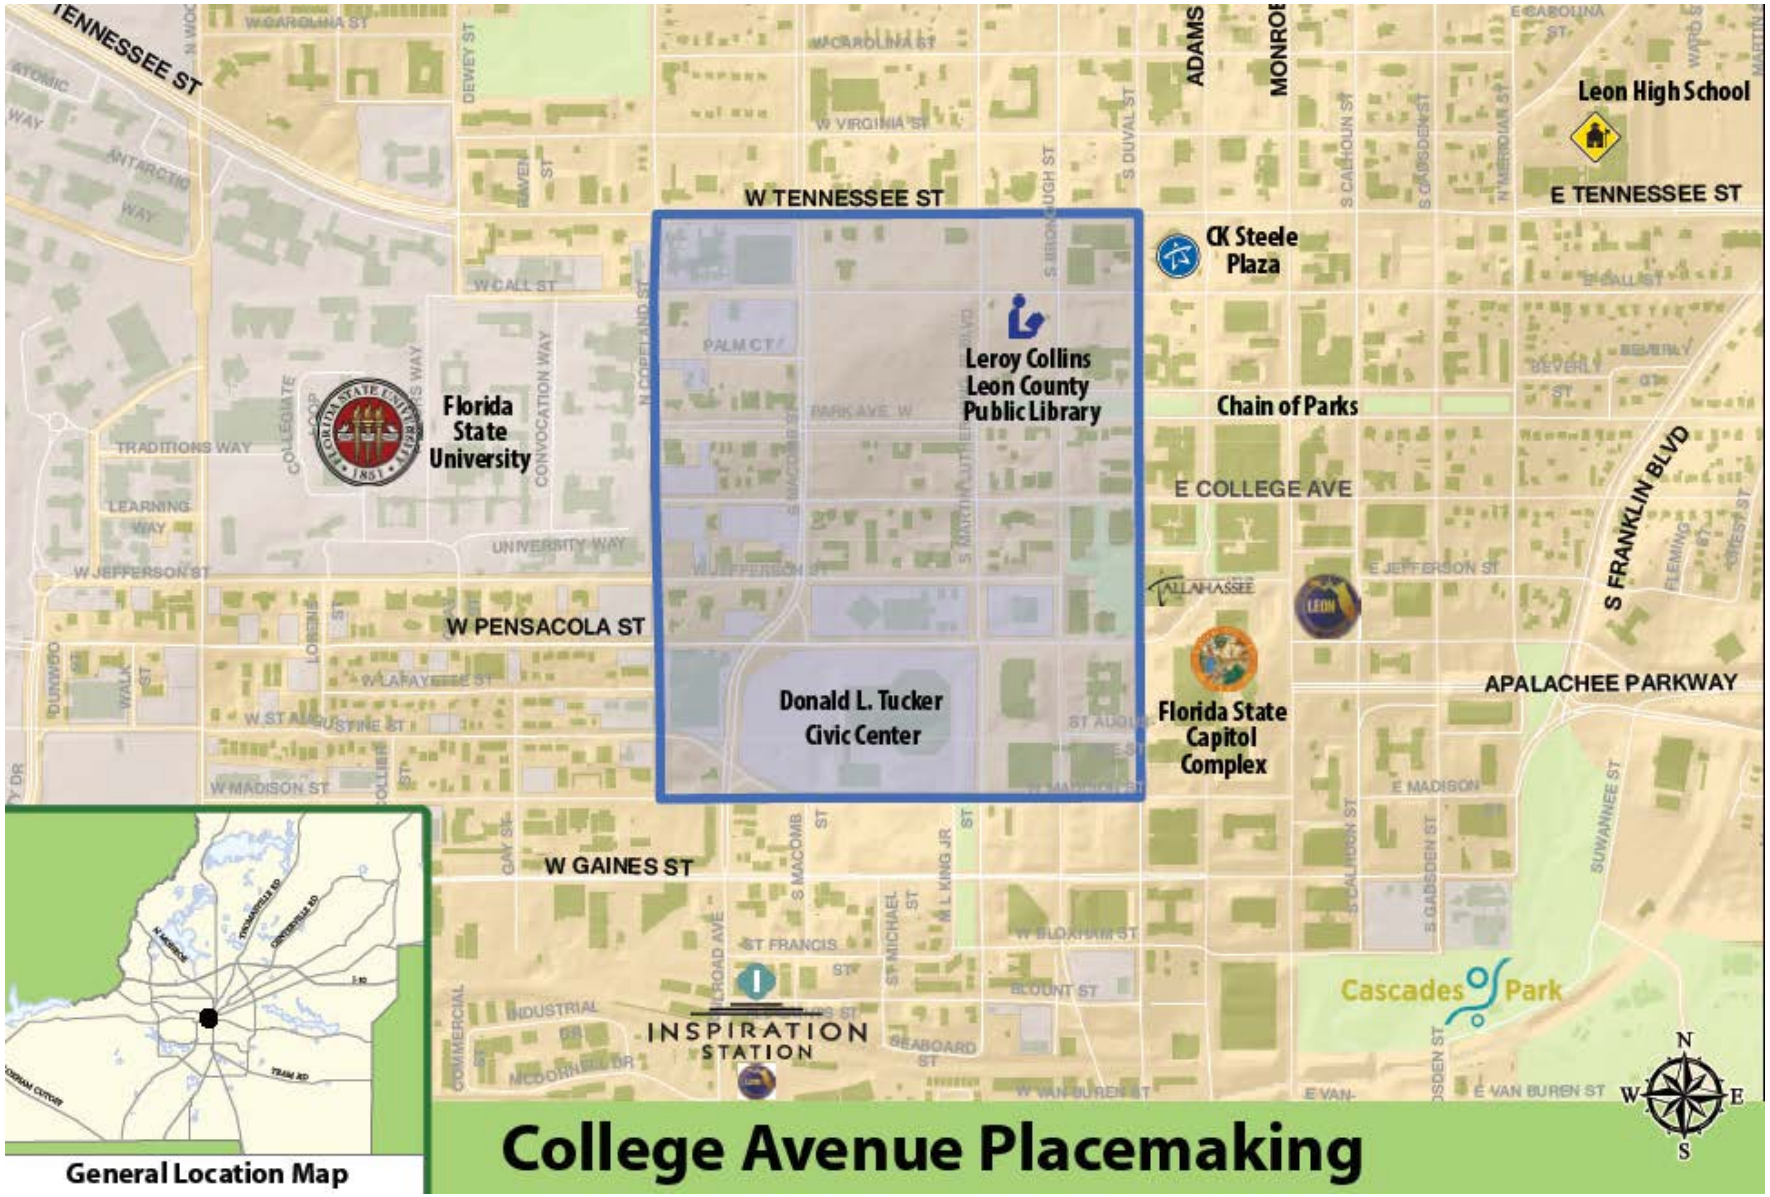

General Location Map

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/debbie-lightsey-nature-park/
Staff Contact: Junious Brown
(850) 219-1063
Junious.Brown@BlueprintIA.org

Debbie Lightsey Nature Park & Capital Circle SW Greenway

Project Highlights

- The project includes development of:
  - Approximately 6.6 miles of greenway trails in the CCSW corridor
  - A 113-acre nature park that includes an approximately 1.6 mile trail network
  - Boardwalks and overlooks for bird-watching
  - Creation of Golden Aster Trail and Munson Slough connection rom Lake Henrietta to CCSW.

Current Status:

- Park component concept ideas have been approved by the IA Board.
- The final design will be presented to the IA Board at the July 15th meeting for approval and authorization to procure construction services.

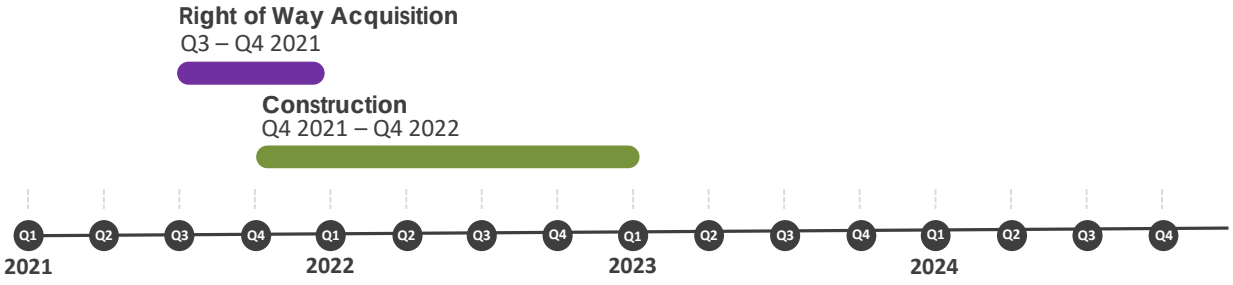

Last Updated: 06.21.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

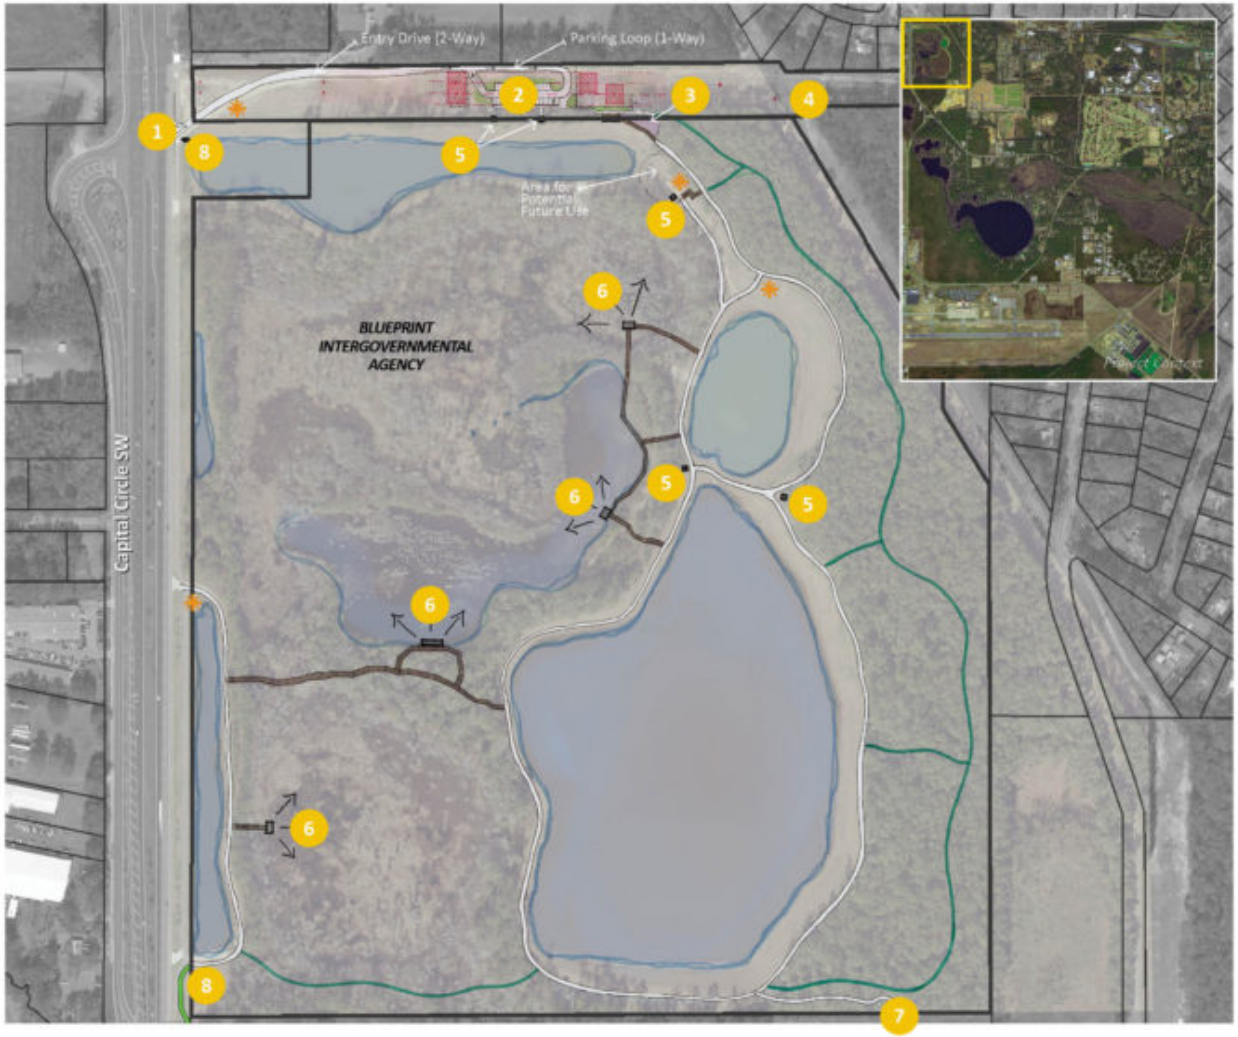

1. Main Park Entry
2. +/- 30 Parking Spaces
3. Nature Play Area
4. Pedestrian Access (from surrounding neighborhoods)
5. Picnic Pavilion
6. Overlook Views
7. Connection to FSU Rec Fields
8. Main Signage

- Eco-Art Opportunity
- Picnic Pavilion
- Main Trail* (10' wide, packed gravel for ADA accessibility)
- Boardwalk (8' wide)
- Rake and Ride bike trails*
- Future Capital Circle SW Multi-Use Trail
- Parcel Lines

* Exact trail paths to be determined on site

NOT TO SCALE

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org
Contact: Tatiana Daguillard, (850) 219-1081
Tatiana.Daguillard@blueprintia.org

Fairgrounds Beautification & Improvement

Project Highlights

- This project will enhance the existing Fairgrounds site while providing supporting new or expanded uses.
- A market study commissioned by the Board of County Commissioners was completed in 2015 which identified potential opportunities for improving the Fairgrounds site and supporting expanded uses.

Current Status:

- In September 2020, the IA Board approved $100,000 for an updated market feasibility study and alternative site analysis for the Fairgrounds.
- A consultant has been selected to conduct the updated market study which will provide a real estate analysis and evaluation of the Fairgrounds to recommend the best use options of the site.

Preliminary Estimated Timeline



Last Updated: 06.08.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Contact: (850) 219-1060
info@blueprintia.org

Florida A&M Entry Points

Project Highlights

- This project will provide funding to develop entry points to Florida A&M University at Osceola Street/Adams Street and Perry Street/Gamble Street.
- Intersection enhancements, turn signals, and intersection access improvements are potential improvements for this project.

Current Status:

- The Florida A&M Entry Points project is yet to be initiated.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

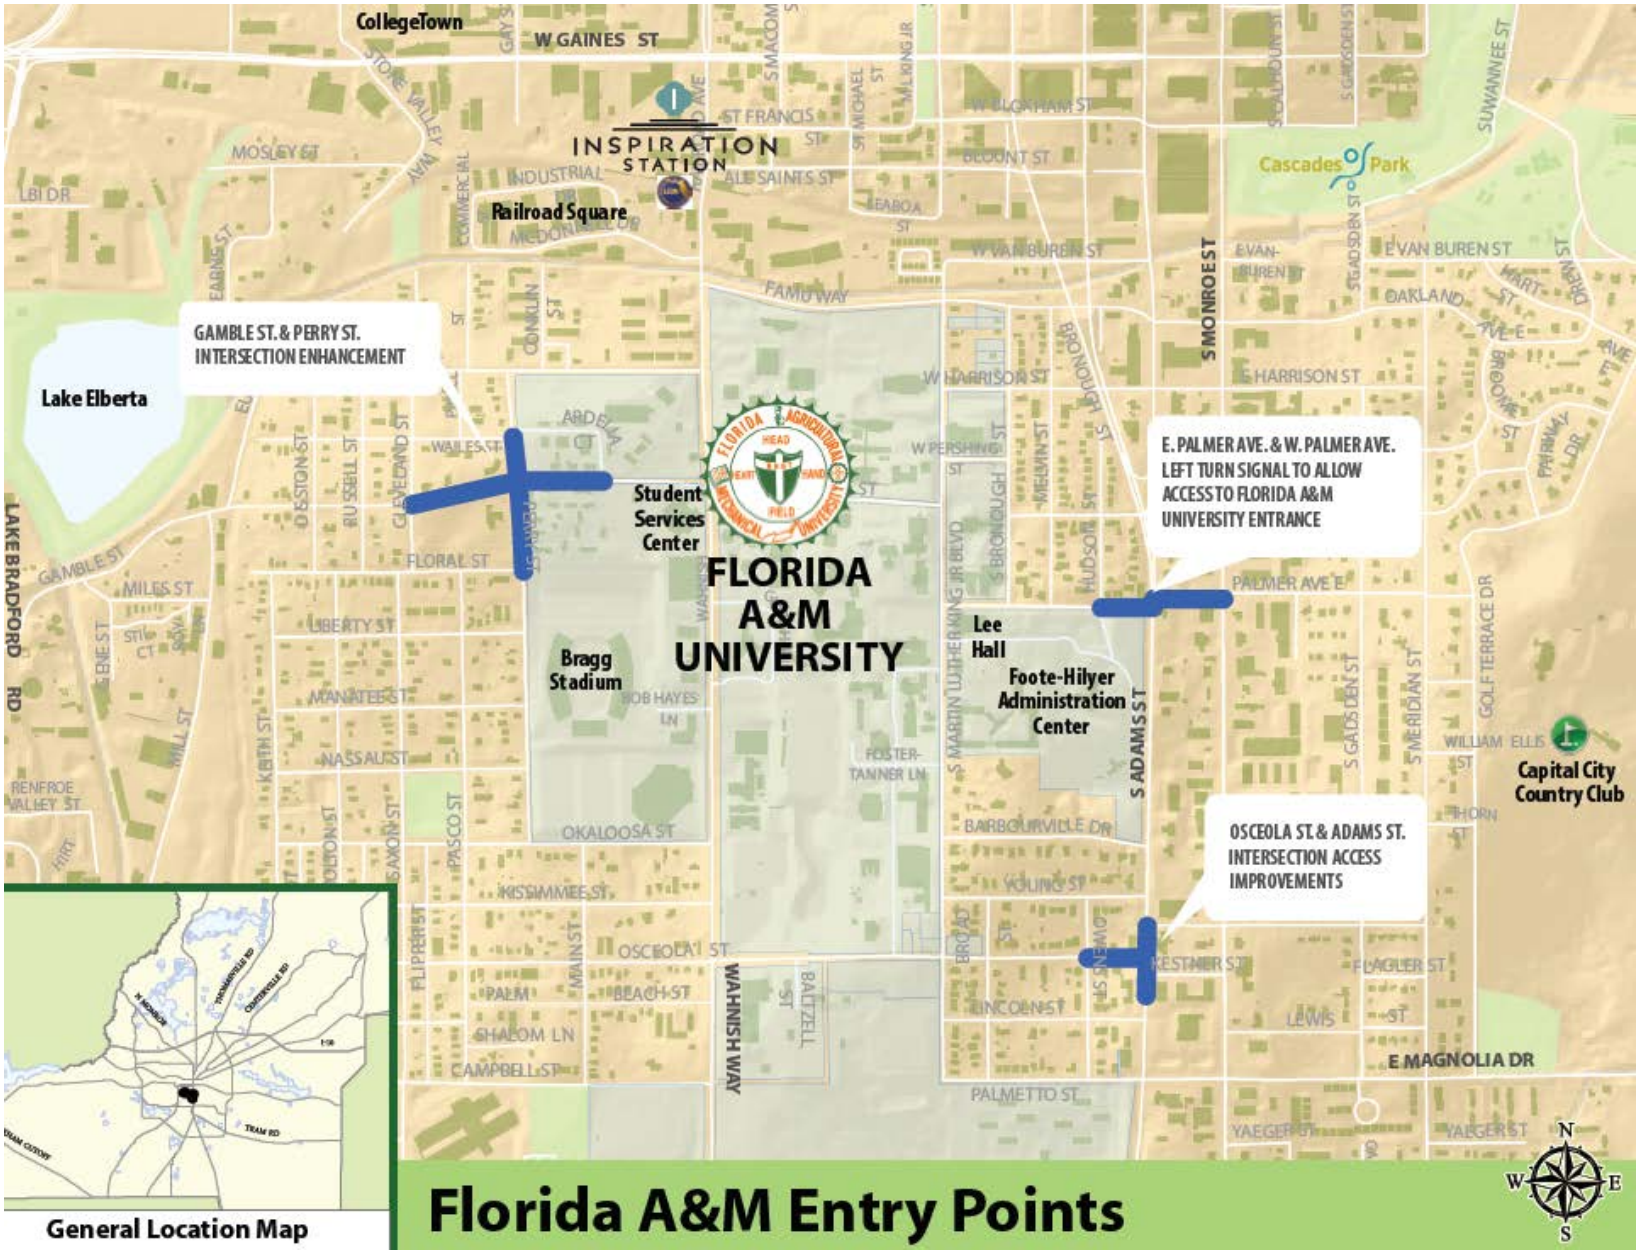

General Location Map

Florida A&M Entry Points

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: blueprintia.org/projects/greenways-master-plan-implementation/

Staff Contact: Mike Alfano
(850) 219-1075 Michael.Alfano@blueprintia.org

Implementation of the Greenways Master Plan

Project Highlights

- There are 32 Projects in the Greenways Master Plan totaling over 150 miles
- Blueprint has been tasked with continuing to implement these projects.
- IA Board has allocated $15.8 Million in annual installments over 20 years of $790,000 to implementing Greenways Master Plan projects.
- Blueprint will also be implementing Greenways Master Plan projects as part of their larger roadway projects.
- By the end of 2025, over 70 miles of Greenways Master Plan projects will have begun being implemented by Blueprint, the City, the County, the CRTPA, or private developers.

Current Status:

- The IA Board has prioritized five Greenways Master Plan Projects for Implementation. They are:
    - University Greenway
    - Thomasville Road Greenway
    - Capital Circle Southwest Greenway and Debbie Lightsey Nature Park
    - Lake Jackson & Lake Jackson South Greenways (combined for implementation)
    - Southwood Greenway (portions approved as part of a leveraging opportunity with the City of Tallahassee).
- The remaining projects were approved by the IA Board December 10, 2020.
- The IA Board approved the FY 2022 Greenways Work Program May 2021.

Last Updated: 6.15.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

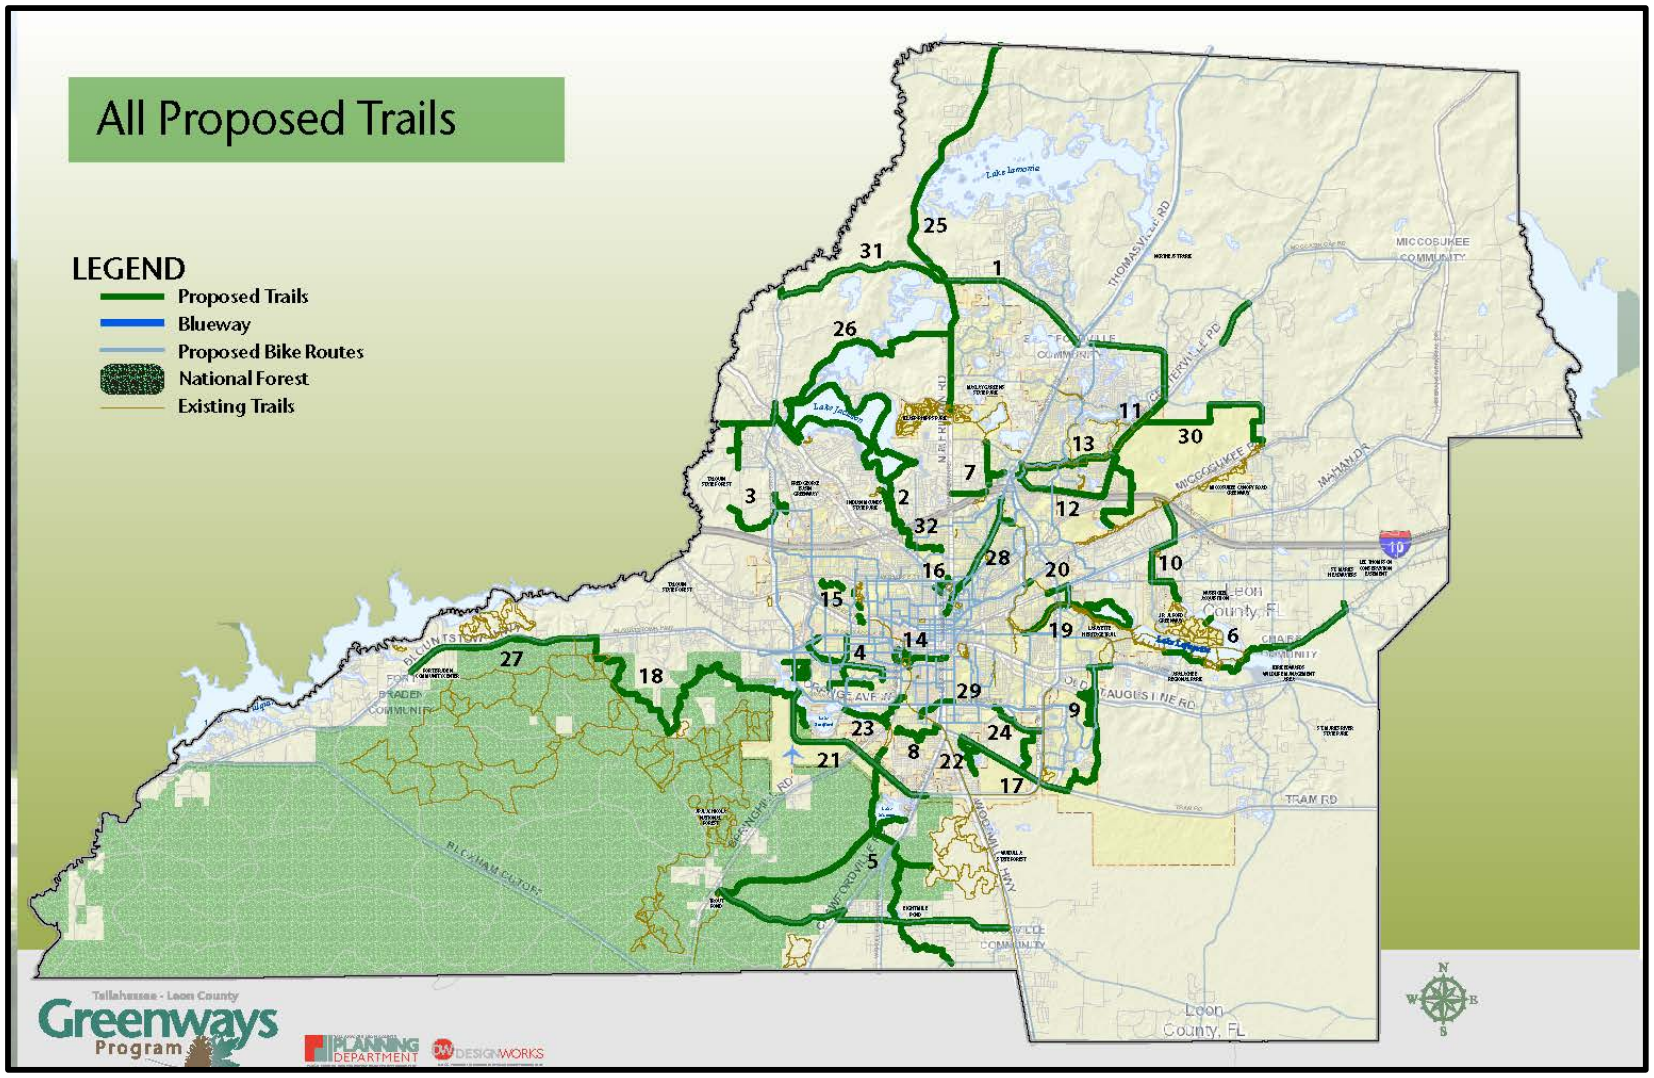

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/lake-jackson-greenway/
Staff Contact: Sue Tanski
(850) 219-1071
susan.tanski@blueprintia.org

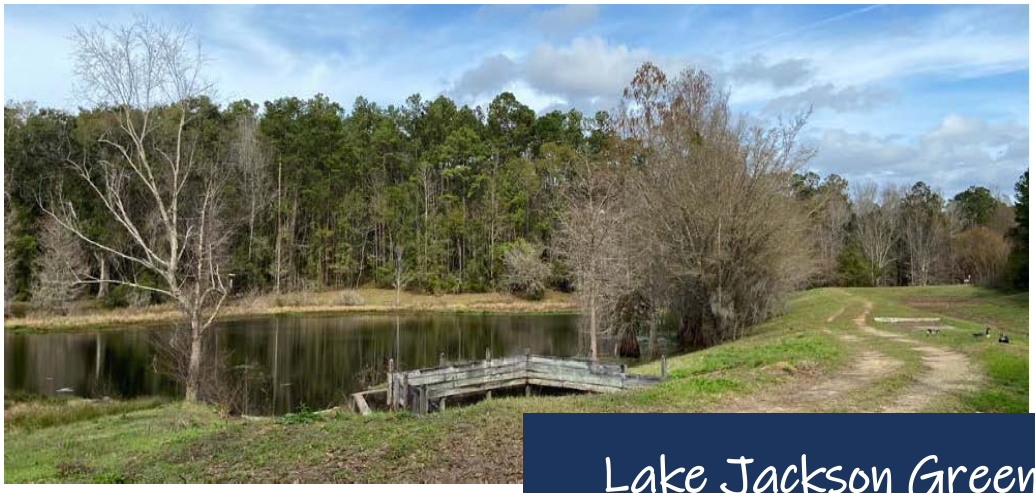

Lake Jackson Greenways

Project Highlights

- Will expand regional bicycle and pedestrian mobility and provide connectivity from Lake Jackson Mounds Archaeological State Park to Lake Ella at Fred O. Drake Park in Midtown Tallahassee
- Includes an over 5-mile long route that will connect a string of public spaces and recreational, residential, and commercial areas.

Current Status:

- The preliminary engineering phase kicked off in June 2020. A feasibility study was completed in November 2020. Results were published to the Intergovernmental Agency Board at their February 2021 meeting.
- Two community engagement sessions were facilitated in March 2021.
- Public engagement on the Lake Jackson Greenways on project design.
- Final design plans will be brought to the IA Board for approval and authorization to procure construction in 2022.

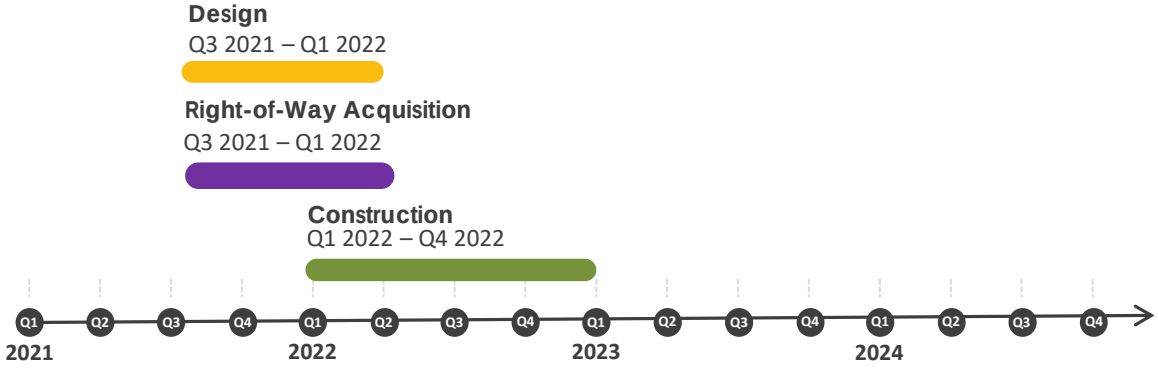

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

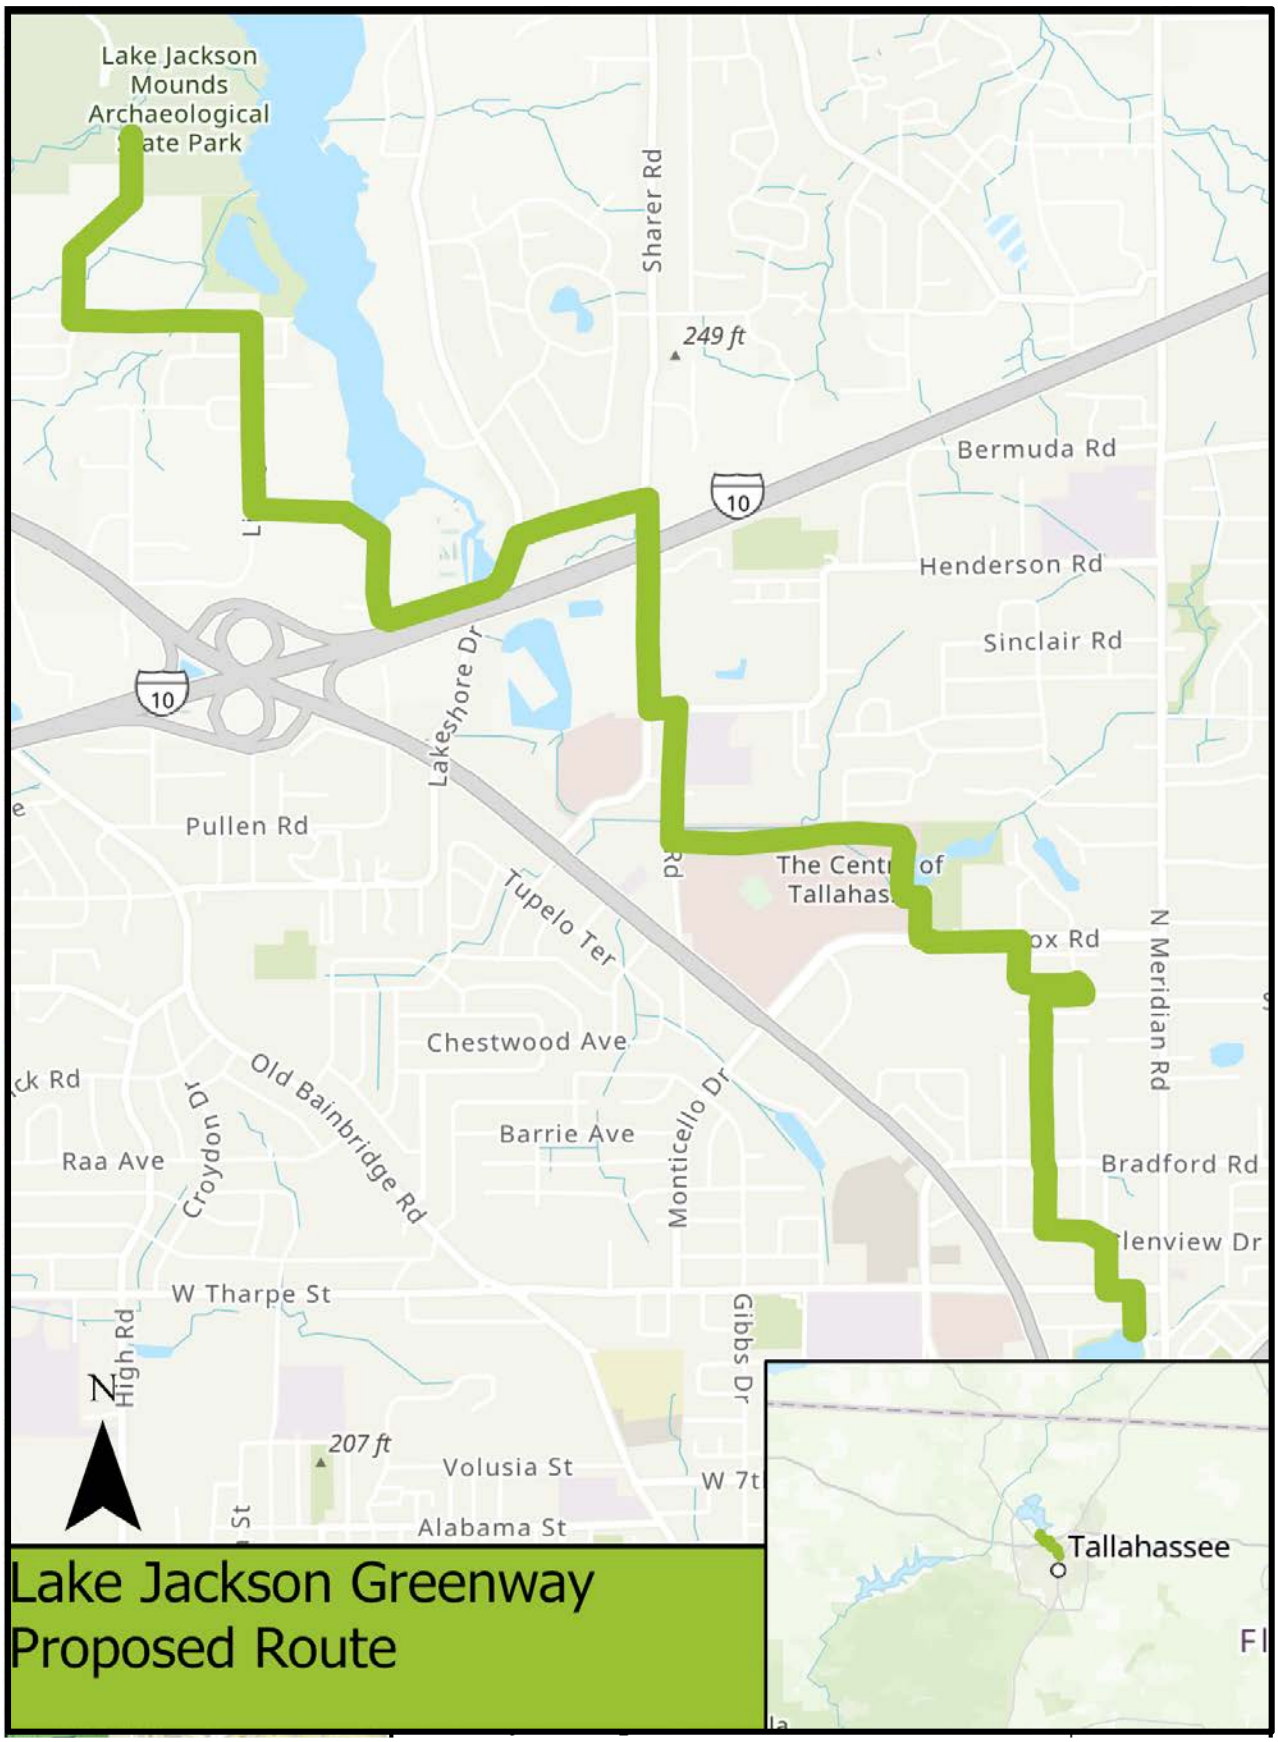

Lake Jackson Greenway
Proposed Route

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: Sue Tanski
(850) 219-1071
susan.tanski@blueprintia.org

Lake Lafayette and St. Marks Regional Linear Park

Project Highlights

- This project will connect 7,200 acres of public recreation lands east of Capital Circle Southeast, as well as provides ecosystem restoration and flooding analysis.
- This project will also provide key trail connections to area amenities, including Tom Brown Park, Lafayette Heritage Park, St. Marks Headwaters, and the Apalachee Regional Park.

Current Status

- The FY 2021 allocation of $750,000 will funding initial environmental studies and planning for this project.

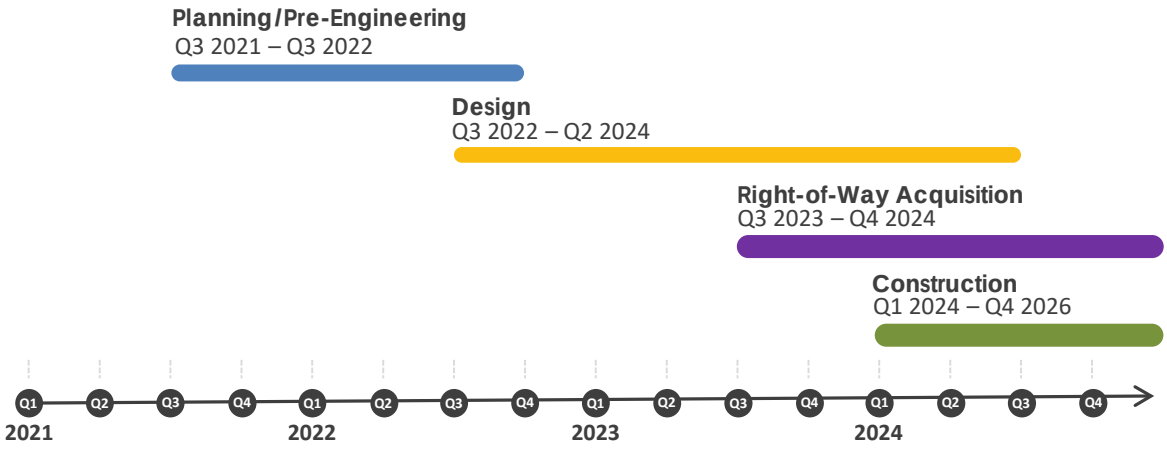

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

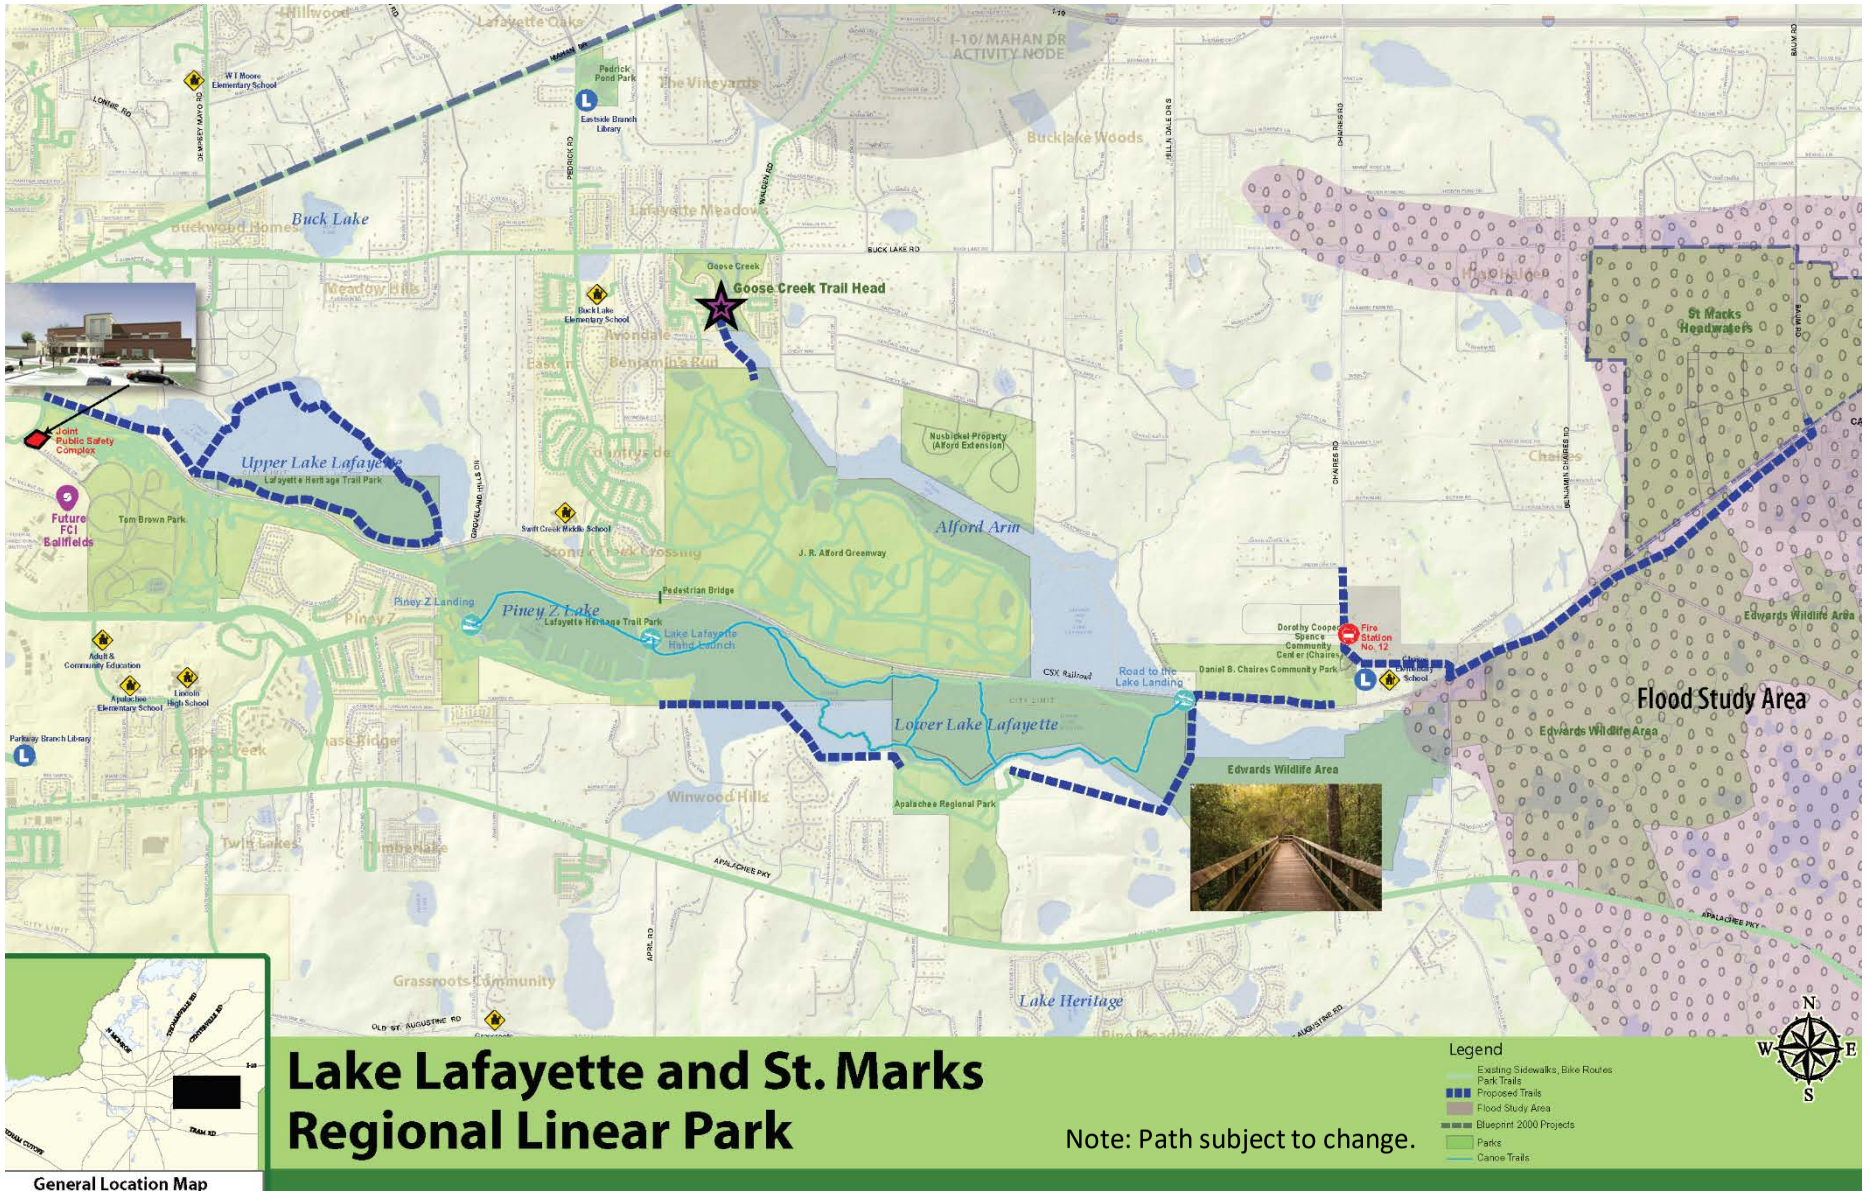

Lake Lafayette and St. Marks Regional Linear Park

Note: Path subject to change.

General Location Map

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/magnolia-drive-multi-use-trail/
Staff Contact: Junious Brown
(850) 219-1063
Junious.Brown@BlueprintIA.org

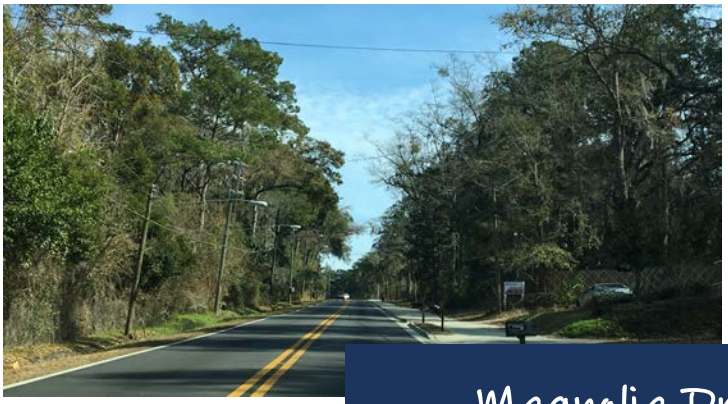

Magnolia Drive Trail

Project Highlights

- The project will construct a new shared-use trail from S. Adams to Apalachee Parkway to provide connectivity and improve safety, as well as underground electric utilities from Chowkeebin Nene to S. Monroe Street.
- Trail construction is complete from Monroe Street to Adams Street (Phase 6).
- Pontiac Drive to Meridian Street will be further improved by undergrounding electric utilities and retrofitting the shared-use trail to add a landscaped buffer.

Current Status:

- Design and right-of-way acquisitions are complete on Phase 1 Retrofit and Phase 4 (S. Monroe to S. Meridian). Construction is expected to begin in Summer 2021.
- Design for Phase 2 (Pontiac to Diamond) and Phase 3 (Diamond to Apalachee) is 90% complete. Right-of-way acquisition is ongoing. Construction is currently scheduled to begin in Summer 2022.

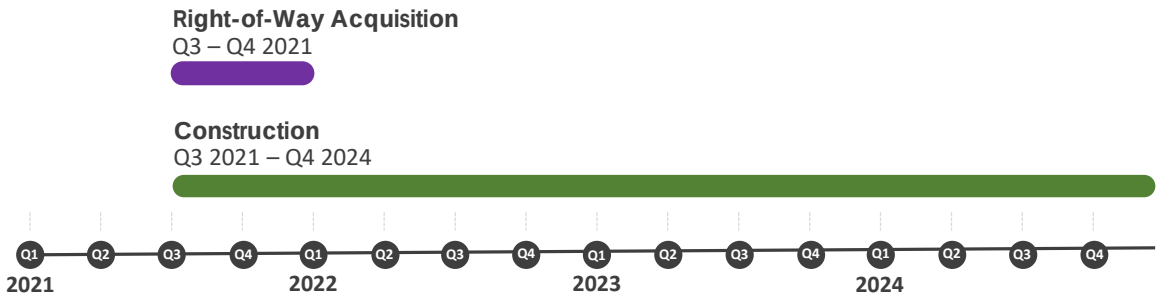

Last Updated: 06.21.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

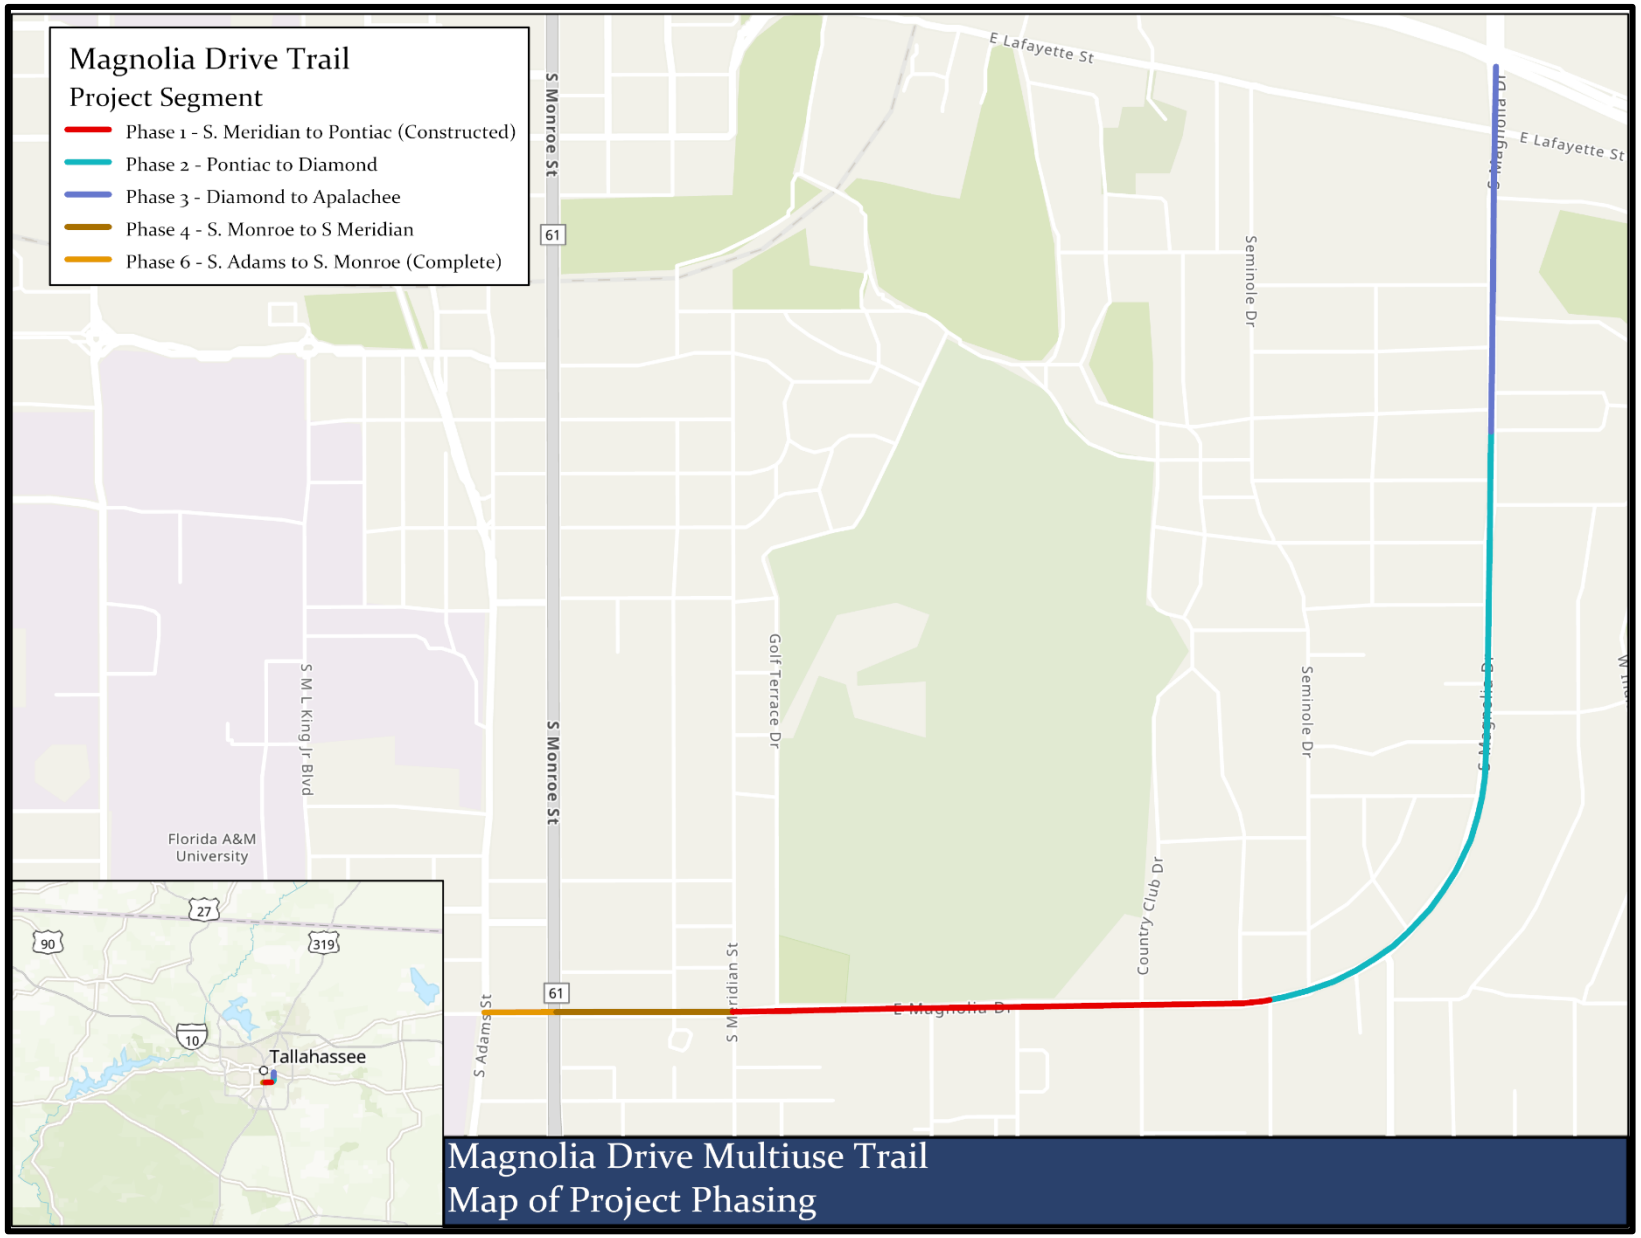

Magnolia Drive Multiuse Trail
Map of Project Phasing

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
http://tallahasseemarketdistrict.com/

Staff Contact: Sue Tanski
(850) 219-1071
susan.tanski@blueprintia.org

Market District Placemaking

Project Highlights

- This project is being advanced as a component of the City of Tallahassee's Market District Multi-Purpose Stormwater Project.
- This project will create a new park along Maclay Boulevard and will improve pedestrian connectivity in and around the Market District.
- The first phase of the project will create the park. Other improvements, such as planned trails and pedestrian improvement projects, will be implemented following the completion of the park.

Current Status:

- The IA Board approved the Market District Park Concept Plan at the May 27th, 2021 meeting and authorized Blueprint to advertise, negotiate, and award a contract for design services for the Blueprint Market District Park.
- Design will begin Fall 2021 and will include community engagement activities. Construction will follow In early 2022.
- The IA Board also approved to remove the northern portion of the Timberlane Greenway and neighborhood connections from the future Market District Placemaking Project Elements.
- Planning for future phases of the Market District Placemaking Project will begin in Fall 2021.

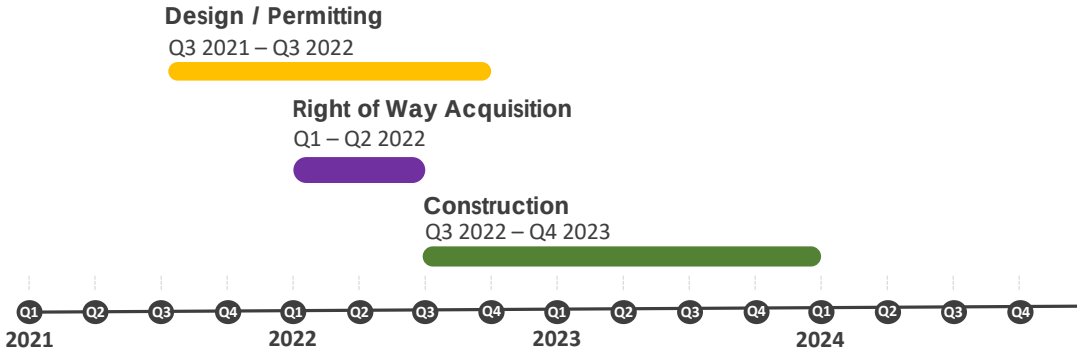

Last Updated: 06.21.2021

BLUEPRINT INTERGOVERNMENTAL AGENCY

programming concept: central park

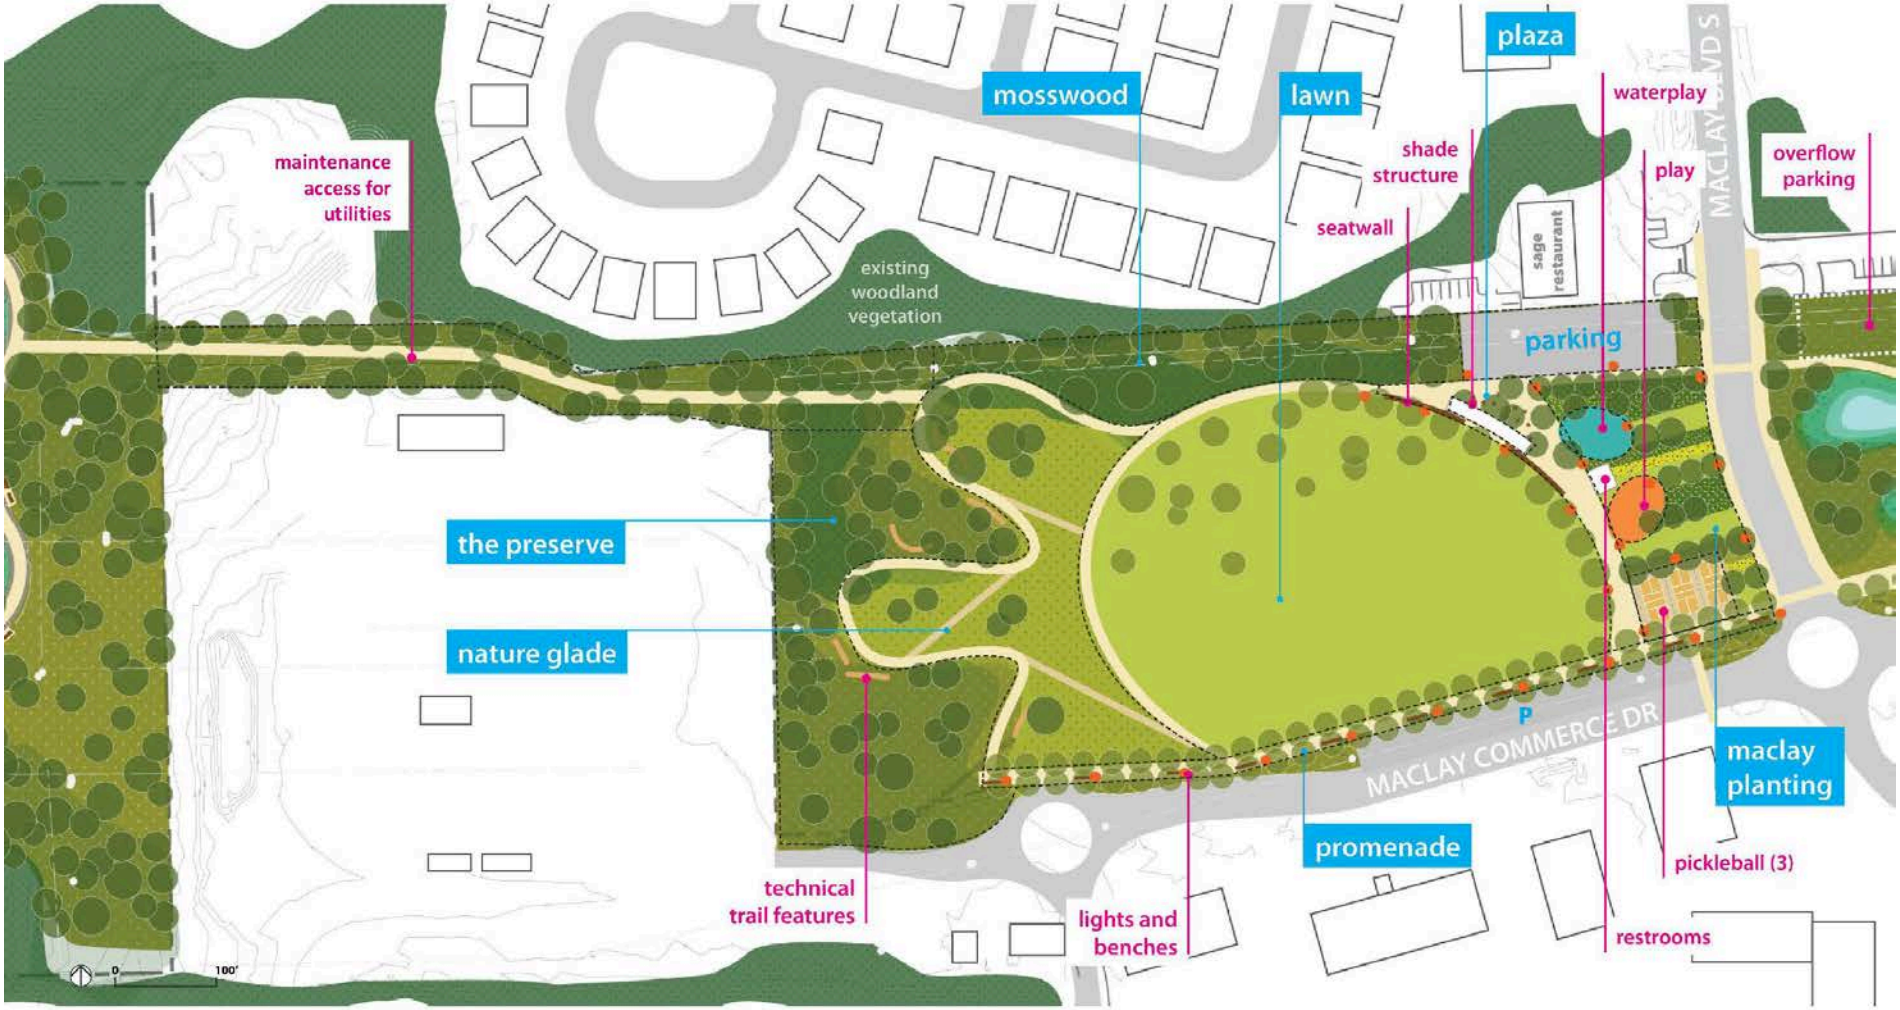

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: Sue Tanski

(850) 219-1071

susan.tanski@blueprintia.org

Meridian Greenway

Project Highlights

- This project will create an approximately 6 mile long shared-use trail project serving equestrians, pedestrians, runners, hikers, bicyclists, and other non-motorized users
- The greenway will connect Elinor Klapp-Phipps Park and Alfred B. Maclay Gardens State Park to the Northeast, Bannerman Road, and Orchard Pond Greenway's East trailhead.

Current Status:

- The implementation of the Meridian Greenway from Bannerman Road to the Lake Overstreet Trailhead is currently included in the scope of the Northeast Connector Corridor Project.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

Meridian Greenway

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: (850) 219-1060
info@blueprintia.org

Midtown Placemaking

Project Highlights

- The IA Board authorized $1,000,000 in FY2021 for engineering and design services along Thomasville Road from Monroe Street to Seventh Avenue.
- Blueprint will also coordinate with the newly established Midtown Stakeholders Committee as the project is developed.
- Over the past three years, the Capital Region Transportation Planning Agency (CRTPA) has conducted numerous traffic studies and developed proposed concepts for streetscaping, safety, and resiliency improvements along the Thomasville Road and Monroe Street corridors.

Current Status

- At the December 10, 2020 IA Board meeting, the IA Board approved the procurement of design services for the Thomasville Road South segment, from 7th Avenue to N. Monroe Street. The scope for these services is under development.

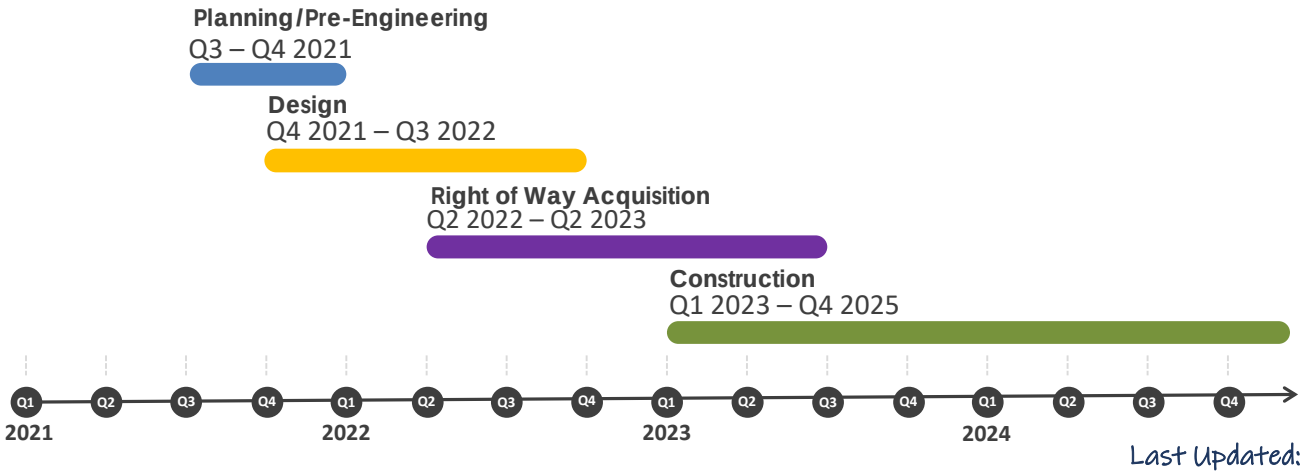

Last Updated: 06.21.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/monroe-adams-corridor-placemaking/
Contact: Michael Alfano (850) 219-1075
Michael.Alfano@BlueprintIA.org

Monroe-Adams Corridor Placemaking

Project Highlights

- This Placemaking Project will create safe, comfortable streets for pedestrians, transit users, and cyclists along the Monroe-Adams corridor.
- This project identifies improvements to five streets connecting the Monroe Street and Adams Street corridors, including: Harrison Street, Pershing Street, Jennings Street, Perkins Road, and Kestner Street.

Current Status:

- The first phase of the Monroe-Adams Placemaking Project will include preliminary survey work and concept design.
- Concepts from the Monroe Adams Action Plan will be updated through public engagement with Florida A&M University, the surroundings communities, and area businesses, to develop project concepts.
- Concept development will kickoff in June 2021, with public engagement anticipated for Fall 2021.

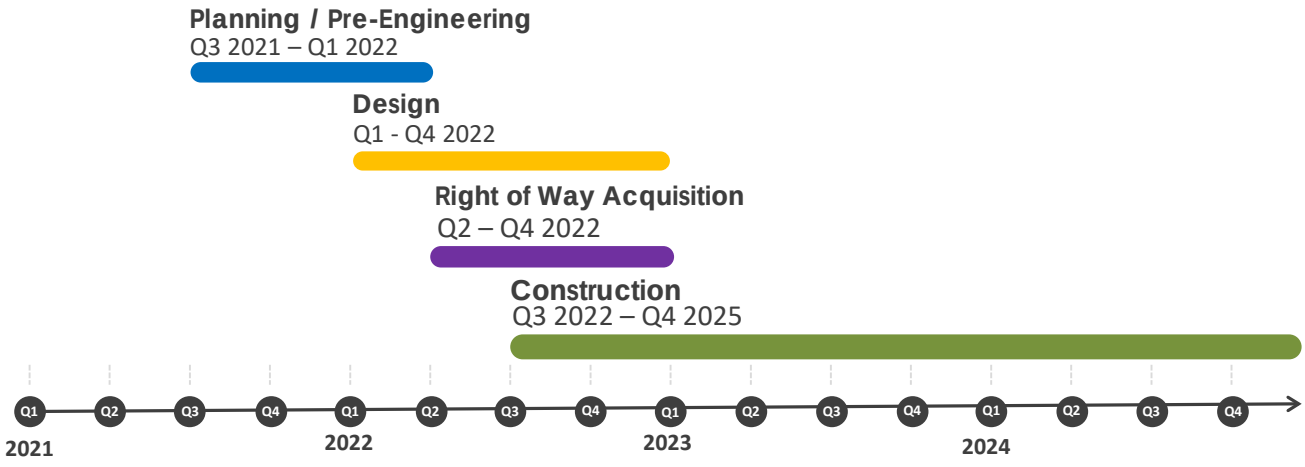

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

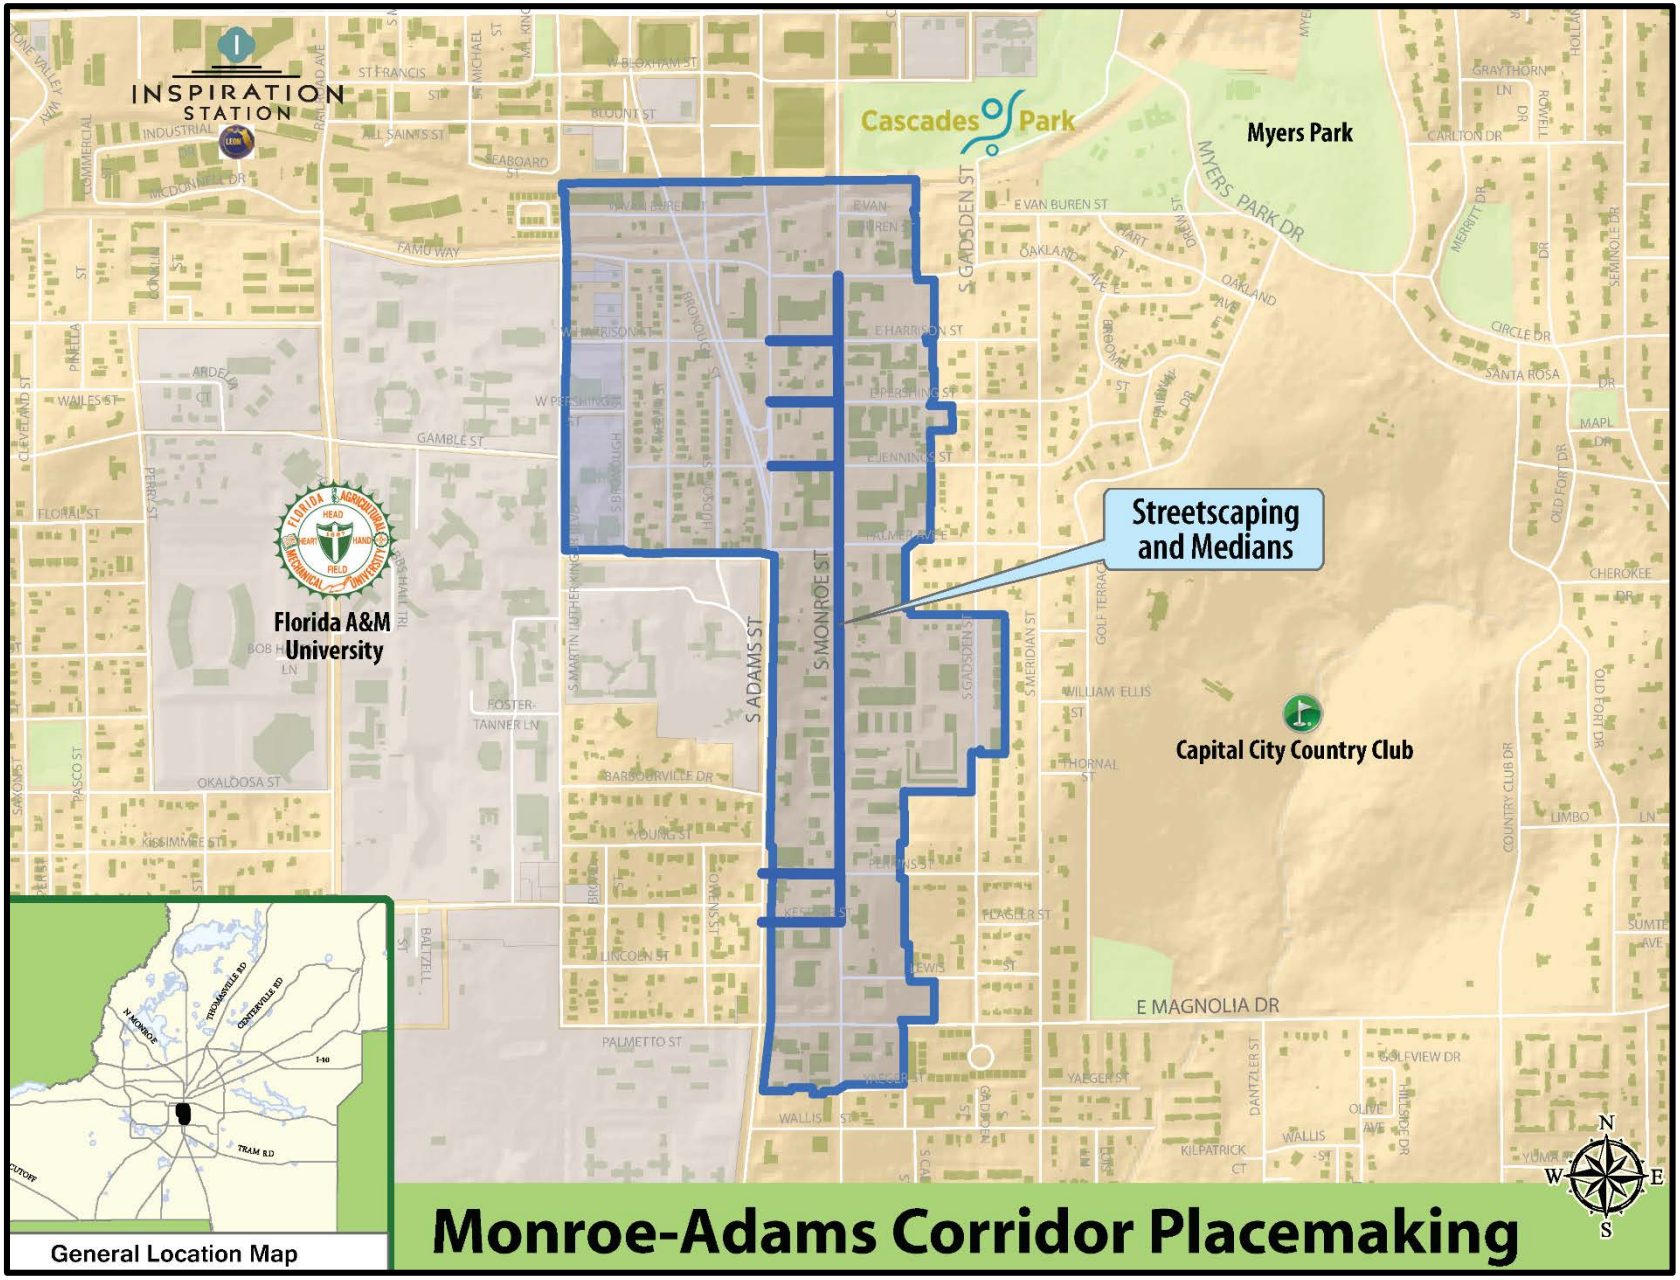

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org
Contact: (850) 219-1060
info@blueprintia.org

North Monroe Gateway

Project Highlights

- Creates northern gateway entrance into Tallahassee that clearly identifies and brands Tallahassee from Interstate 10 to Seventh Avenue.
- Project goals include improving safety through pedestrian and bicycle enhancements, promoting reinvestment, and improving the quality of life for residents and daily commuters.

Current Status:

- While this project has not yet been initiated by Blueprint, staff has been collaborating with FDOT on improvements to the North Monroe corridor consistent with the goals of the Blueprint 2020 North Monroe Gateway project.
- Since 2014 FDOT has invested $7.67 million in improving corridor, with the majority of investment supporting the Blueprint 2020 project goals.
- The tentative FDOT FY 2021 –2026 Work Program includes $486,190 in funding for the design of a sidewalk on the west side of North Monroe from John Knox to Lakeshore Drive. Blueprint is coordinating with FDOT and the City to explore opportunities to enhance landscaping as part of this project.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
www.bannermanroad.com
Staff Contact: Megan Doherty
(850) 219-1060
Megan.Doherty@Blueprintia.org

Northeast Corridor Connector: Bannerman Road & Meridian Greenway

Project Highlights

- Enhances the Bannerman Road corridor by widening to four lanes from Quail Common Drive to Preservation Road and adding a median to accommodate turn lanes from Quail Common Drive to Meridian Road.
- Improvements also include new multimodal facilities along Bannerman Road to improve accessibility and safety for people walking and biking.
- The Meridian Greenway project will create an approximately 6 mile long shared-use trail project serving equestrians, pedestrians, runners, hikers, bicyclists, and other non-motorized users.

Current Status

- Field survey and technical analyses, including intersection evaluation, environmental assessment, and stormwater planning, are currently underway.
- Design is anticipated to begin summer 2021.
- The 2020 Traffic Feasibility Analysis and the widening of Bannerman Road to four lanes from Quail Common Drive to Preservation Road was approved by the IA Board at their September 17, 2020 meeting.
- Blueprint Staff are currently reviewing potential routes and implementation options for the Meridian Greenway.

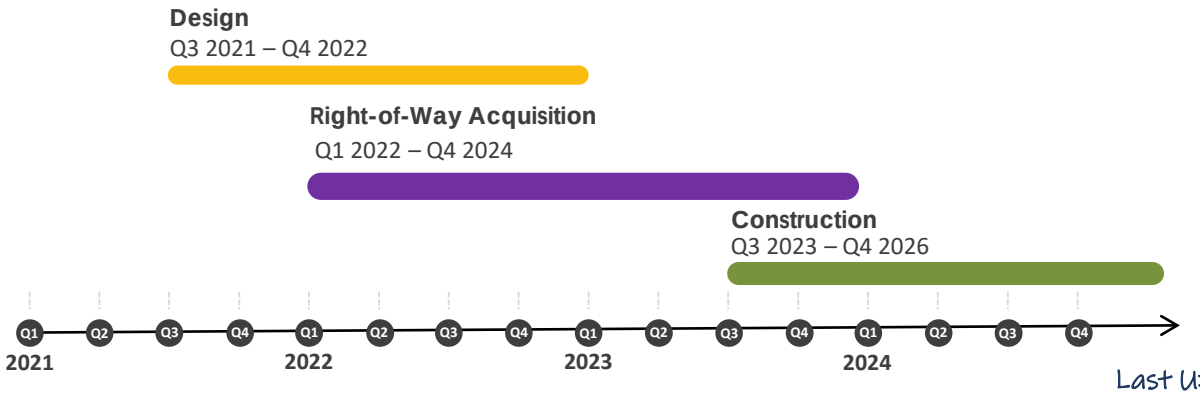

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

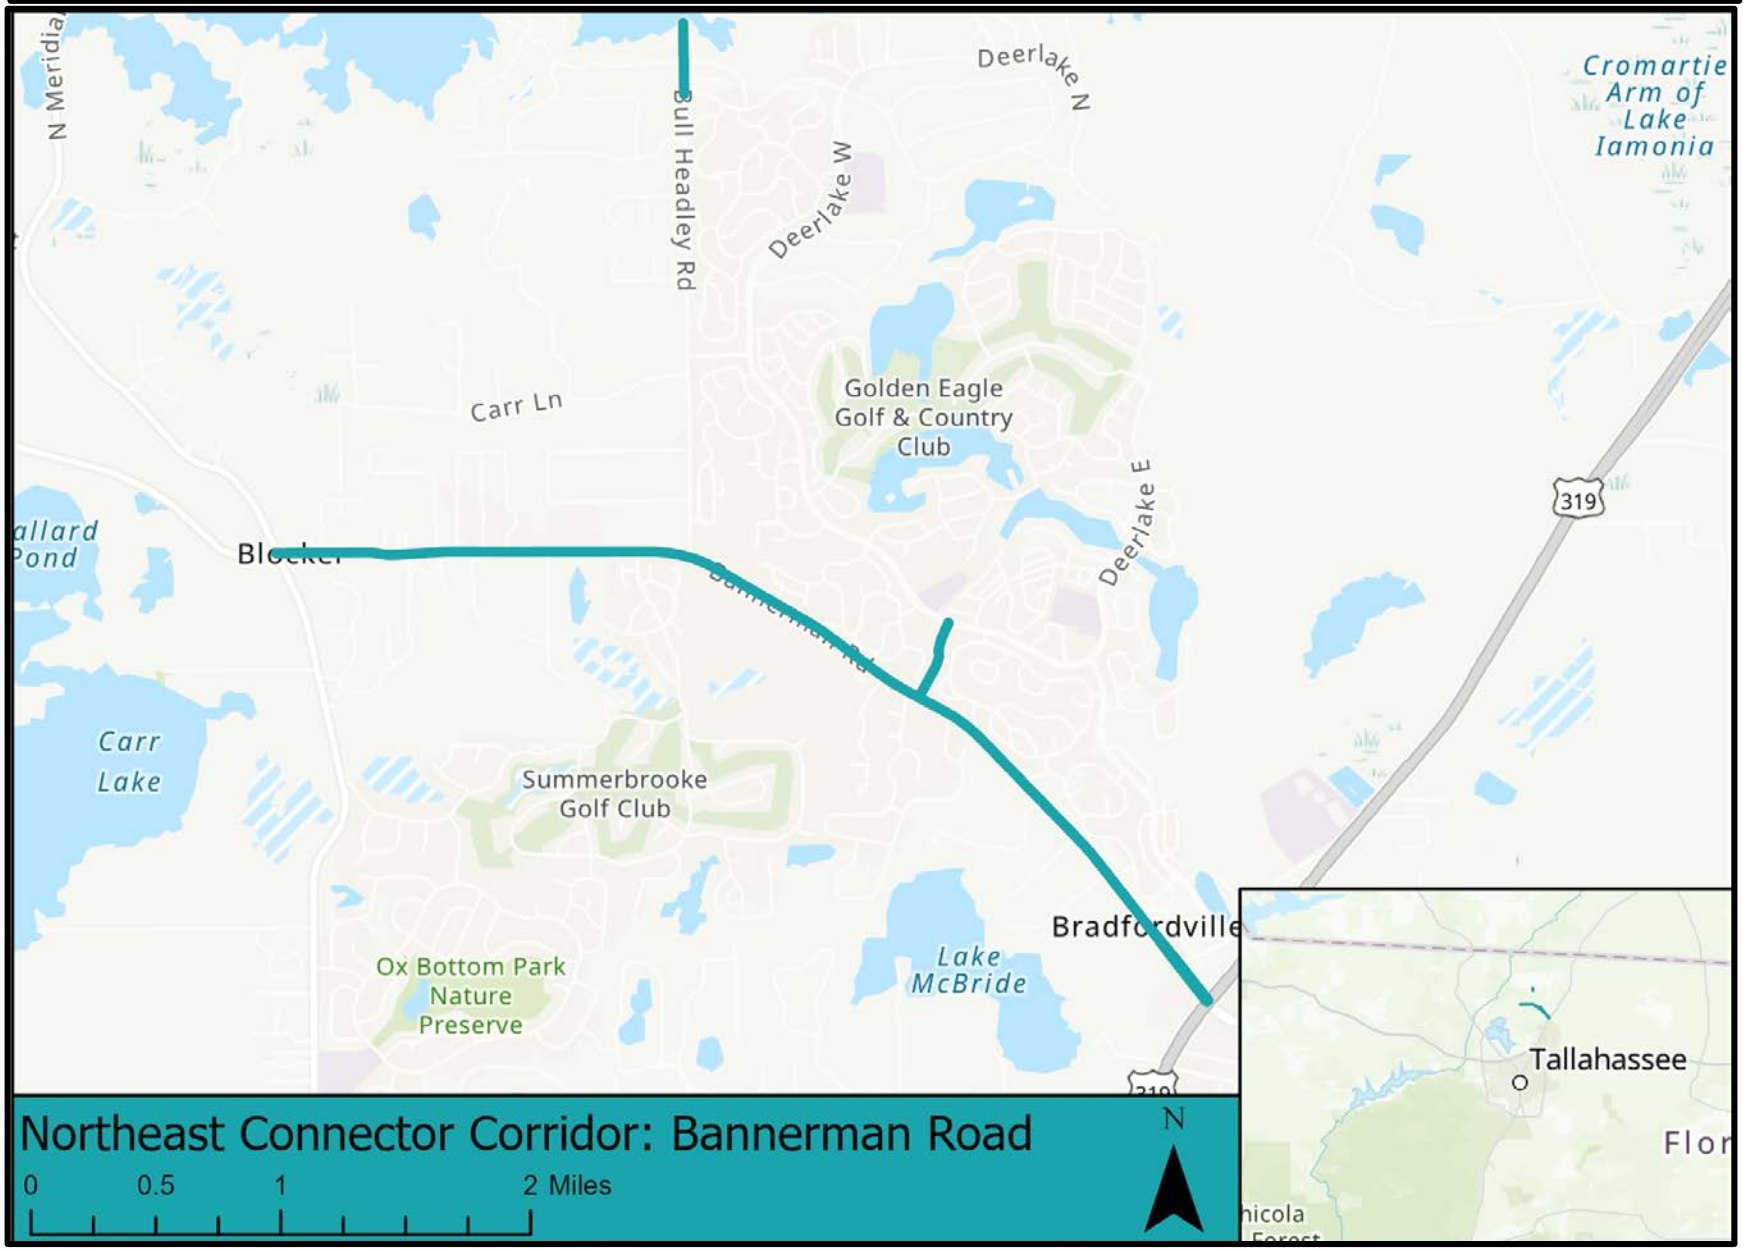

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.NEgateway.com
Staff Contact: Daniel Scheer
(850) 219-1066
Daniel.Scheer@BlueprintIA.org

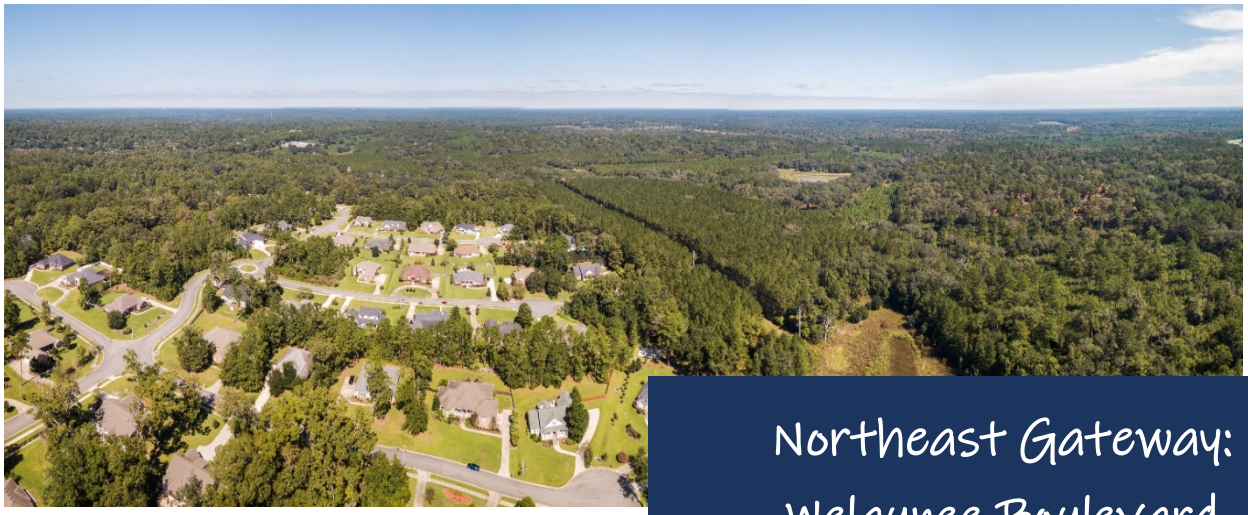

Northeast Gateway: Welaunee Boulevard

Project Highlights

- Project goals are to improve regional mobility, enhance connectivity, and reduce transportation pressures on surrounding roadways.
- The project supports developing Welaunee Boulevard to Roberts Road, and creating a two-lane extension of Shamrock Street to create a gateway into northeast Tallahassee-Leon County.
- The Welaunee Greenway will also be developed as part of this project.

Current Status:

- The Northeast Gateway Project Development & Environment (PD&E) Study was accepted by the IA Board at their June 15, 2021 meeting.

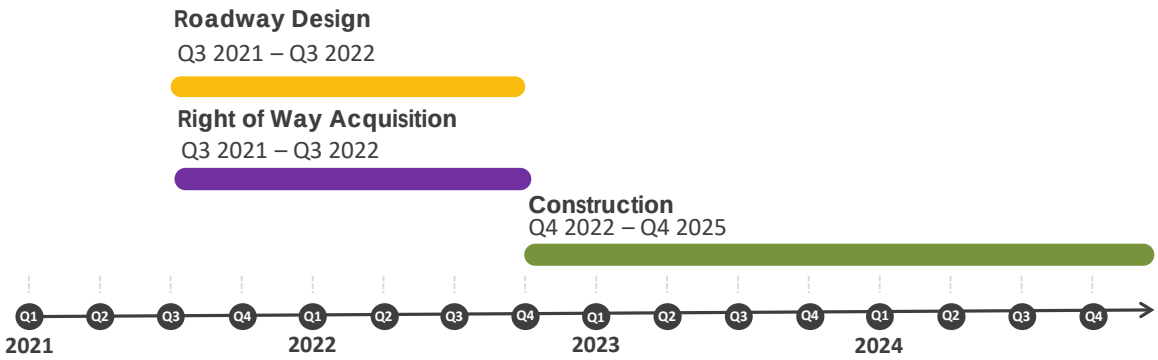

Last Updated: 06.21.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

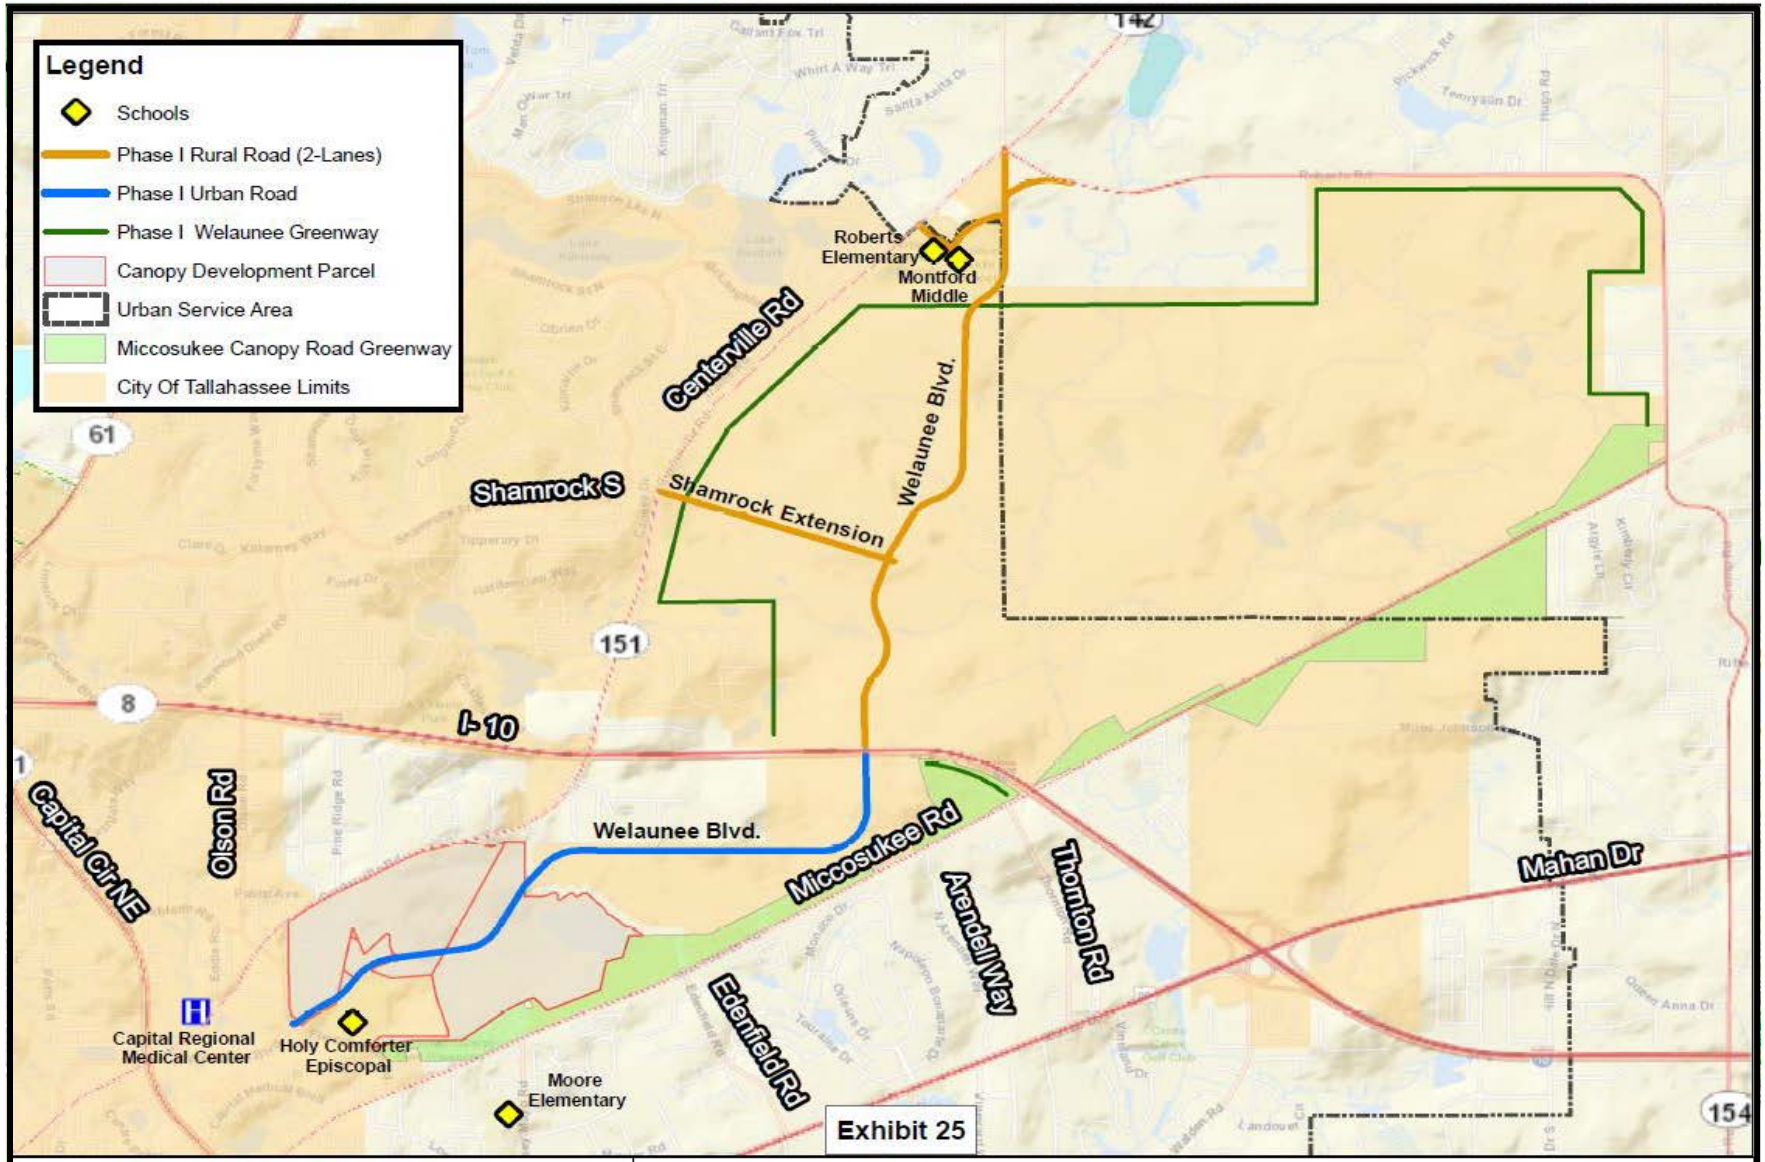

BLUEPRINT INTERGOVERNMENTAL AGENCY

Northeast Gateway

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: (850) 219-1060
info@blueprintia.org

Northeast Park

Project Highlights

- The project provides for the construction of a park in Northeast Tallahassee located on Centerville Road adjacent to the Montford Middle and Roberts Elementary Schools.
- A mixture of active and passive uses have been envisioned for this 50-acre park.

Current Status:

- A new location for the park was approved by the IA Board at their April 8, 2021 meeting. The new location is located on Centerville Road adjacent to the Montford Middle and Roberts Elementary Schools.
- The planning phase and technical analysis is anticipated to begin in Summer 2021.
- Design is anticipated to begin in Summer 2022.

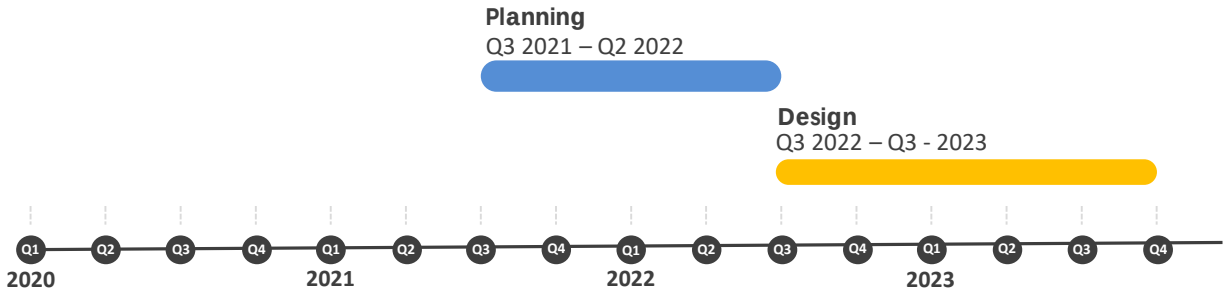

Last Updated: 06.22.2021

BLUEPRINT
INTERGOVERNMENTAL AGENCY

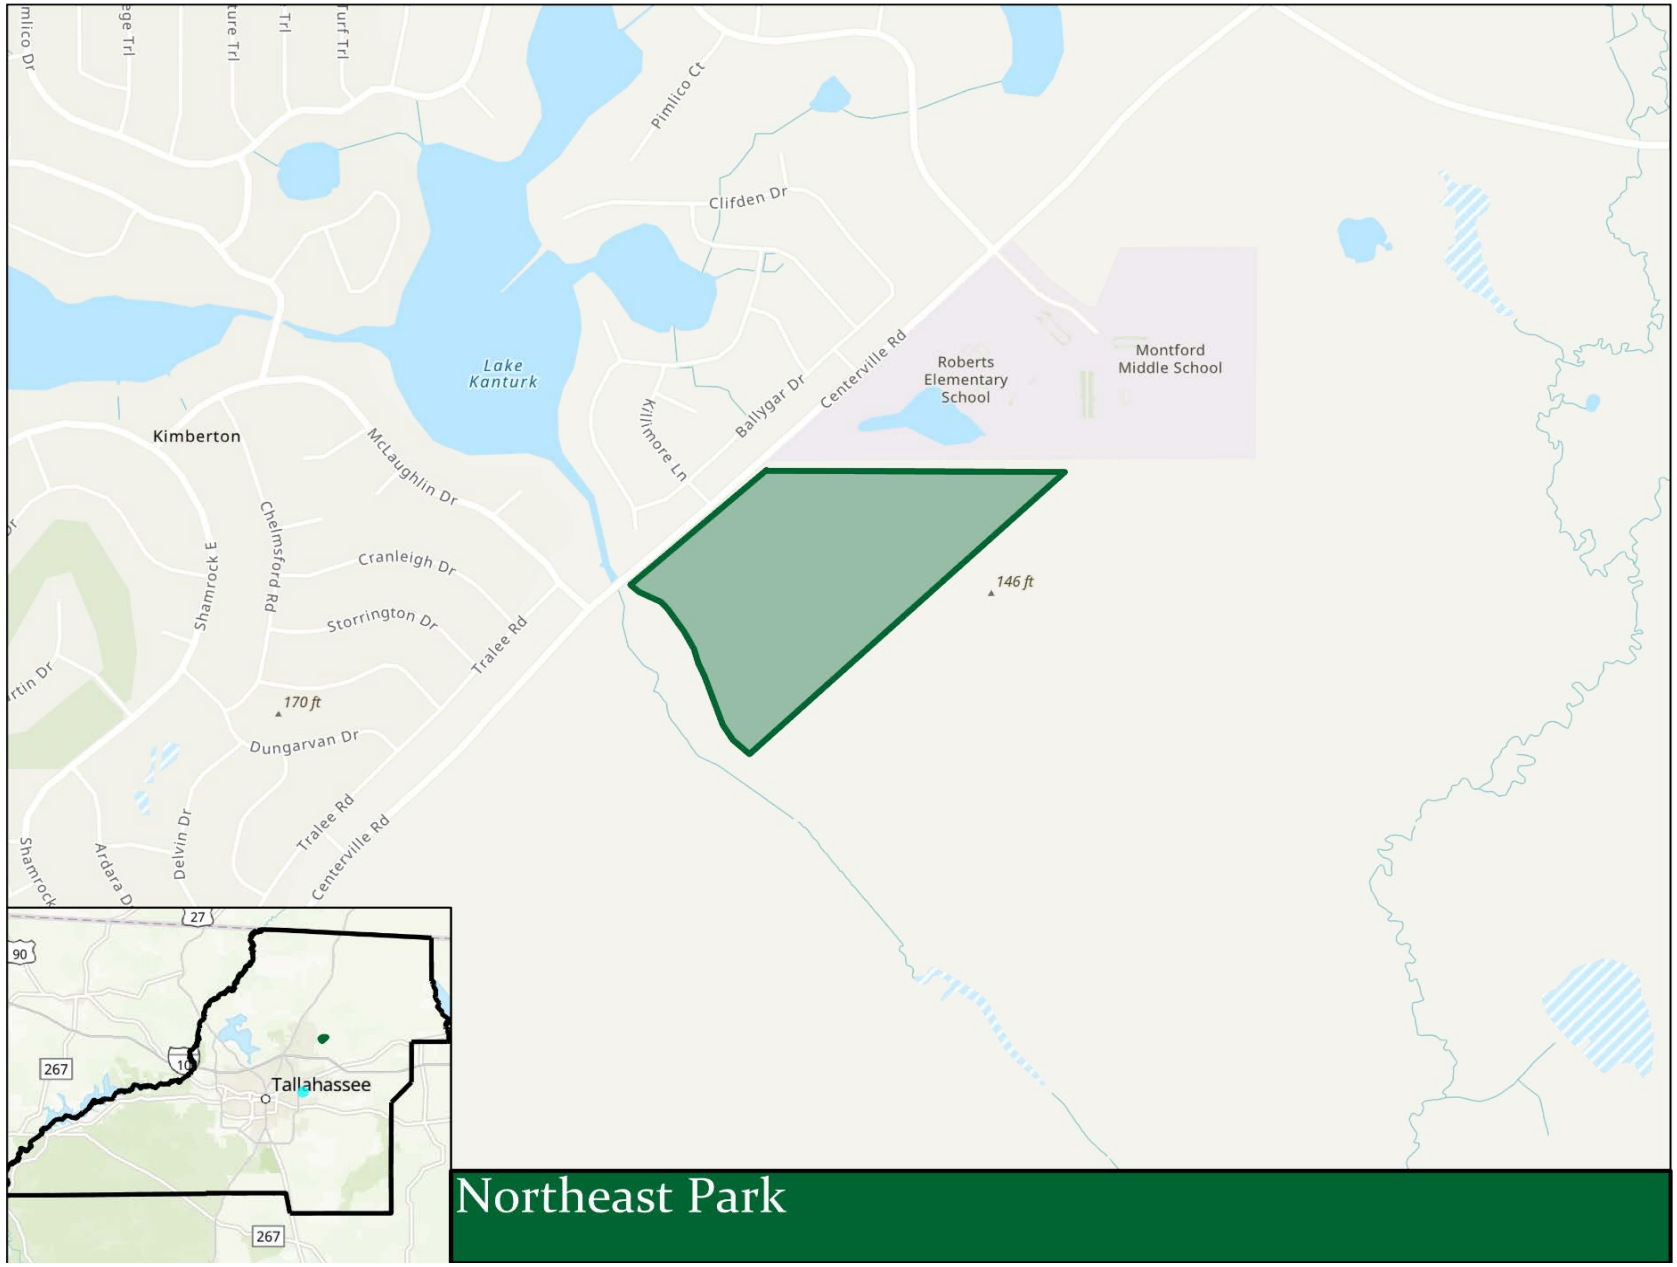

Northeast Park

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Contact: (850) 219-1060
info@blueprintia.org

Northwest Connector: Tharpe Street

Project Highlights

- The Northwest Connector will widen Tharpe Street to four lanes from Ocala Road to Capital Circle Northwest.
- The project adds approximately nine miles of additional trail and sidewalk connectivity.
- The project also improves access to Old Bainbridge County Park near Tower Road, and Stoneler Road County Park, on Stoneler Road.

Current Status:

- This project is scheduled to be initiated in FY 2024.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

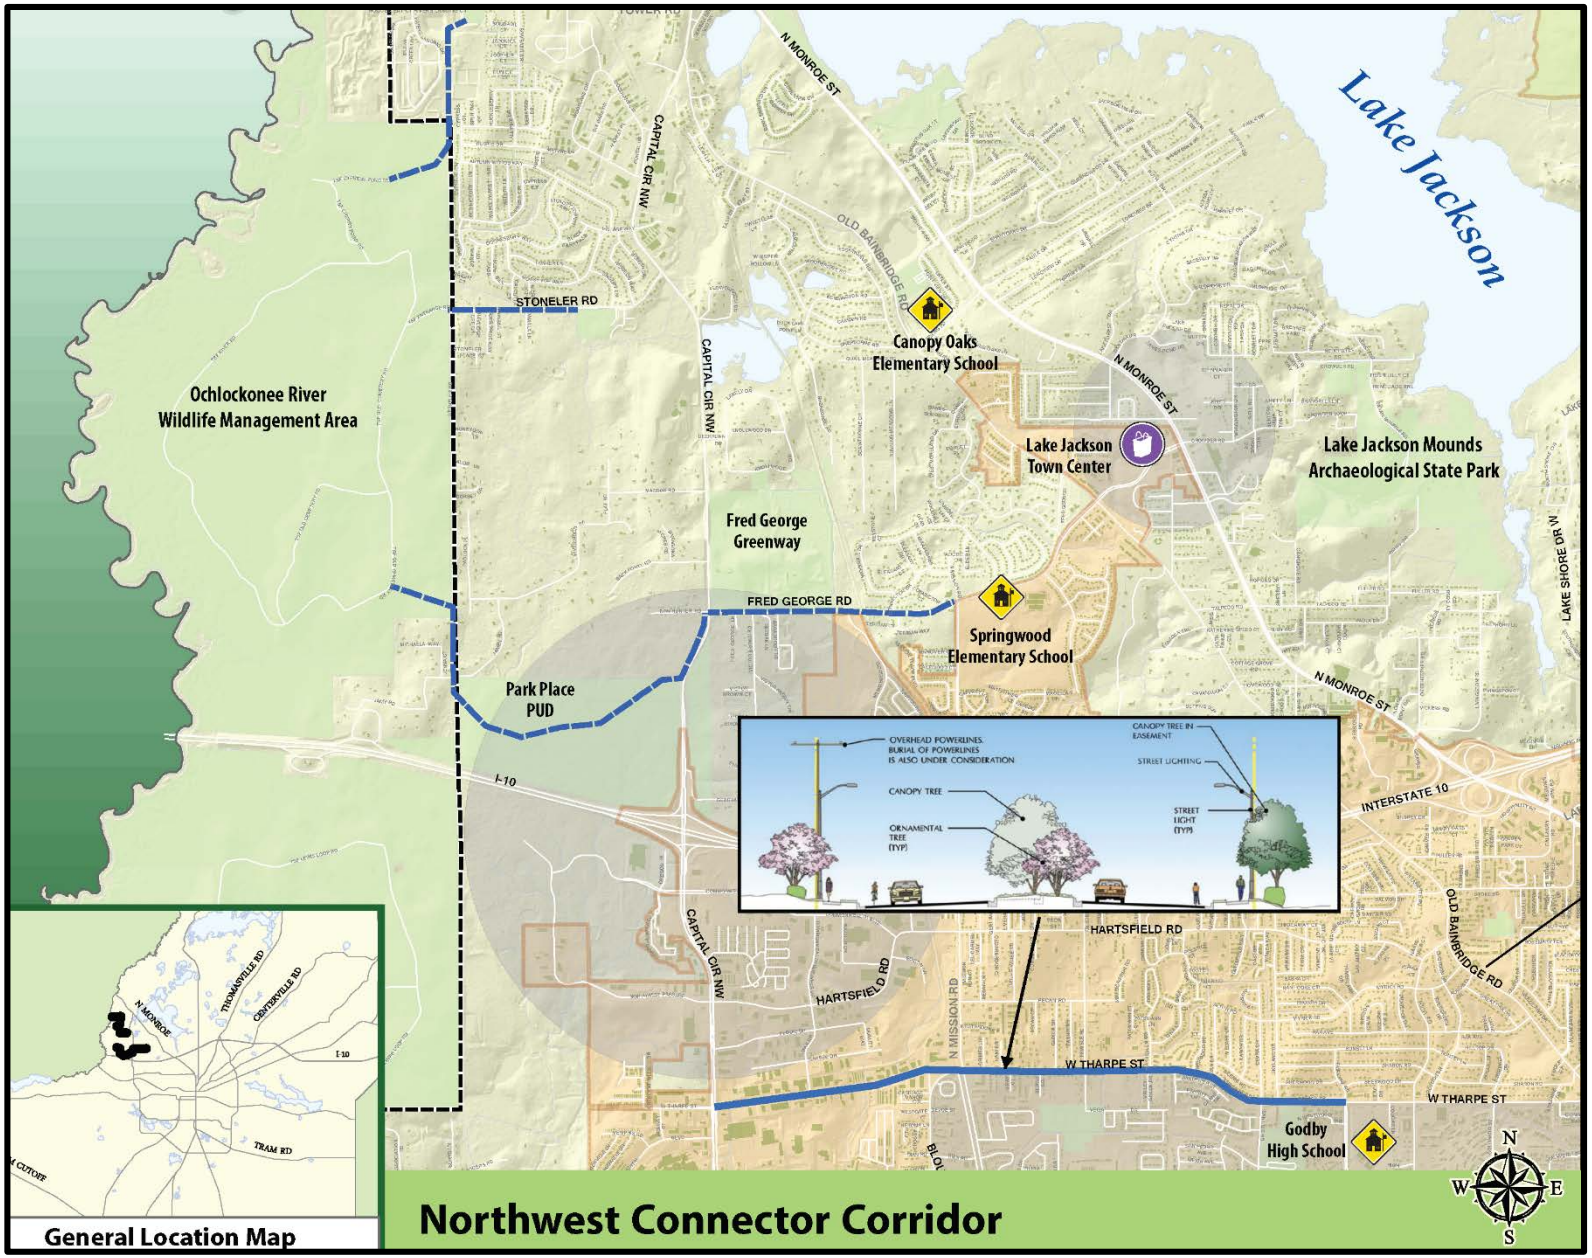

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: (850) 219-1060
info@blueprintia.org

Orange Avenue Widening

Project Highlights

- This project provides improvements to Orange Avenue, a state roadway, including widening the roadway to four lanes from Adams Street to Springhill Road.
- Increases pedestrian and bicycle access with sidewalks and a multi use path
- Enhances the aesthetics of the corridor with additional landscaping
- Design of this project is currently being implemented by the Florida Department of Transportation.

Current Status:

- Blueprint and the Capital Region Transportation Planning Agency partnered on the Southwest Area Transportation Plan Study to develop locally preferred alternatives and options for this corridor. The study was completed in 2019.
- FDOT is currently implementing the PD&E study for this roadway and has also provided funding for Design.
- The PD&E is expected to be complete in 2021.

Planning/Pre-Engineering
Q3 – Q4 2021

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website:
blueprintia.org/projects/orange-meridian-placemaking/
Staff Contact: Junious Brown
(850) 219-1063
Junious.Brown@blueprintia.org

Orange-Meridian Placemaking

Project Highlights

- Create a neighborhood park and community gathering space at Orange Avenue and Meridian Street with the opportunity for trails, exercise opportunities, and a kids' play area.
- Enclose the East Drainage Ditch between South Monroe and Meridian streets and build multi-use path in its place to promote safety and connectivity.
- Contributes $1 million to the development of a planned South City Transit Center.

Current Status:

- Stormwater modeling, community engagement activities to guide park design, and design services for the replacement ditch of the portion of East Drainage Ditch between Meridian and S. Monroe streets are underway.
- Planning and Design is expected to be complete in 2021. Construction will follow in early 2022.

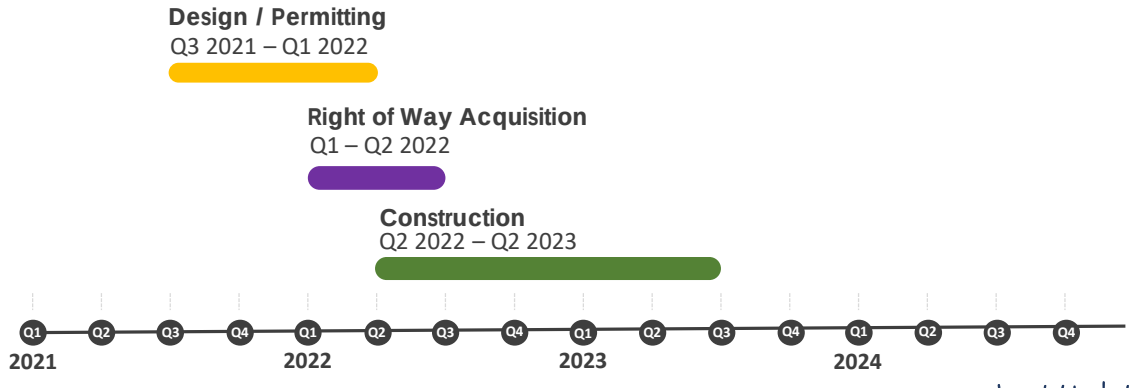

Last Updated: 06.21.2021

BLUEPRINT

INTERGOVERNMENTAL AGENCY

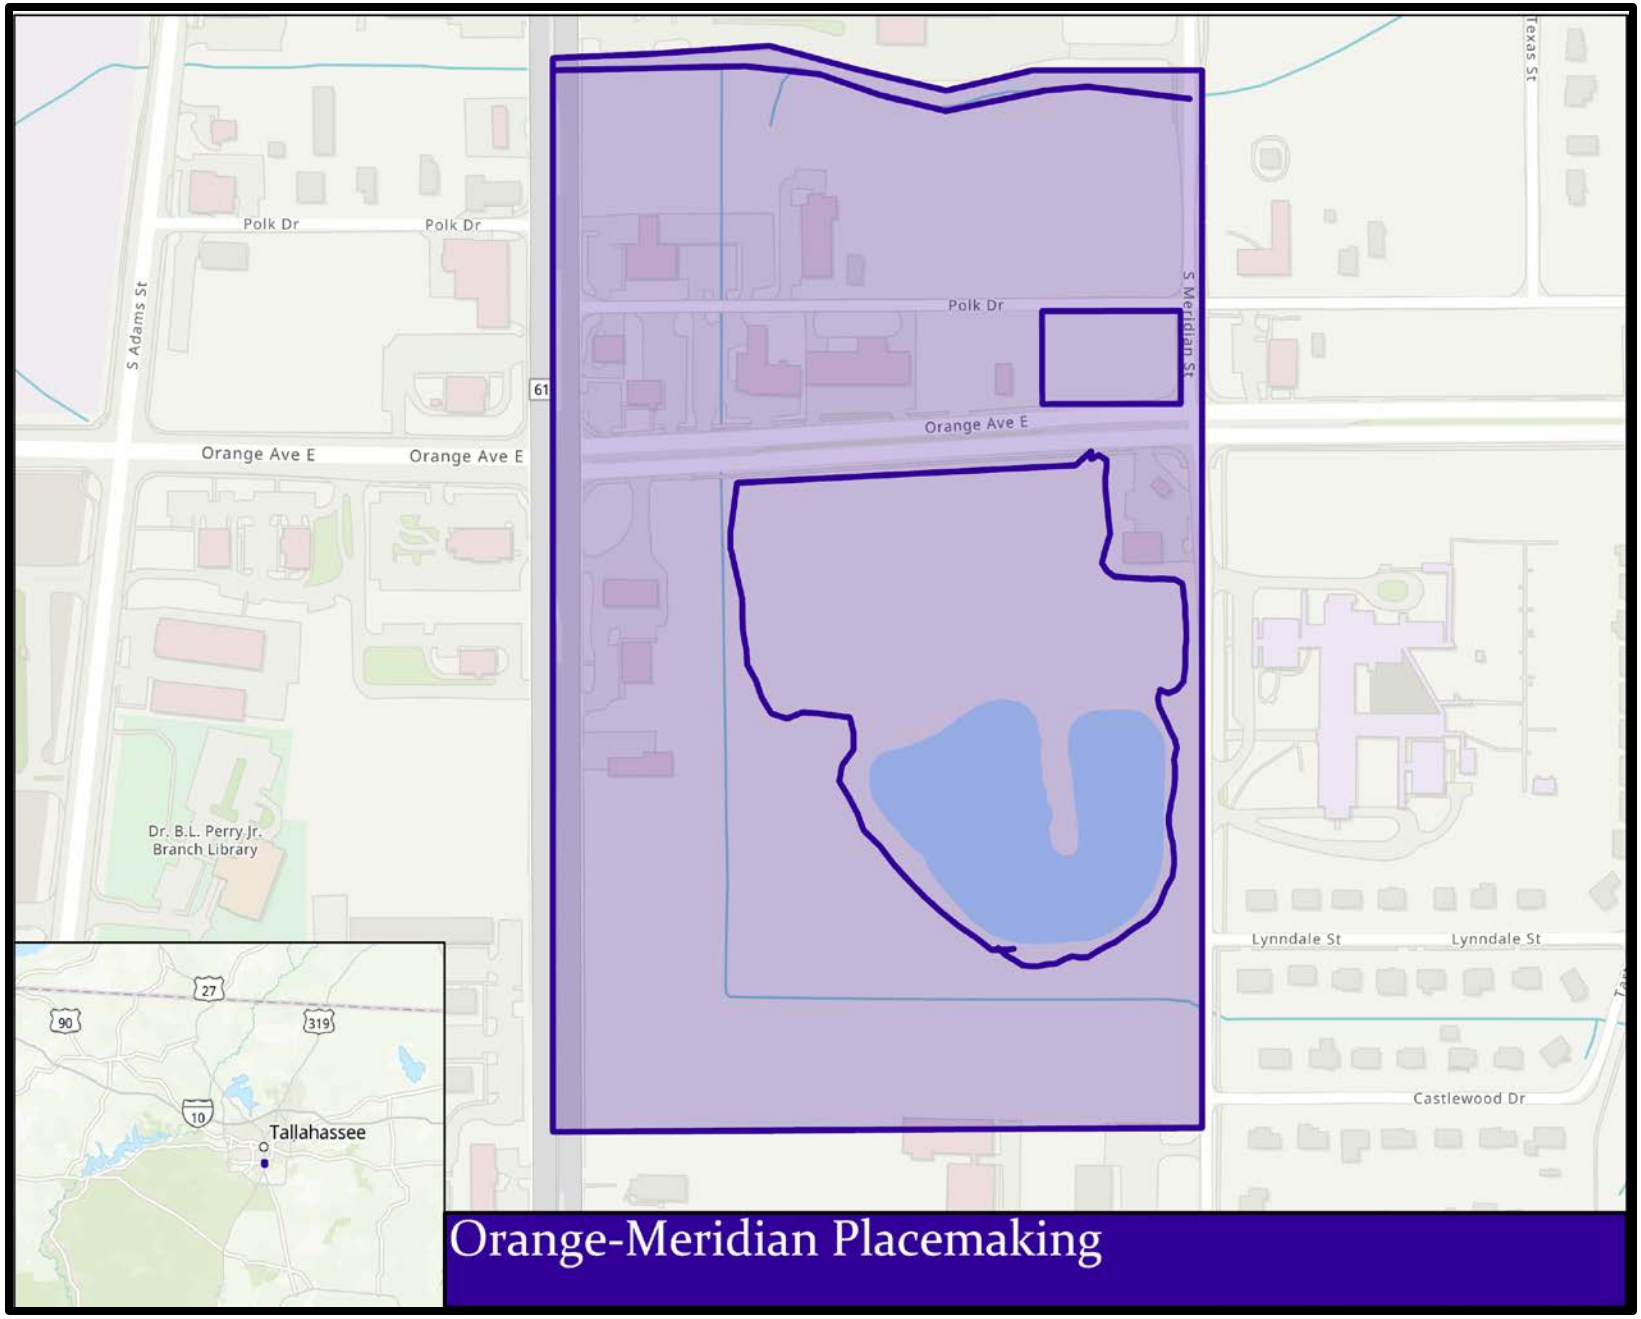

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org
Staff Contact: (850) 219-1060
info@blueprintia.org

Southside Gateway: Woodville Highway

Project Highlights

- The Southside Gateway will widen Woodville Highway from Capital Circle Southwest to Tram Road, which will enhance capacity along a key evacuation route.
- The project includes right-of-way acquisition, construction costs, gateway streetscaping, and stormwater for roadway improvements.

Current Status:

- Right-of-Way acquisition is underway by FDOT along Woodville Highway from Capital Circle SW to Gaile Avenue and scheduled through FY21.
- Tentative FY 2021-2026 FDOT Work Program identifies funding for construction for resurfacing along Woodville Highway from Briandav Street to Sunday Court in FY23 in the amount of $2,176,103.
- Tentative FY 2021-2026 FDOT Work Program identifies funding for construction of lighting along Crawfordville Rd from Capital Circle SW to Mckenzie Dr in FY23 in the amount of $778,465.
- Blueprint has executed an agreement with FDOT for curb extensions.

BLUEPRINT

INTERGOVERNMENTAL AGENCY

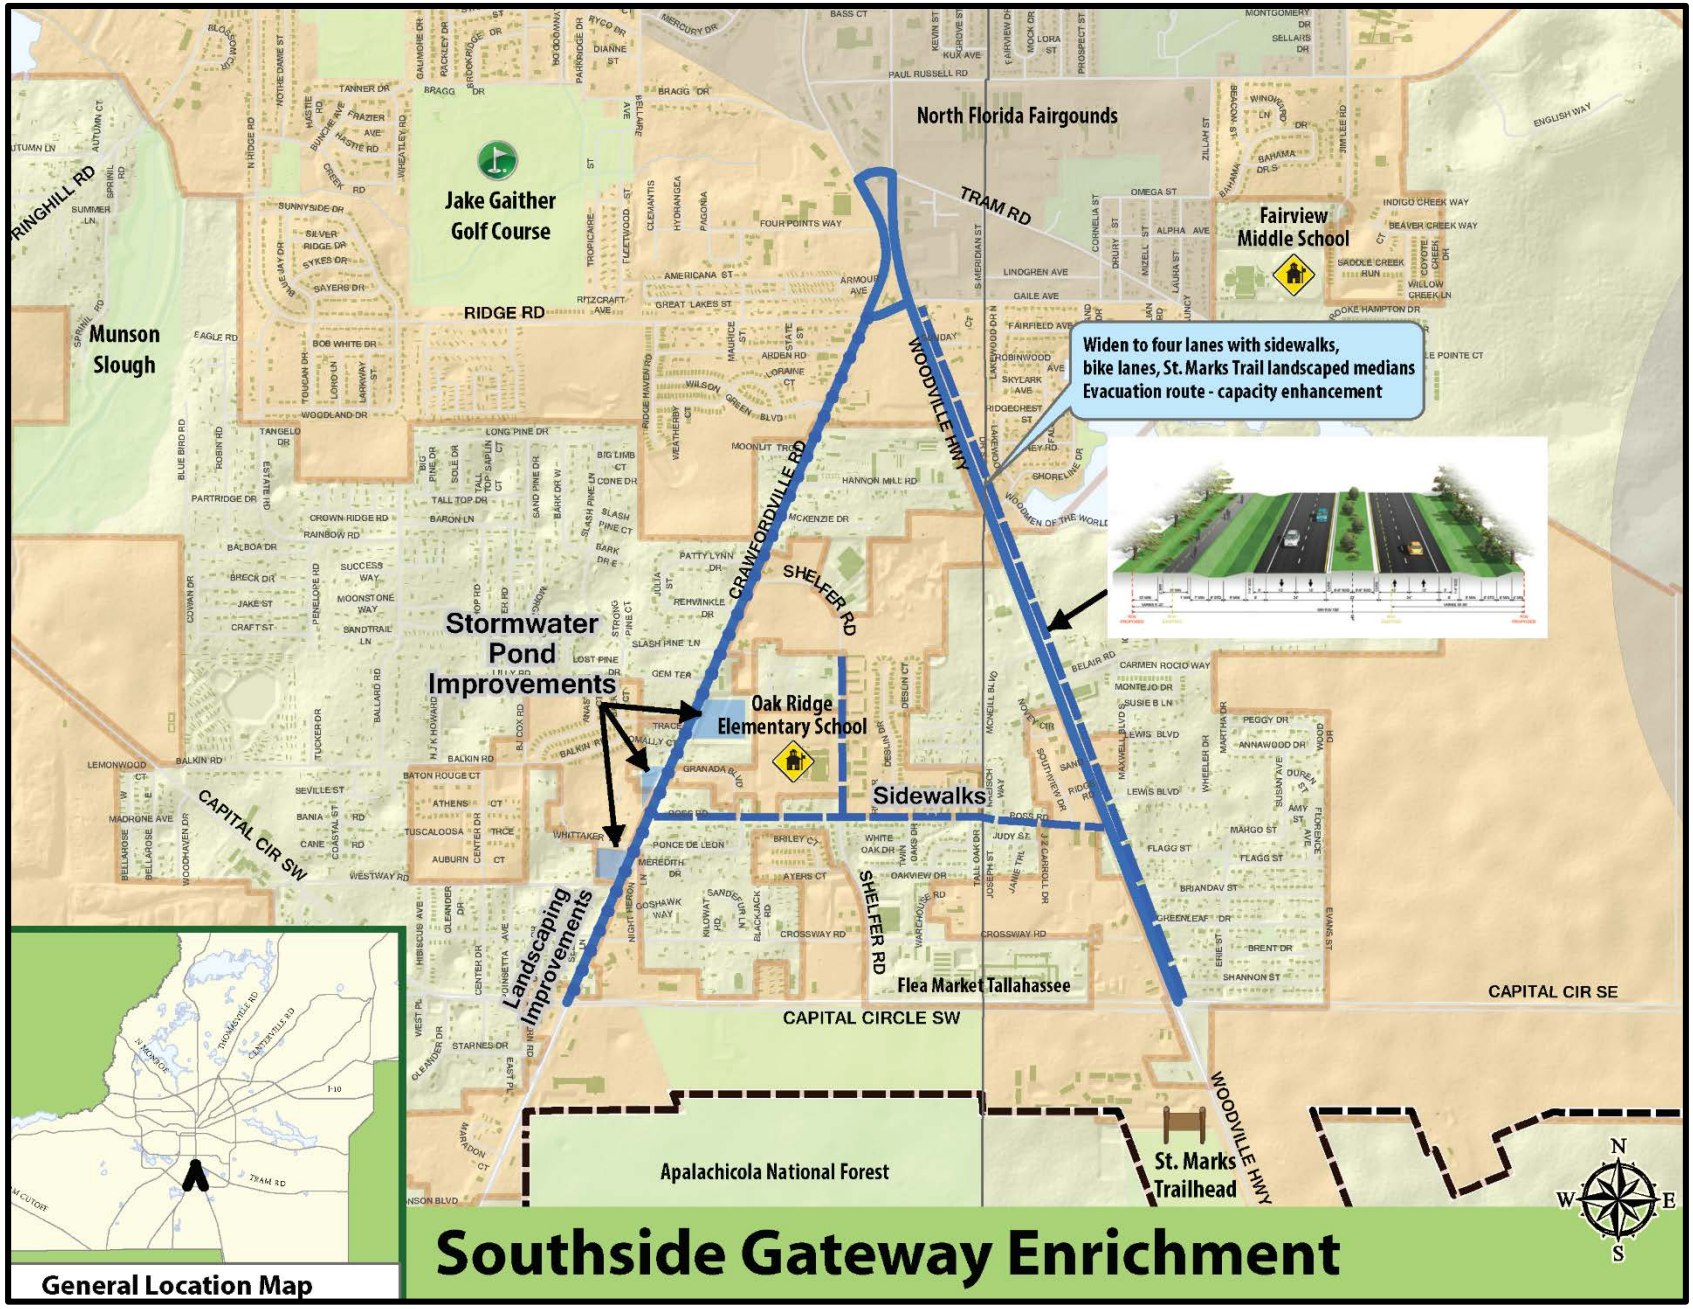

BLUEPRINT INTERGOVERNMENTAL AGENCY

Project Website: www.BlueprintIA.org

Staff Contact: (850) 219-1060
info@blueprintia.org

Westside Student Gateway

Project Highlights

- Widens Pensacola Street/Highway 20 (from Capital Circle to Appleyard) to four lanes and adds landscaped medians
- Includes funding for stormwater improvements in the Gum Creek/West Drainage Ditch
- Will create gateway features and network connectivity

Current Status:

- Funding for PD&E for this project is currently 8th on the CRTPA Road Project Priority List for 2021-2025. No funding has been identified/allocated yet.
- Blueprint has not yet initiated this project.

BLUEPRINT INTERGOVERNMENTAL AGENCY

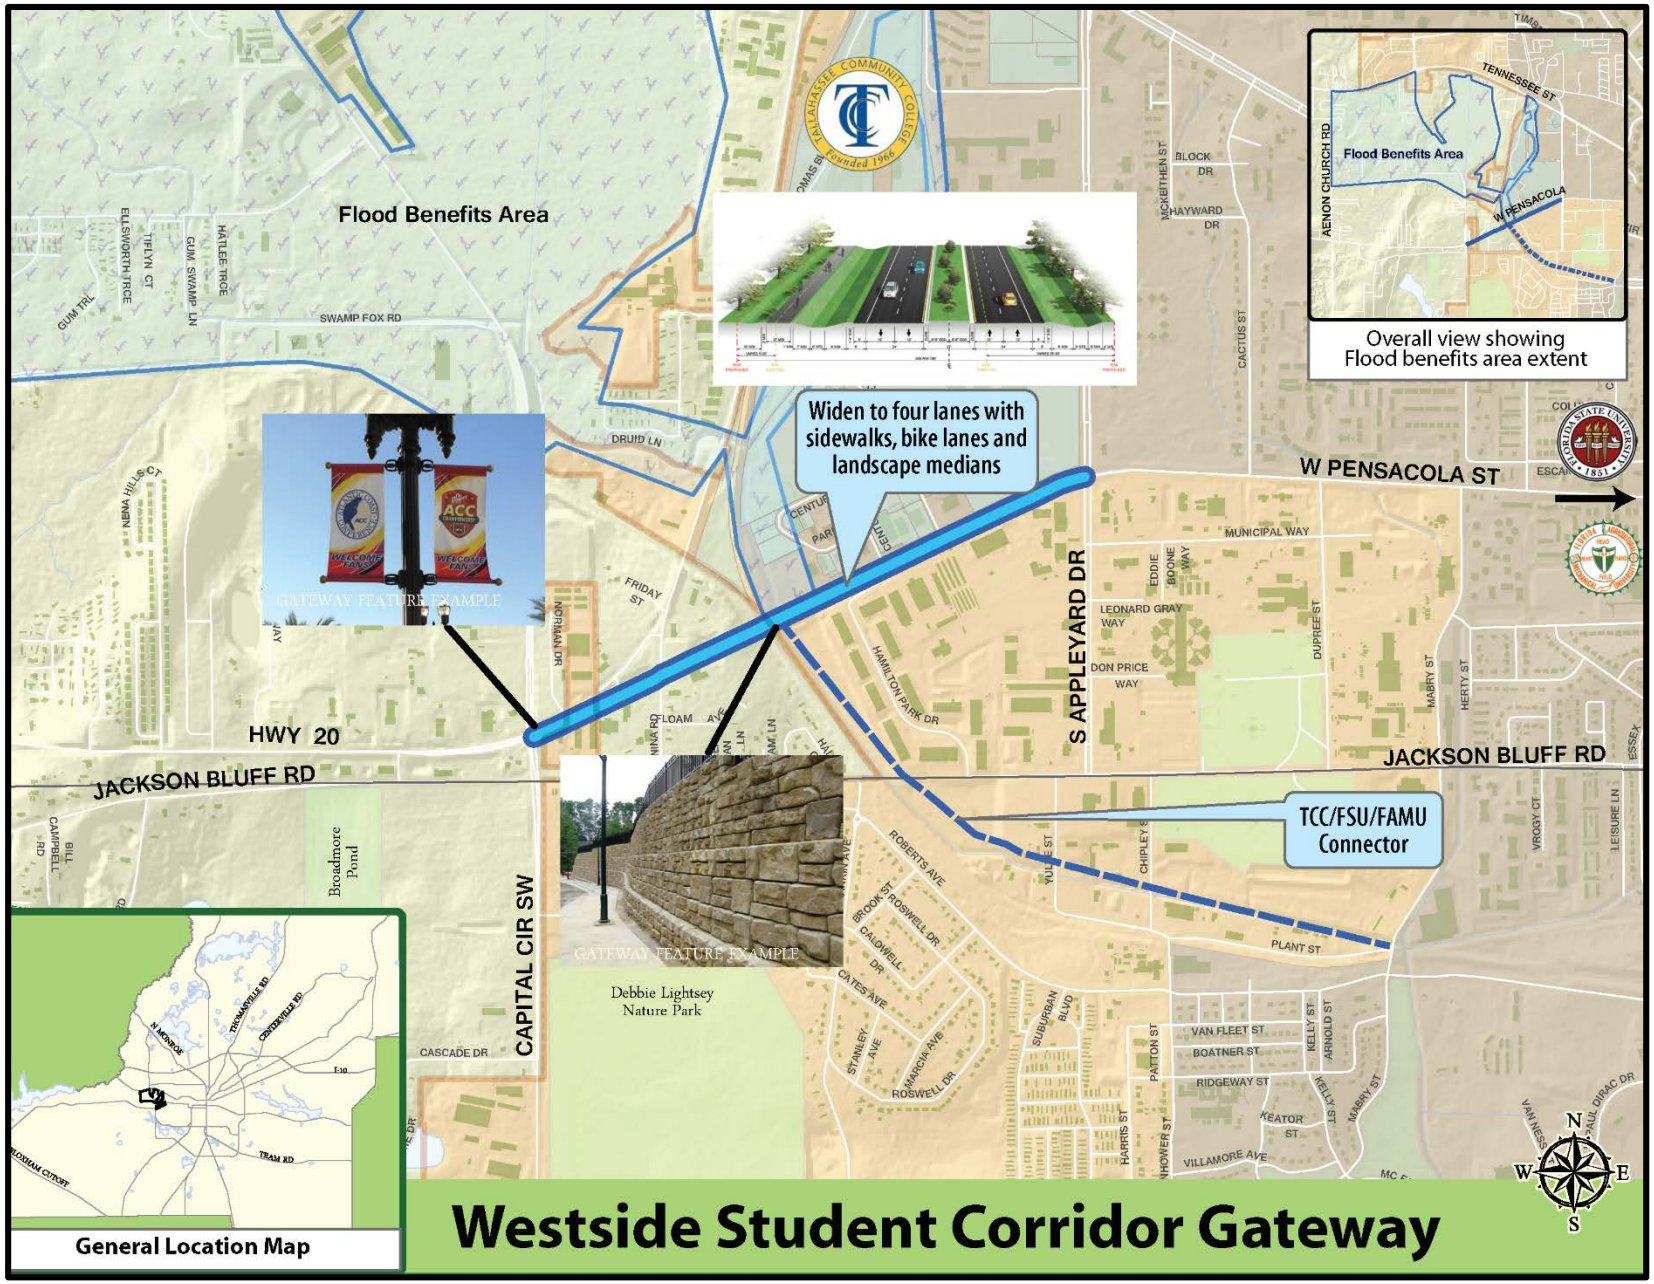

Westside Student Corridor Gateway
